

ID	Task Mod	Task Name	Livrabile	Duration	Start	May '24				
						22	29	06	13	20
1		<b>PLAN DE ELABORARE SI IMPLEMENTARE A SOLUTIEI DE DIGITALIZARE A PROCESELOR DE MANAGEMENT RESURSE UMANE - RECRUTARE, ANGAJARE, ADMINISTRARE PERSONAL (SDPMRURAAP) BNM</b>		<b>380 days</b>	<b>Mon 16.12.24</b>					
2		<b>Project Management</b>		<b>135 days</b>	<b>Mon 16.12.24</b>					
3		Kick-off meeting		0 days	Mon 16.12.24					
4		Activitati de Project management	L1 Plan initial de management al Proiectului   L2 Plan de management al proiectului actualizat   L3 Prezentare de suport pentru intalnirea de lansare   L4 Raport final pe	134 days	Mon 16.12.24					
5		Toleranta generala proiect		0 days	Fri 20.06.25					
6		<b>Analiza necesitatilor si dezvoltarea specificatiilor de design</b>		<b>14 days</b>	<b>Tue 17.12.24</b>					
7		Analiza situatie actuala		3 days	Tue 17.12.24					
8		Analiza procesului de recrutare		3 days	Wed 18.12.24					
9		Analiza procesului de angajare		3 days	Thu 19.12.24					
10		Analiza procesului de administrare a personalului		3 days	Fri 20.12.24					
11		Analiza procesului de evidență a timpului de muncă		3 days	Mon 23.12.24					
12		Analiza procesului de gestiune a structurii organizatorice		3 days	Tue 24.12.24					
13		Analiza procesului - Deplasările de serviciu ale personalului		3 days	Wed 25.12.24					
14		Analiza procesului - Gestiunea practicii de producție în cadrul BNM		3 days	Thu 26.12.24					

Project: PLAN DE ELABORAREA  
Date: Thu 28.11.24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

ID	Task Mod	Task Name	Livrabile	Duration	Start	May '24				
						22	29	06	13	20
15		Elaborare Documentatie de analiza	L5 Document analiză tehnică și de activitate   L6 Criterii de acceptare   L7 Concept model de date al soluției   L8 Conceptul arhitecturii soluției și diagramele de infrastructură   L9 Planul de proiect detaliat și actualizat	11 days	Fri 20.12.24					
16		<b>Implementarea solutiei - etapa de constructie</b>		<b>81 days</b>	<b>Tue 17.12.24</b>					
17		Instalarea		3 days	Tue 17.12.24					
18		Configurarea mediilor de testare si productie		5 days	Fri 20.12.24					
19		Dezvoltarea si customizarea functionalitatilor solutiei		70 days	Fri 27.12.24					
20		Integrarea cu sisteme terte, interne si externe		20 days	Fri 27.12.24					
21		Migrarea/importarea datelor aferente angajaților BNM (dosarele angajaților) din sistemul HR exploatat în cadrul SI al BNM	L10 Plan de migrare	11 days	Fri 27.12.24					
22		Demonstrarea modului de acoperire al functionalitatilor		1 day	Fri 04.04.25					

Project: PLAN DE ELABORAREA  
Date: Thu 28.11.24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

ID	Task Mod	Task Name	Livrabile	Duration	Start	May '24				
						22	29	06	13	20
23		Elaborarea Documentatie	L11 Raport de instalare pe mediul de TEST, configurare, customizare   L12 Proceduri operationale pentru gestiunea solutiei inclusiv: instalare, modificare, arhivare date, efectuare copii de rezerva, restabilire	3 days	Fri 04.04.25					
24		<b>Testarea</b>		<b>81 days</b>	<b>Mon 06.01.25</b>					
25		Elaborare Plan general și detaliat de testare	L13 Plan de testare	3 days	Mon 06.01.25					
26		Efectuarea testarii		10 days	Fri 04.04.25					
27		Remediarea erorilor si neconformitatilor depistate in timpul testarii		5 days	Fri 18.04.25					
28		Elaborare Raport de testare	L14 Raport de testare	2 days	Fri 25.04.25					
29		<b>Instruirea administratorilor și utilizatorilor</b>		<b>10 days</b>	<b>Fri 25.04.25</b>					

Project: PLAN DE ELABORAREA  
Date: Thu 28.11.24


Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

ID	Task Mod	Task Name	Livrabile	Duration	Start	May '24				
						22	29	06	13	20
30		Elaborarea documentatiei de instruire	L15 Ghidul Utilizatorului   L16 Ghidul Administratorului   L17 Ghidul de instalare   L18 Ghidul de configurare   L19 Ghidul de efectuare a back-up   L20 Ghidul de recuperare si	3 days	Fri 25.04.25					
31		Instruirea administratorilor și utilizatorilor		5 days	Wed 30.04.25					
32		Elaborarea Raport de instruire	L21 Raport de instruire	2 days	Wed 07.05.25					
33		<b>Acceptanta finala</b>		<b>5 days</b>	<b>Fri 09.05.25</b>					
34		Acceptanta finala	L22 Raport Acceptanta Finala	5 days	Fri 09.05.25					
35		<b>Toleranta generala pe proiect</b>		30 days	Fri 16.05.25					
36		<b>Lansarea in productie</b>		<b>10 days</b>	<b>Fri 16.05.25</b>					
37		Exploatarea experimentală		10 days	Fri 16.05.25					
38		<b>Mentenanță si suport post-implementare</b>			<b>Fri 30.05.25</b>					
39		Mentenanță si suport post-implementare			Fri 30.05.25					




Project: PLAN DE ELABORAREA  
Date: Thu 28.11.24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

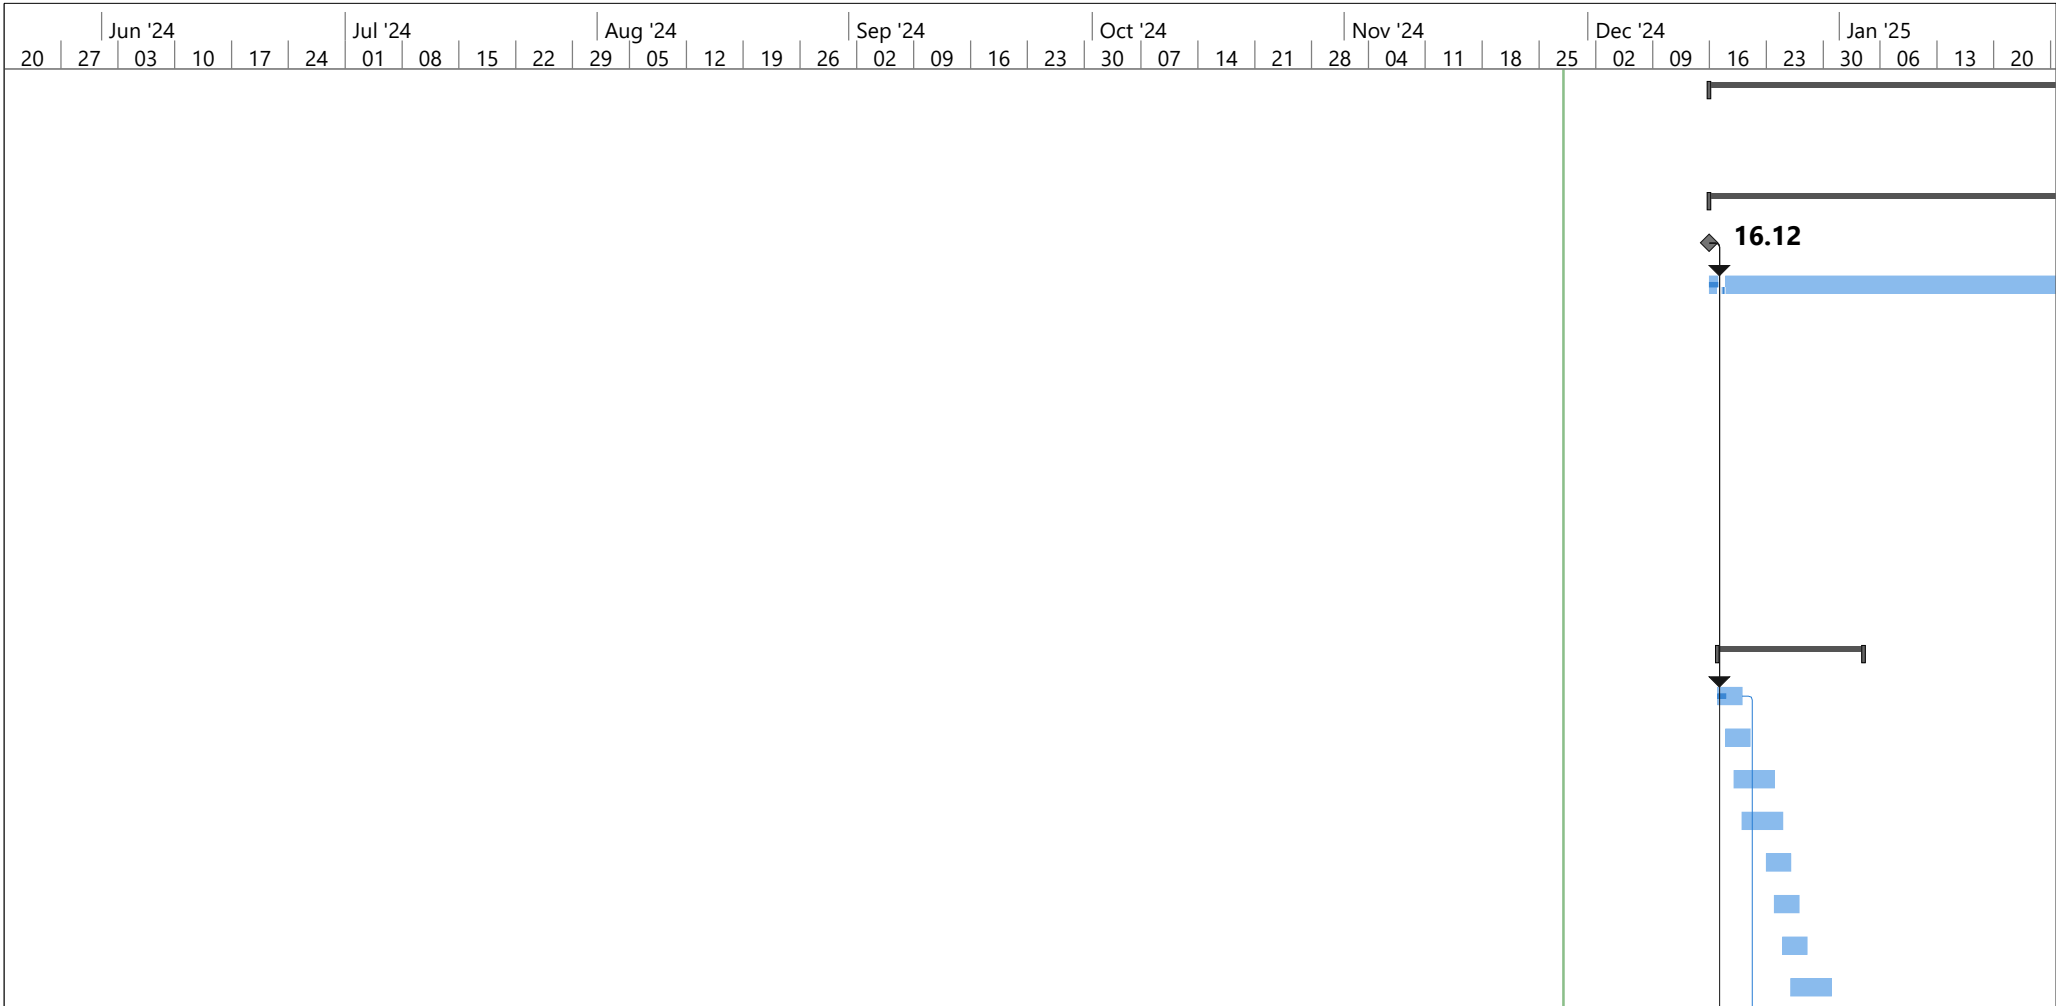


Project: PLAN DE ELABORAREA  
Date: Thu 28.11.24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

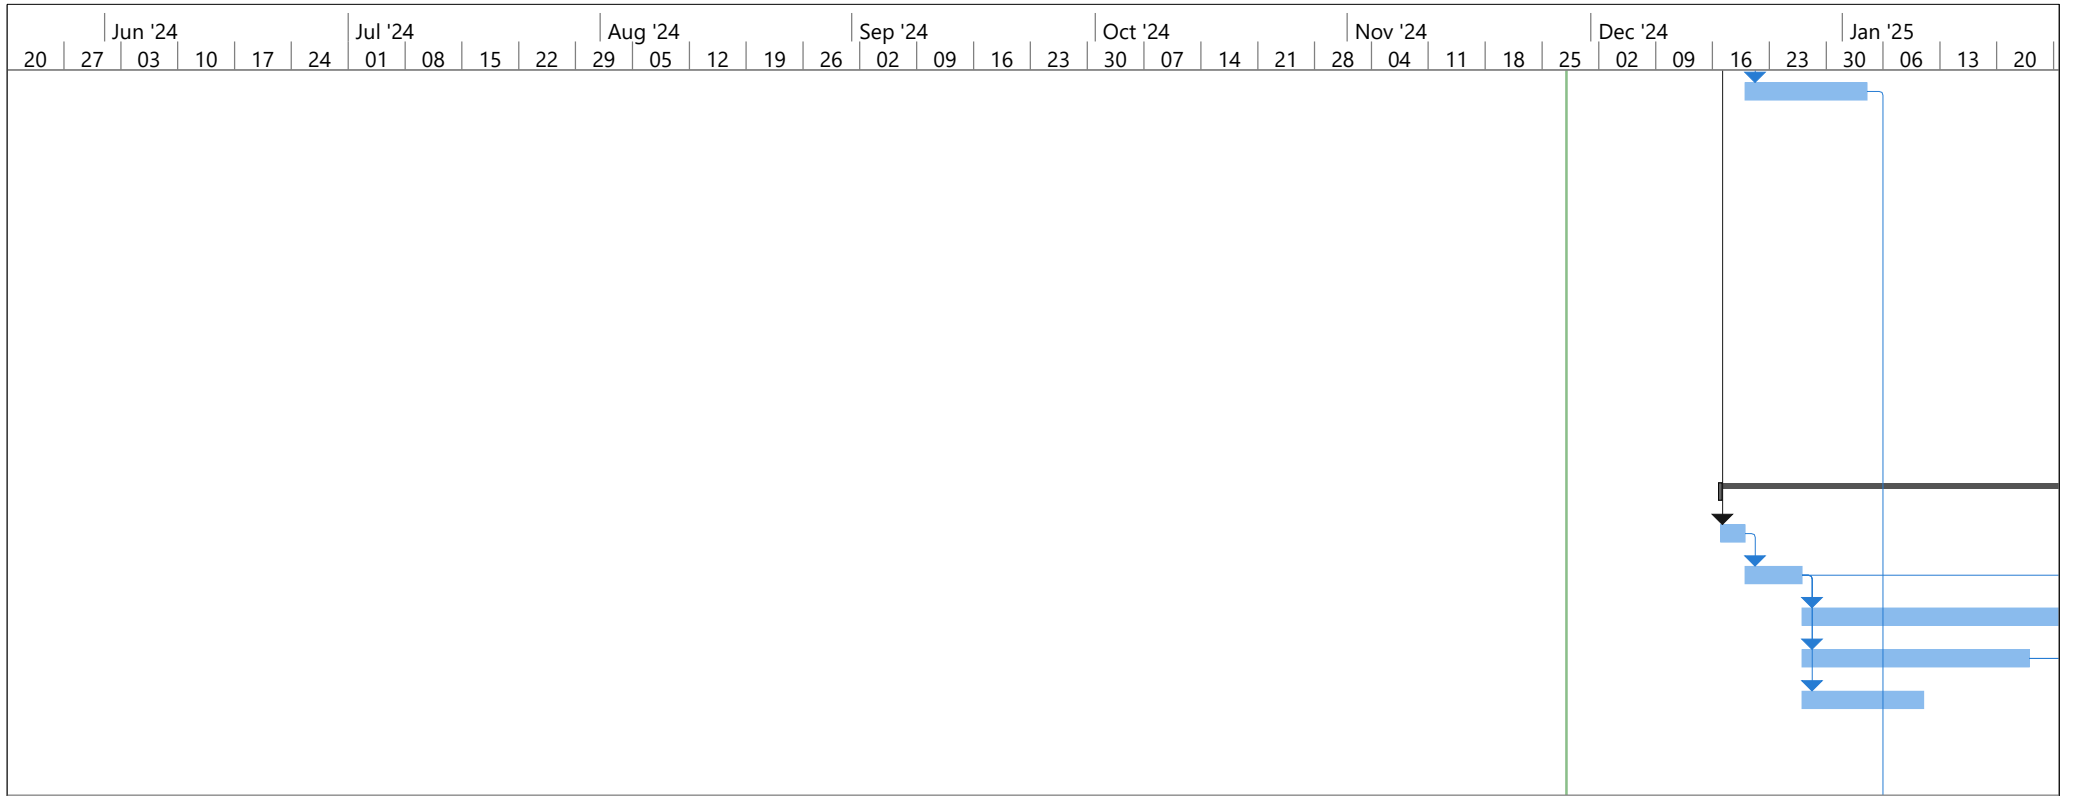

Project: PLAN DE ELABORAREA  
Date: Thu 28.11.24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

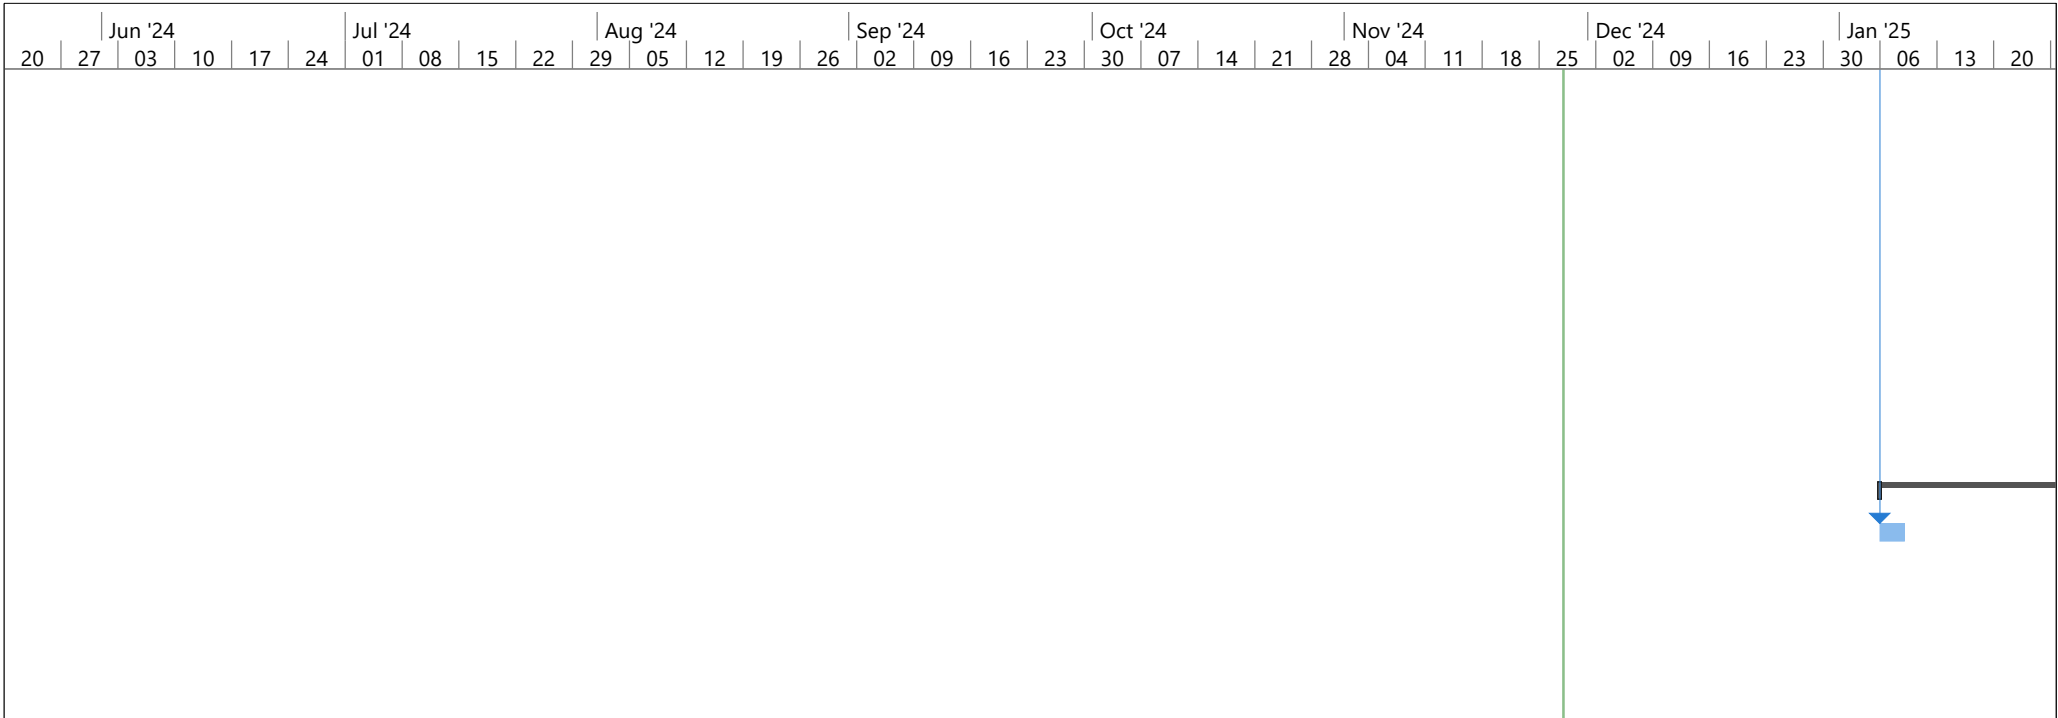

Project: PLAN DE ELABORAREA  
Date: Thu 28.11.24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




Project: PLAN DE ELABORAREA  
Date: Thu 28.11.24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			



Feb '25 27 03 10 17 24 Mar '25 03 10 17 24 Apr '25 31 07 14 21 May '25 28 05 12 19 26 Jun '25 02 09 16 23 Jul '25 30 07 14 21 Aug '25 28 04 11 18 25 Sep '25 01 08 15 22 Oct 29




Project: PLAN DE ELABORAREA Date: Thu 28.11.24	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

Feb '25 27 03 10 17 24 Mar '25 03 10 17 24 Apr '25 31 07 14 21 May '25 28 05 12 19 26 Jun '25 02 09 16 23 Jul '25 30 07 14 21 Aug '25 28 04 11 18 25 Sep '25 01 08 15 22 Oct 29







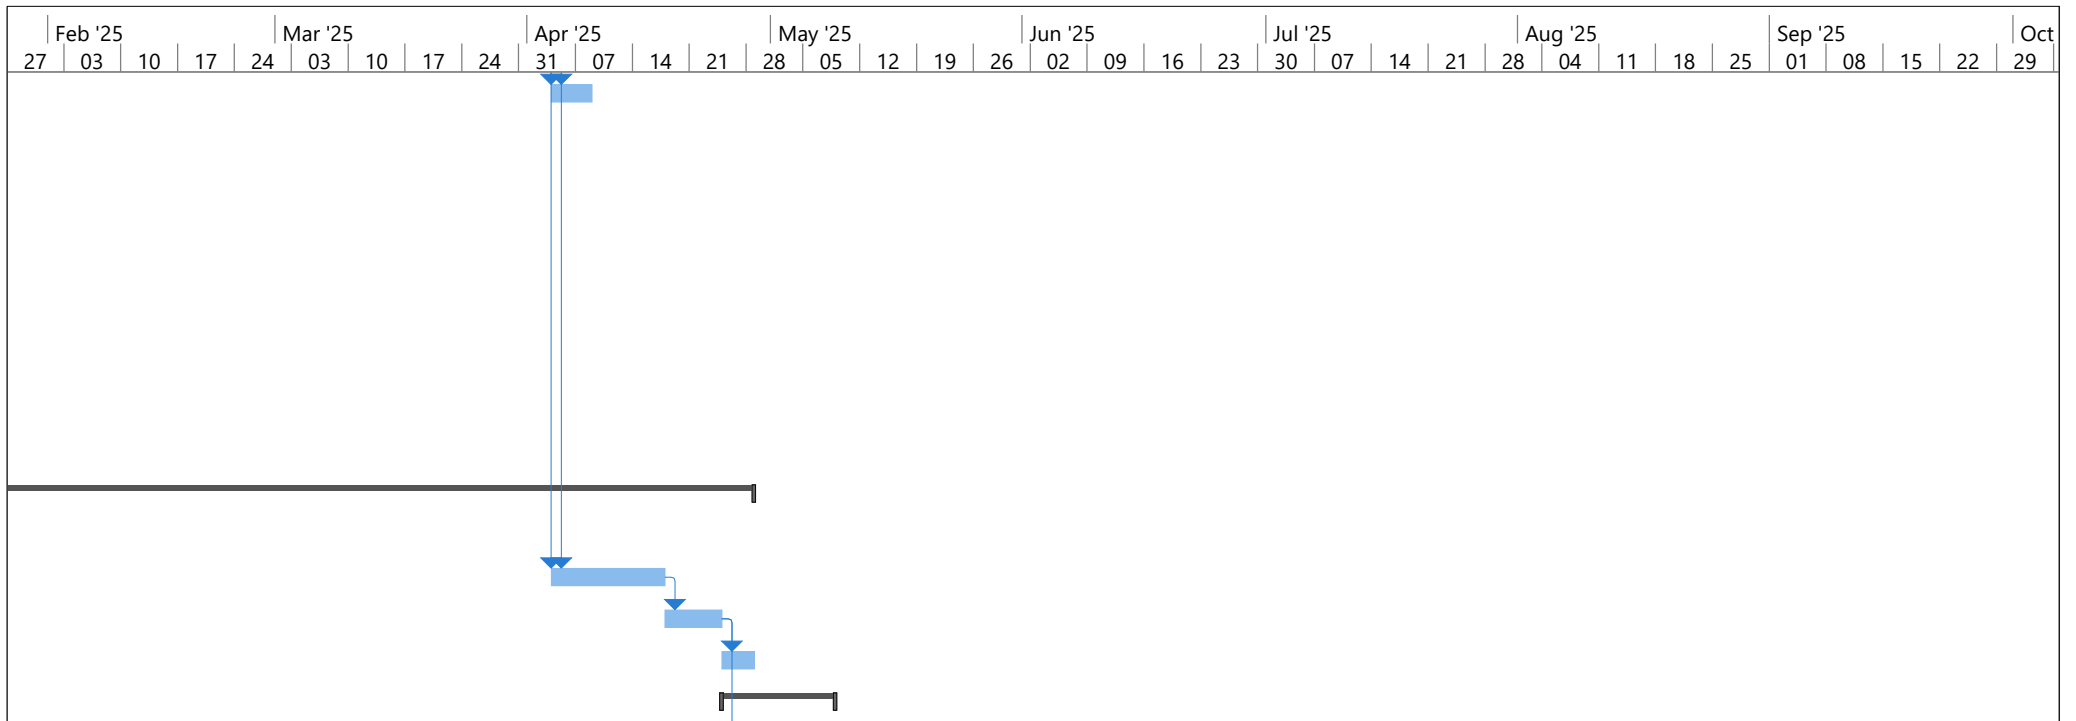














Project: PLAN DE ELABORAREA  
Date: Thu 28.11.24


Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			



Project: PLAN DE ELABORAREA  
Date: Thu 28.11.24


Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

Feb '25 27 03 10 17 24 Mar '25 03 10 17 24 Apr '25 31 07 14 21 May '25 28 05 12 19 26 Jun '25 02 09 16 23 Jul '25 30 07 14 21 Aug '25 28 04 11 18 25 Sep '25 01 08 15 22 Oct 29



Project: PLAN DE ELABORAREA  
Date: Thu 28.11.24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

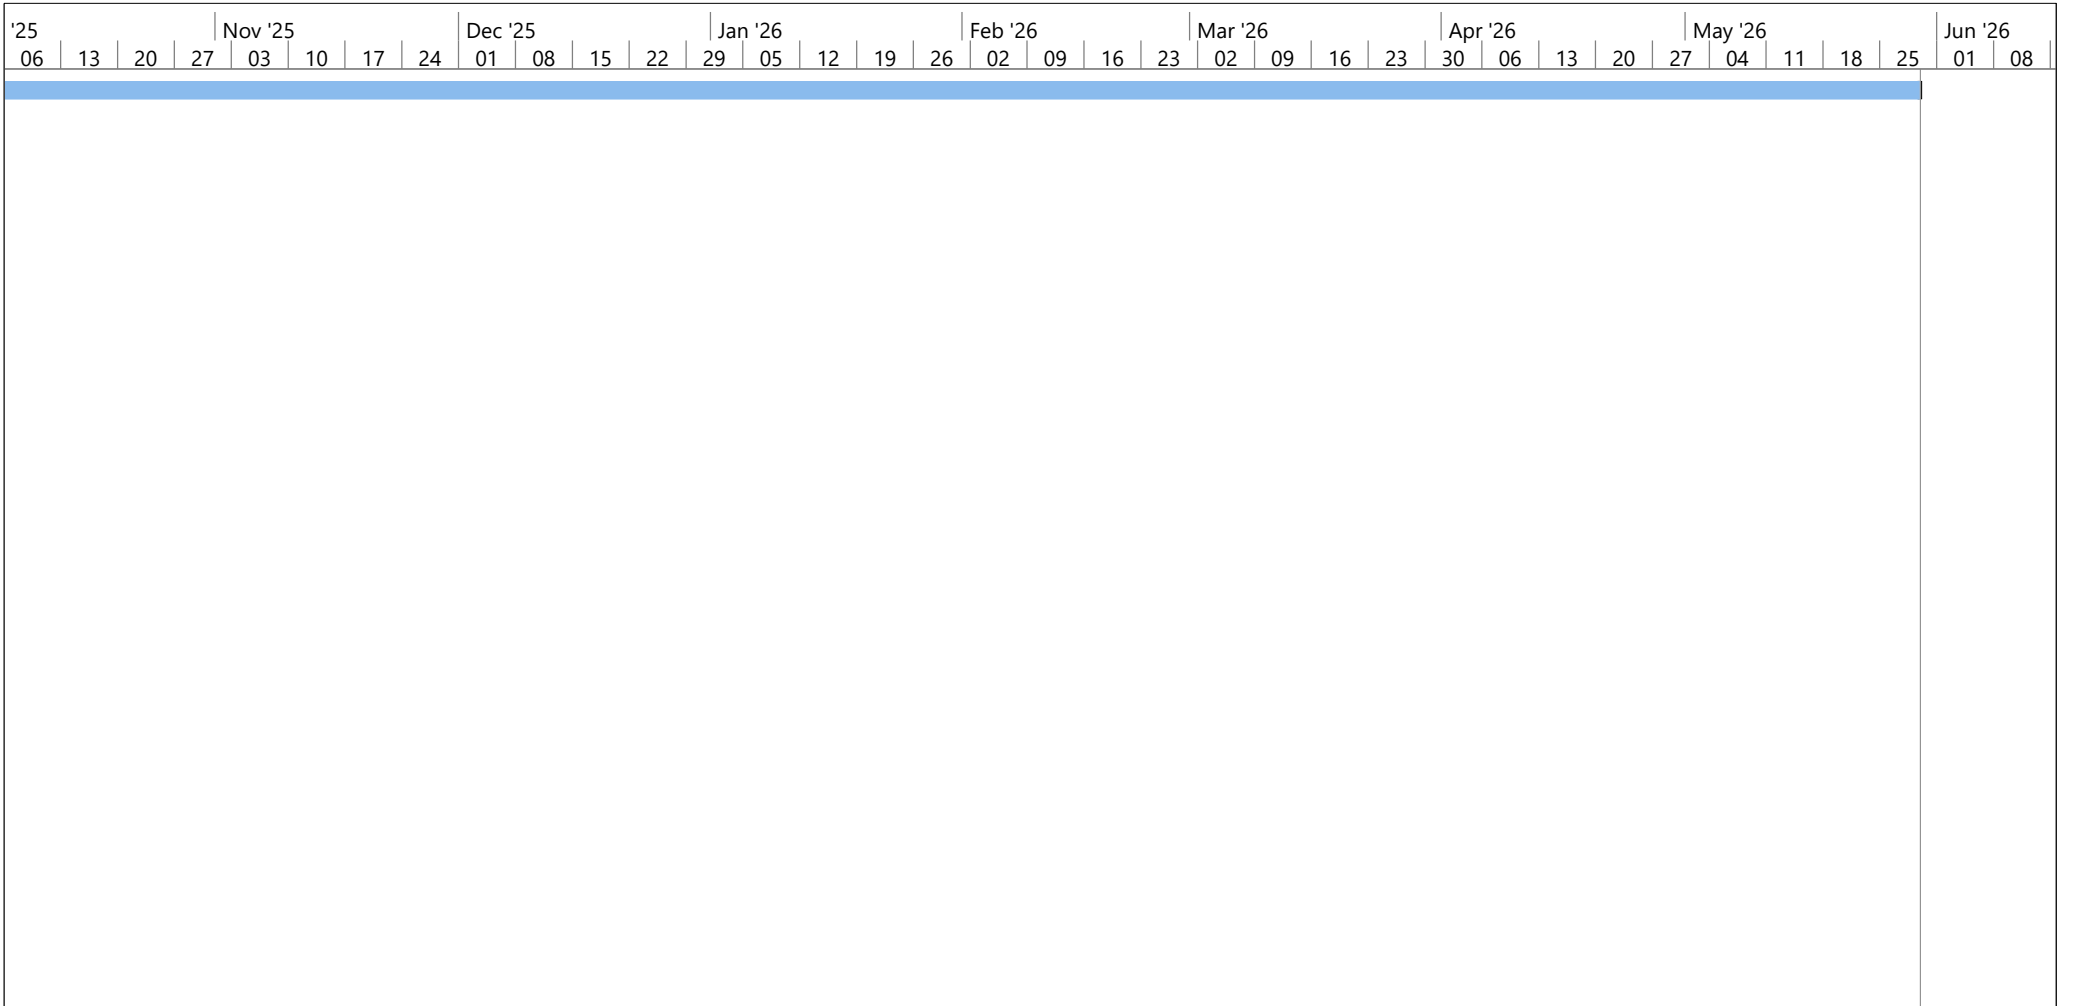


Project: PLAN DE ELABORAREA  
Date: Thu 28.11.24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			








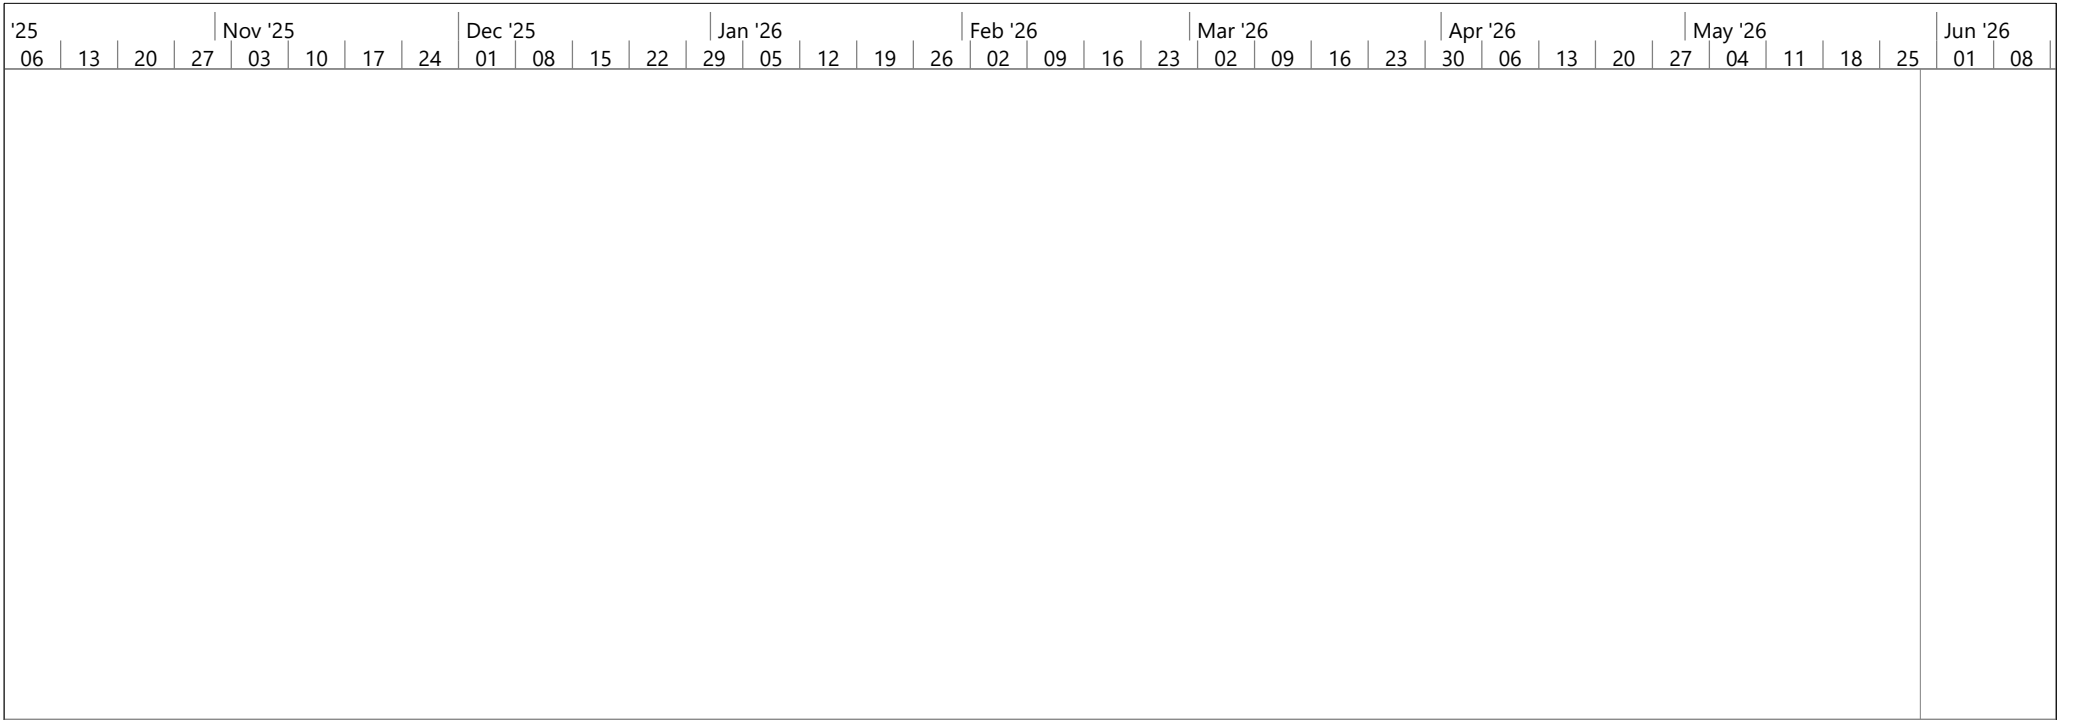













Project: PLAN DE ELABORAREA  
Date: Thu 28.11.24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			



Project: PLAN DE ELABORAREA  
Date: Thu 28.11.24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

'25 06 | 13 | 20 | 27 | Nov '25 03 | 10 | 17 | 24 | Dec '25 01 | 08 | 15 | 22 | 29 | Jan '26 05 | 12 | 19 | 26 | Feb '26 02 | 09 | 16 | 23 | Mar '26 02 | 09 | 16 | 23 | Apr '26 30 | 06 | 13 | 20 | 27 | May '26 04 | 11 | 18 | 25 | Jun '26 01 | 08 |



Project: PLAN DE ELABORAREA  
Date: Thu 28.11.24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			
