














































ID		Task Mode	Task Name	30 Aug '21
				M T W T F S
1			Moldova IPS	
2			Agreement signed	
3			Project management	
4			Phase 1 - Planning and Clarification: pre-study(Business Analysis Phase)	
5			Onsite visit for project pre-study analysis and solution negotiations	
6			National Switch Solution description preparation and GAPs analysis	
7			Hardware and software requirements analysis	
8			Off-site Tieto documents preparation	
9			Solution description preparation (including functional and technical architecture) preparations and list of gaps)	
10			Detailed project implementation plan creation	
11			Solution documentation review and approval by Customer	
12			Phase 2 - Environment and solution preparation (Design Phase)	
13			Preparatory work on customer site	
14			Purchase of hardware, system software, and other equipment	
15			Data centers set up	
16			HW, system software installation, other equipment (Servers, LAN). Test and production environment ready	
17			Customer Preparation works support	
18			Customer Data Center ready for implementation	
19			Preparatory work on Tieto site	
20			Licenses preparation	



Project: IPL_Estimation_ips_Mol Date: Fri 11.06.21	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

ID	i	Task Mode	Task Name	30 Aug '21					
				M	T	W	T	F	S
21		→	Tieto test environment preparation on Tieto premises - solution components installation and configuration						
22		→	Development						
23	👤	→	Pre-study agreed Gaps development						
24	👤	→	Development buffer - 300 hours						
25		→	Test activities						
26		→	Solution tests plan preparation						
27		→	Test plan review and approval by Customer						
28		→	Solution validation Testing						
29		→	Phase 3 - Solution preparation(Build phase)						
30		→	Solution intallation on Customer environments(Test, Training, Dev, PreProduction, Production)						
31		→	OS and Database configuration						
32		→	Kurbernets env. configuration						
33		→	Instant Payment deployment on Kubernetes env. and optimization						
34		→	Instant Payment business configuration						
35		→	Central Alias service deployment and optimization						
36		→	Central Alias business configuration						
37		→	Statistic, reporting and monitoring alerts technical configuration						
38		→	Business reporting configuration						
39		→	PKI env. setup and configuration						
40		→	Liquidity monitoring and management setup						
41		→	RTGS and Instant payment interface setup and configuration						
42		→	Participant portal setup & configuration, including access rights						

Project: IPL_Estimation_ips_Mol
Date: Fri 11.06.21

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

ID	i	Task Mode	Task Name	30 Aug '21						
				M	T	W	T	F	S	
43		→	Participant unreachable setup							
44		→	Audit trail setup							
45		→	Deployment guide preparation							
46		→	HA configuration							
47		→	Functional solution tests(without participants)							
48	●●	→	System Deployment on all envs. - Test/Training/Dev/Pre-Production/Production							
49	●●	→	Support of connection to Instant Payment solution of 2-x Bank participants							
50		→	Support of connection to Central Alias Service of 2-x Bank participants							
51		→	Functional tests with 2-x Bank participants & RTGS system							
52		→	System integration testing							
53		→	Training Phase							
54		→	Training for Customer's personnel							
55		→	Testing Phase							
56		→	Functional testing							
57		→	Hight Availabilty solution testing							
58		→	Remote support during UAT							
59		→	Security testing							
60		→	Load testing							
61		→	Usability testing							
62		→	Storage & Volumes testing							
63		→	Installation testing							
64		→	Documentation testing							

Project: IPL_Estimation_ips_Mol Date: Fri 11.06.21	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

ID	i	Task Mode	Task Name	30 Aug '21						
				M	T	W	T	F	S	
65		→	Recovery and continuity testing							
66		→	Phase 4 - Go live and Final Acceptance phases - Pilot							
67		→	Consultation to configure on production system and pilot project start							
68		→	Monitoring after pilot go-live							
69		→	Phase 5 - Go live and Final Acceptance phases							
70		→	Rollout consultations of all national system participants							
71		→	Technical deployment completion and delivery to Customer							
72		→	Phase 6 - Transfer to maintenance mode							
73		→	Transfer to support department							
74		→	Project closing							

Project: IPL_Estimation_ips_Mol Date: Fri 11.06.21	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S

06 Sep '21

13 Sep '21

20 Sep '21

27 Sep '21


04 Oct '21

11 Oct '21

18 Oct '21


oEVRY;NBM

oEVRY;NBM

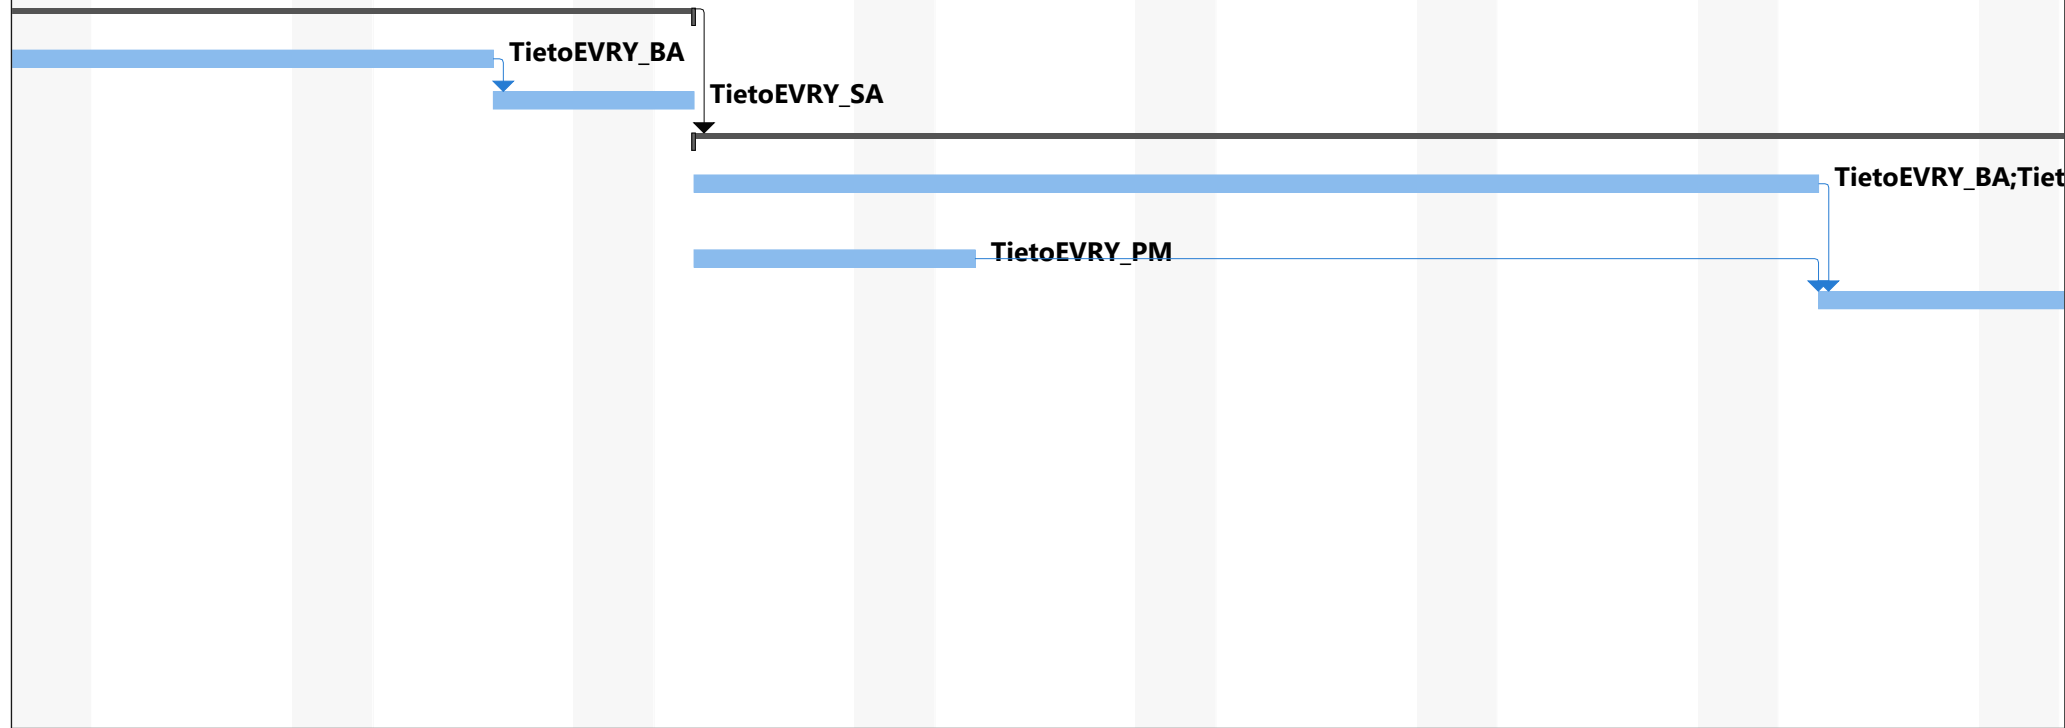


Project: IPL_Estimation_ips_Mol
Date: Fri 11.06.21

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

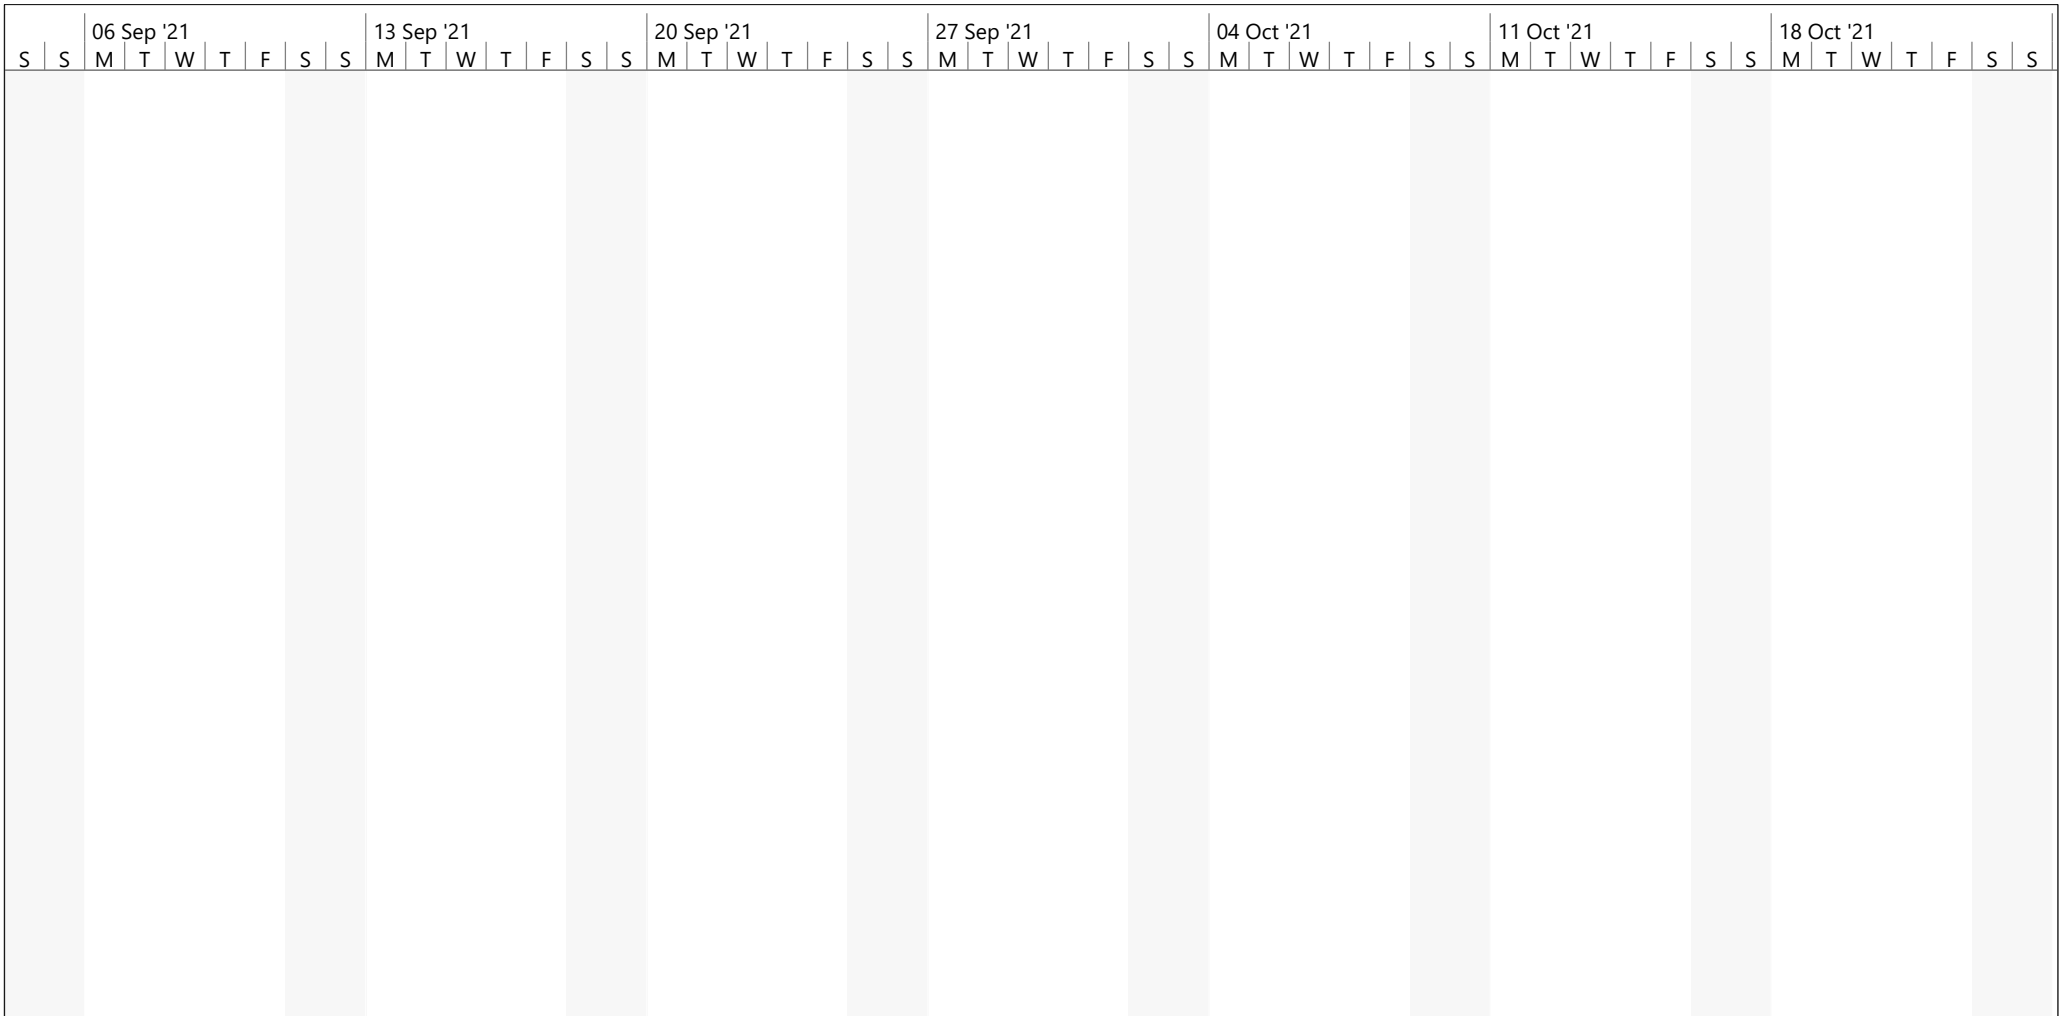


Project: IPL_Estimation_ips_Mol
Date: Fri 11.06.21

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

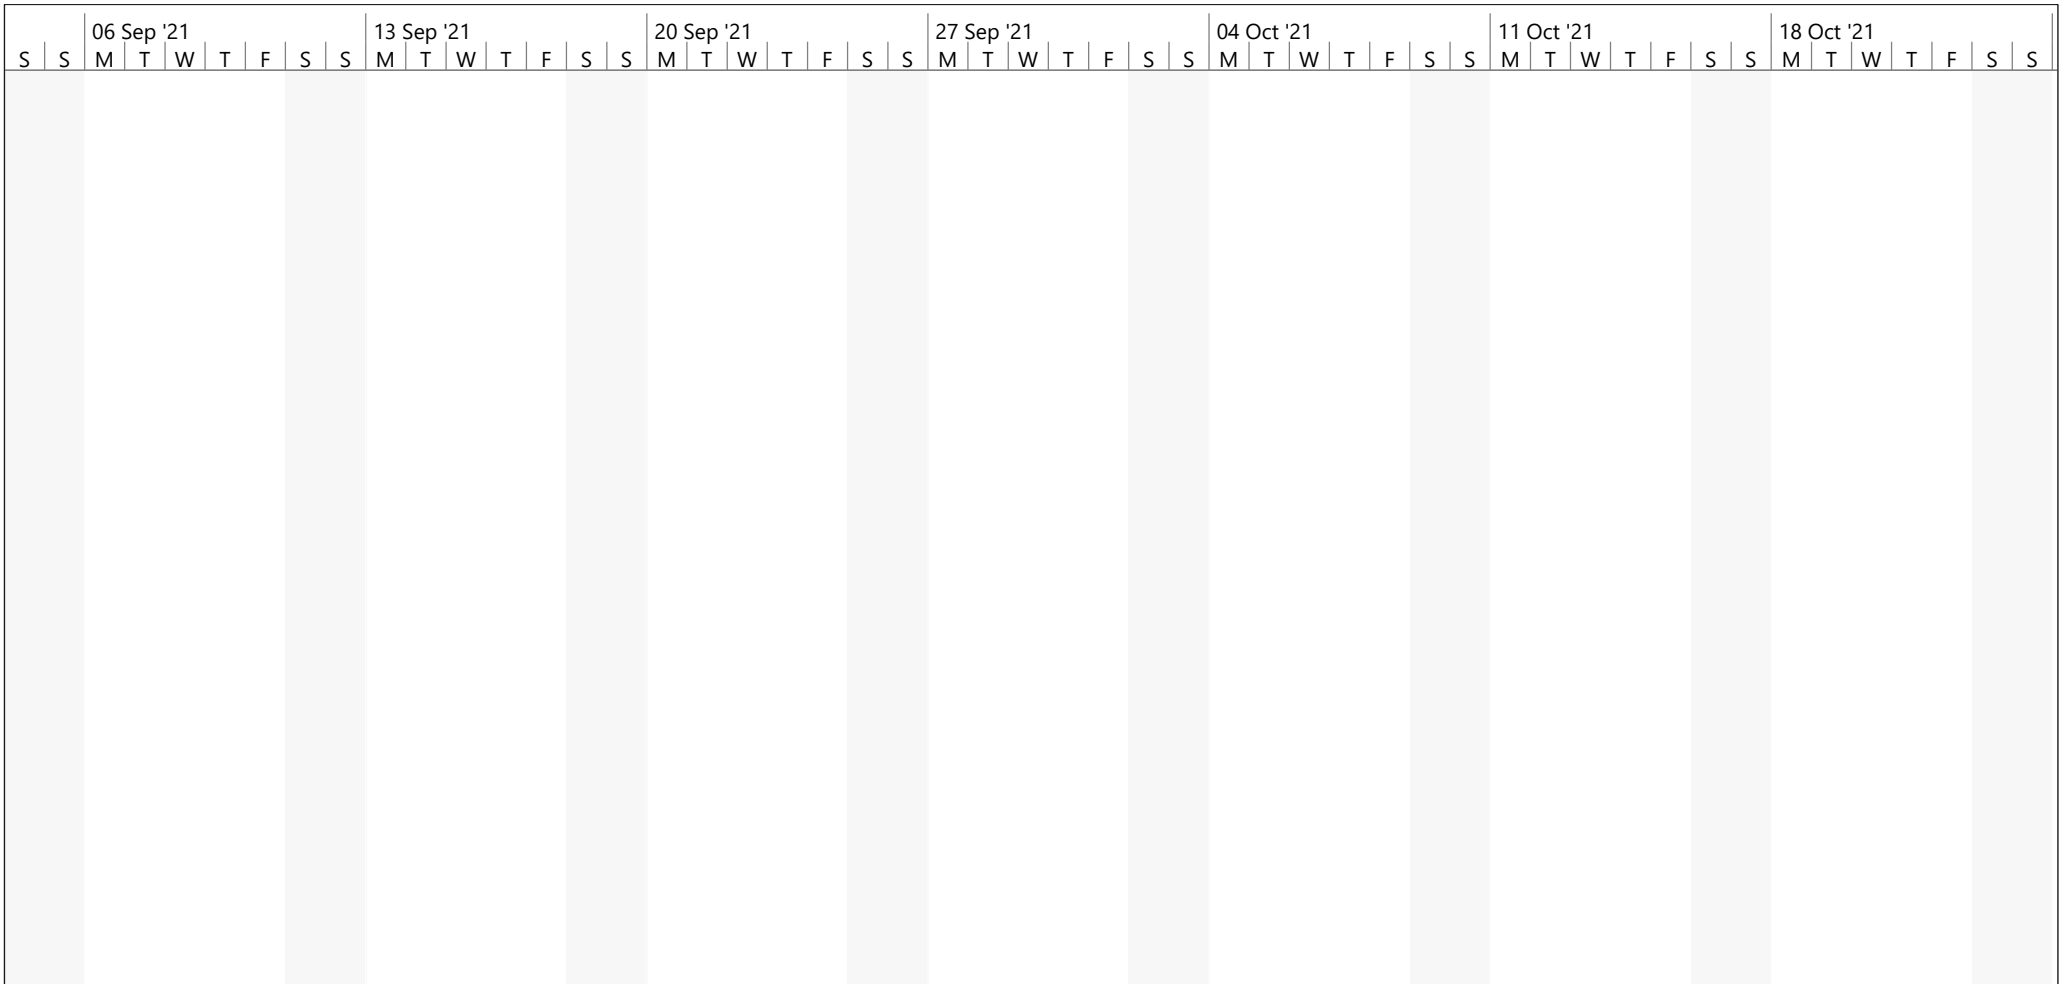


Project: IPL_Estimation_ips_Mol
Date: Fri 11.06.21

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			



Project: IPL_Estimation_ips_Mol Date: Fri 11.06.21	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

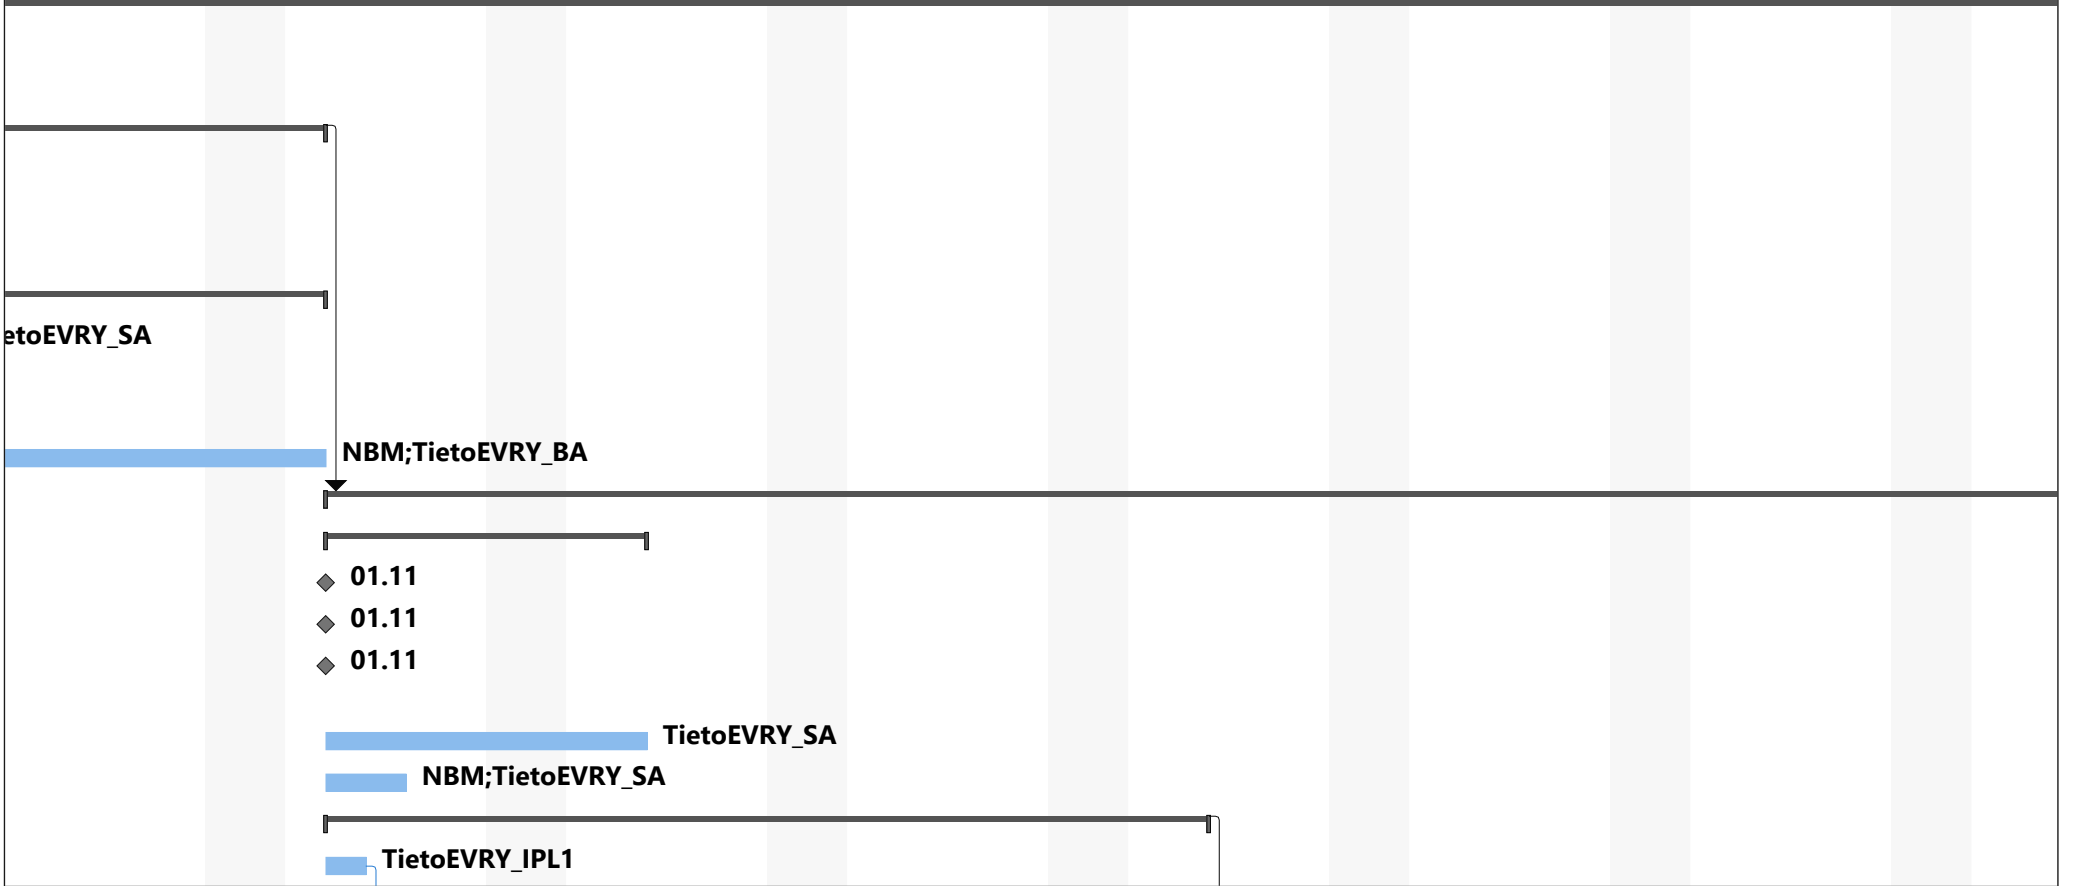


Project: IPL_Estimation_ips_Mol
Date: Fri 11.06.21

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




Project: IPL_Estimation_ips_Mol
Date: Fri 11.06.21




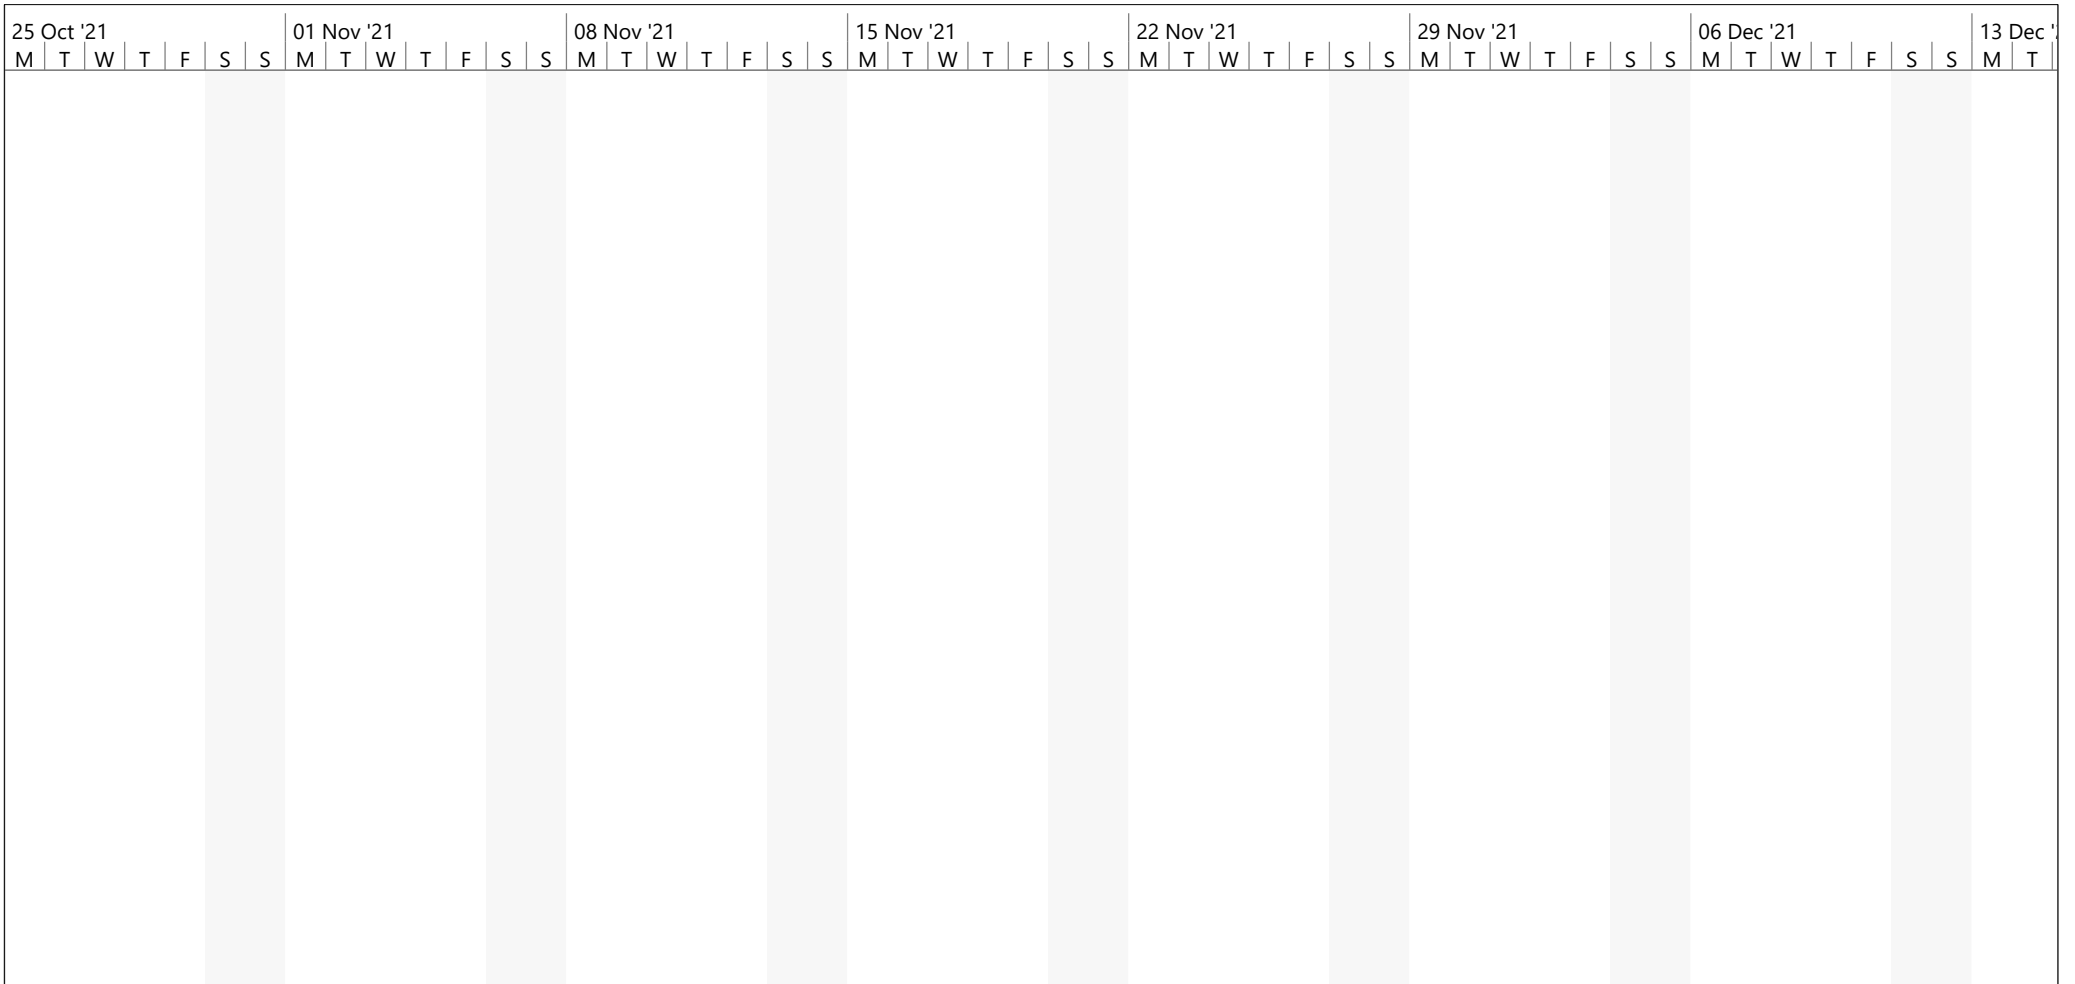















Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




Project: IPL_Estimation_ips_Mol
Date: Fri 11.06.21

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




Project: IPL_Estimation_ips_Mol Date: Fri 11.06.21	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

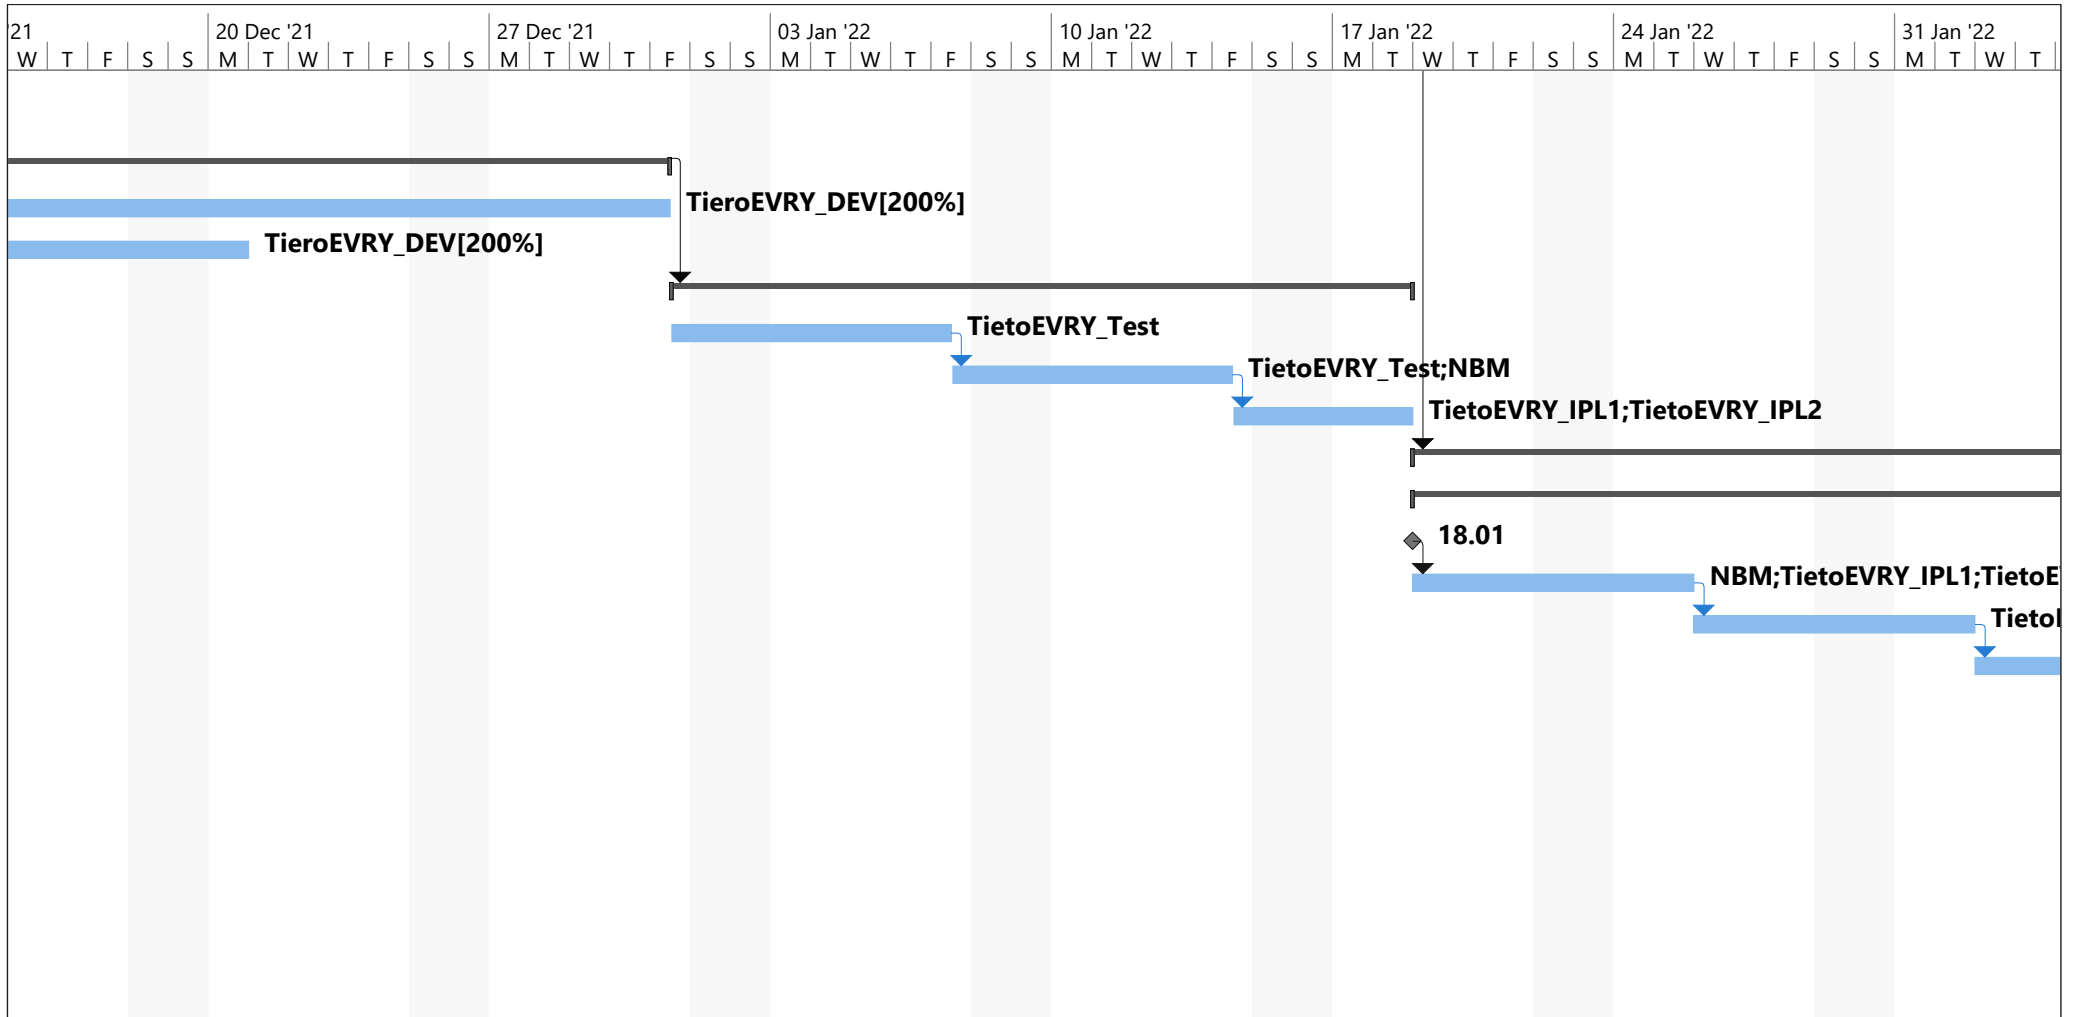


Project: IPL_Estimation_ips_Mol
Date: Fri 11.06.21

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

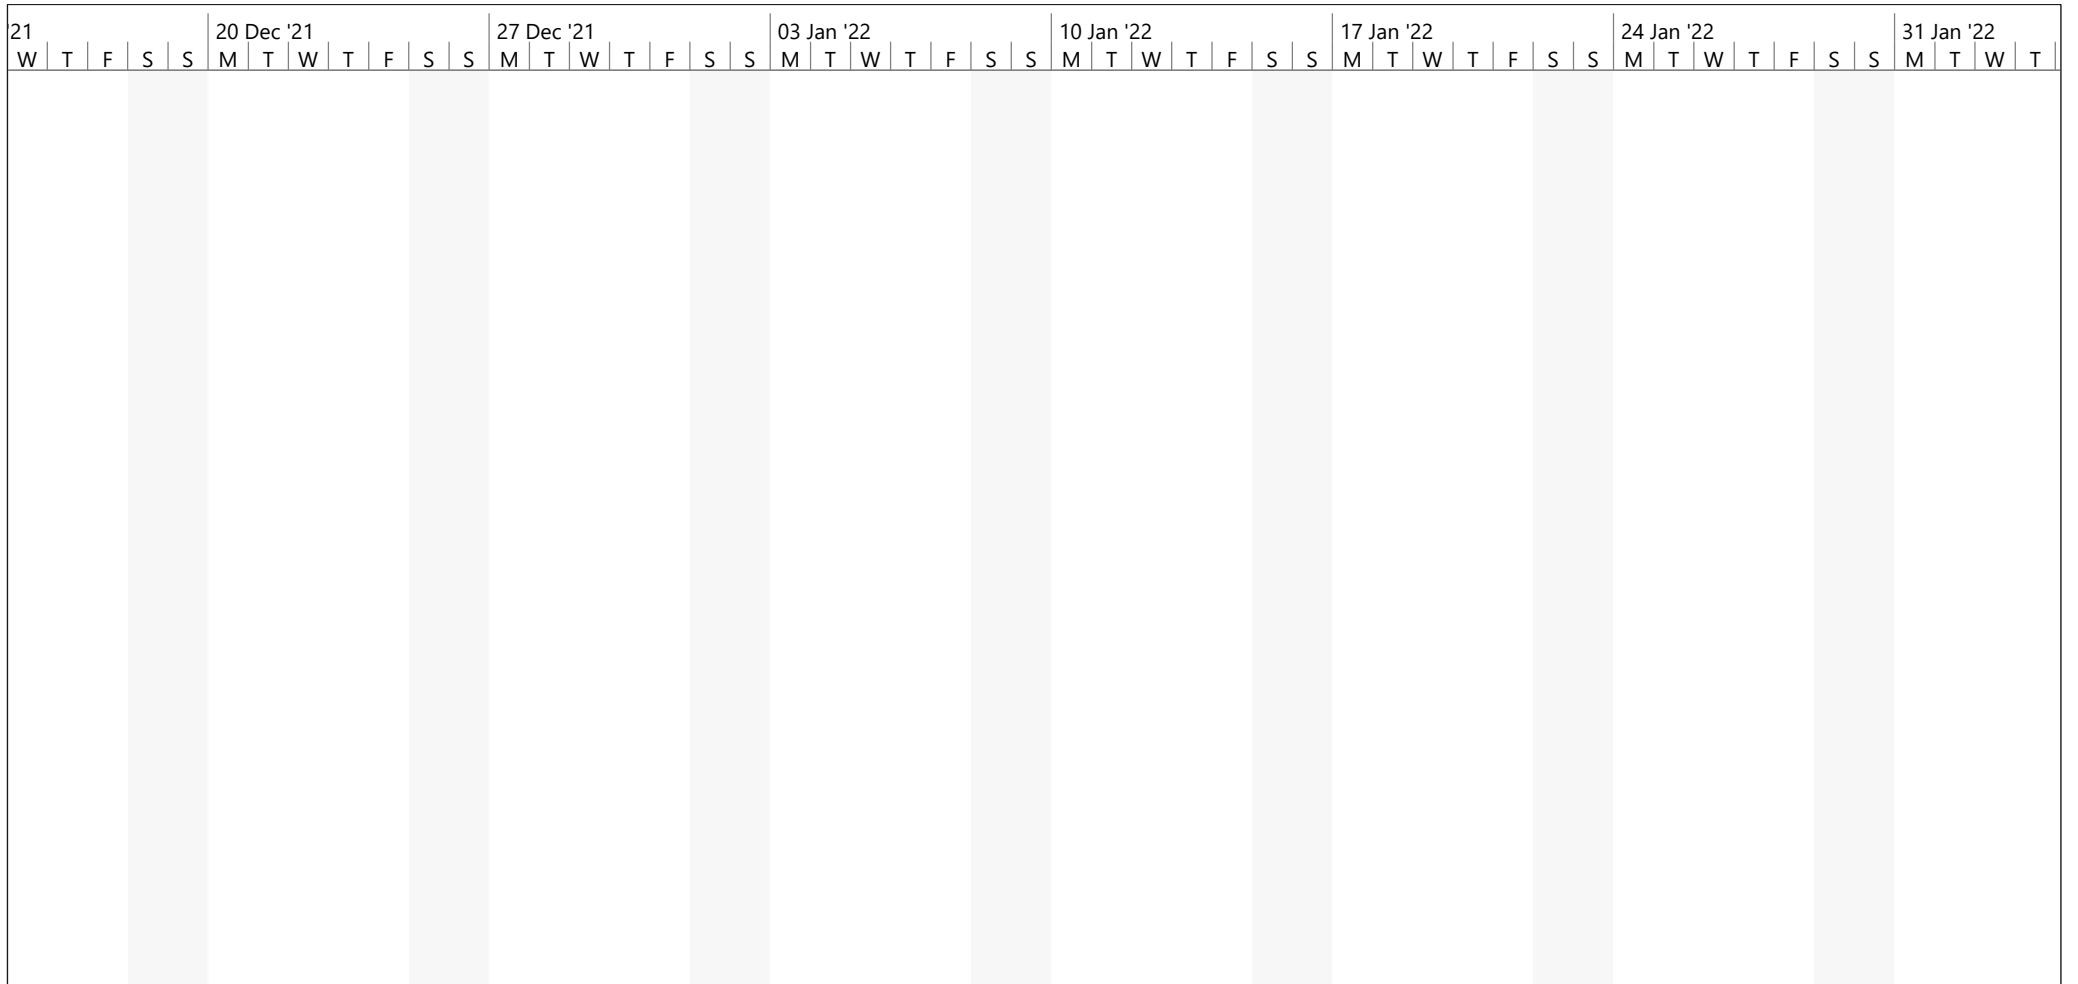


Project: IPL_Estimation_ips_Mol
Date: Fri 11.06.21

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			





Project: IPL_Estimation_ips_Mol Date: Fri 11.06.21	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

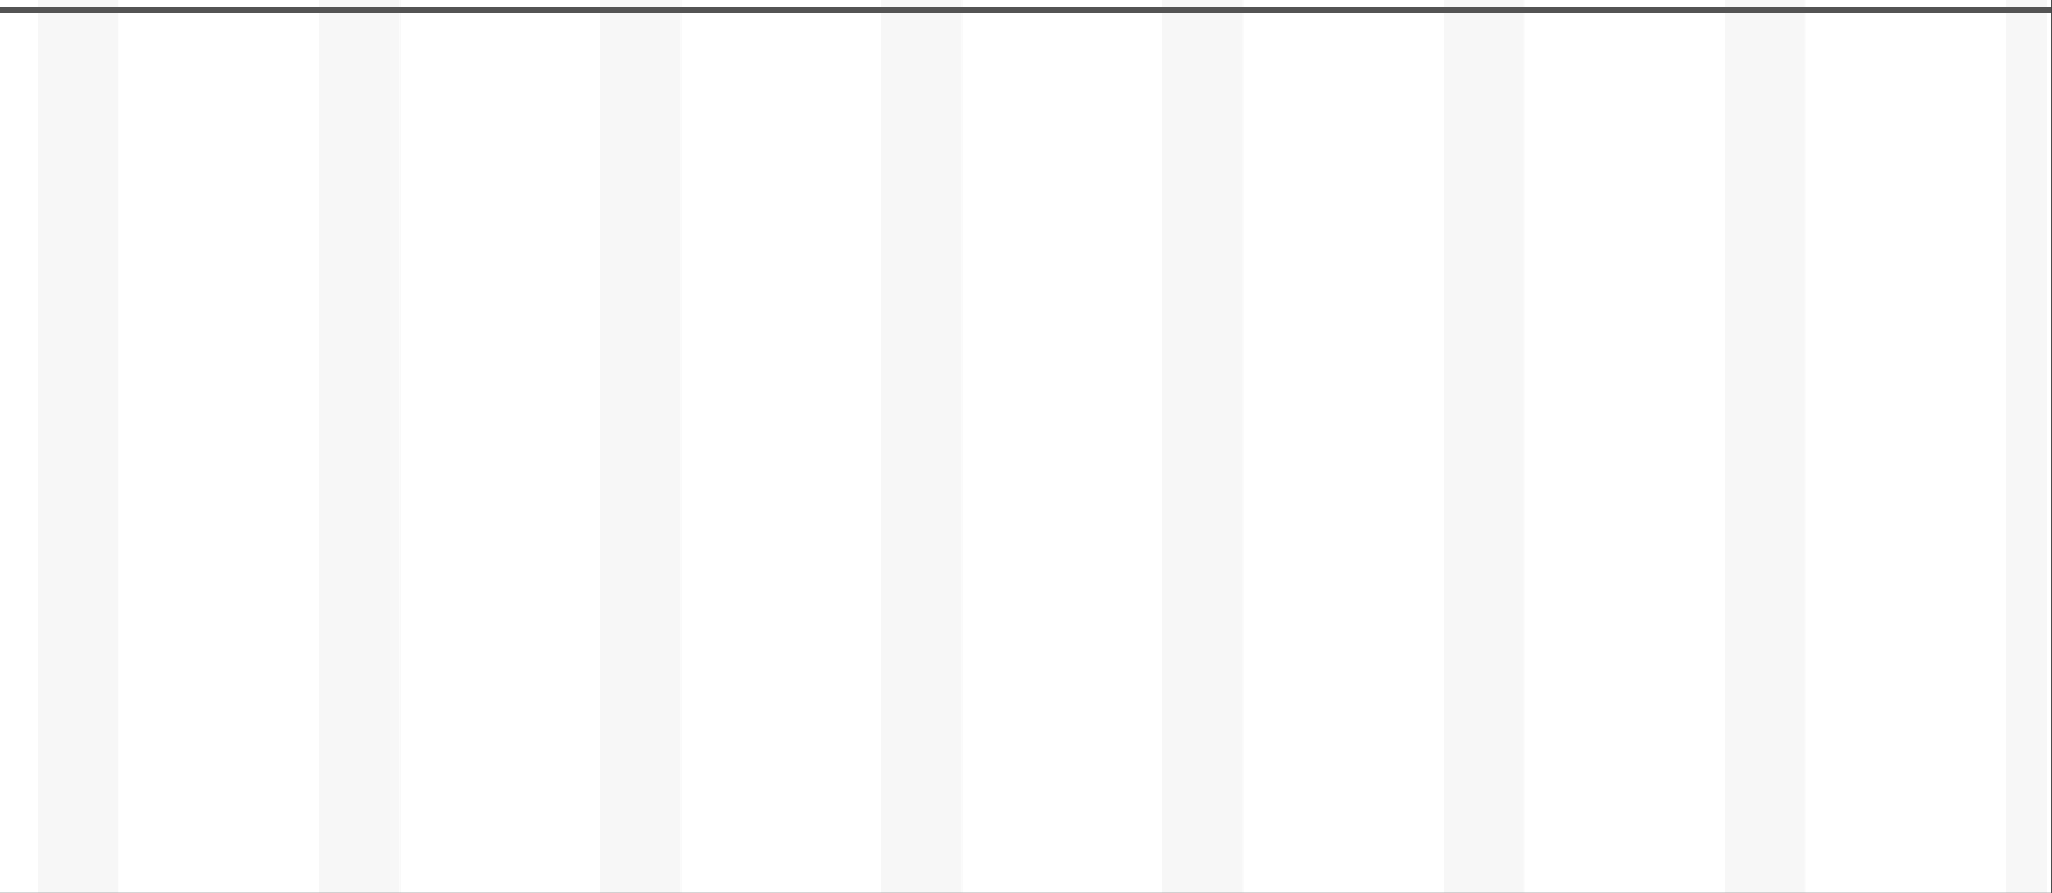


Project: IPL_Estimation_ips_Mol
Date: Fri 11.06.21

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

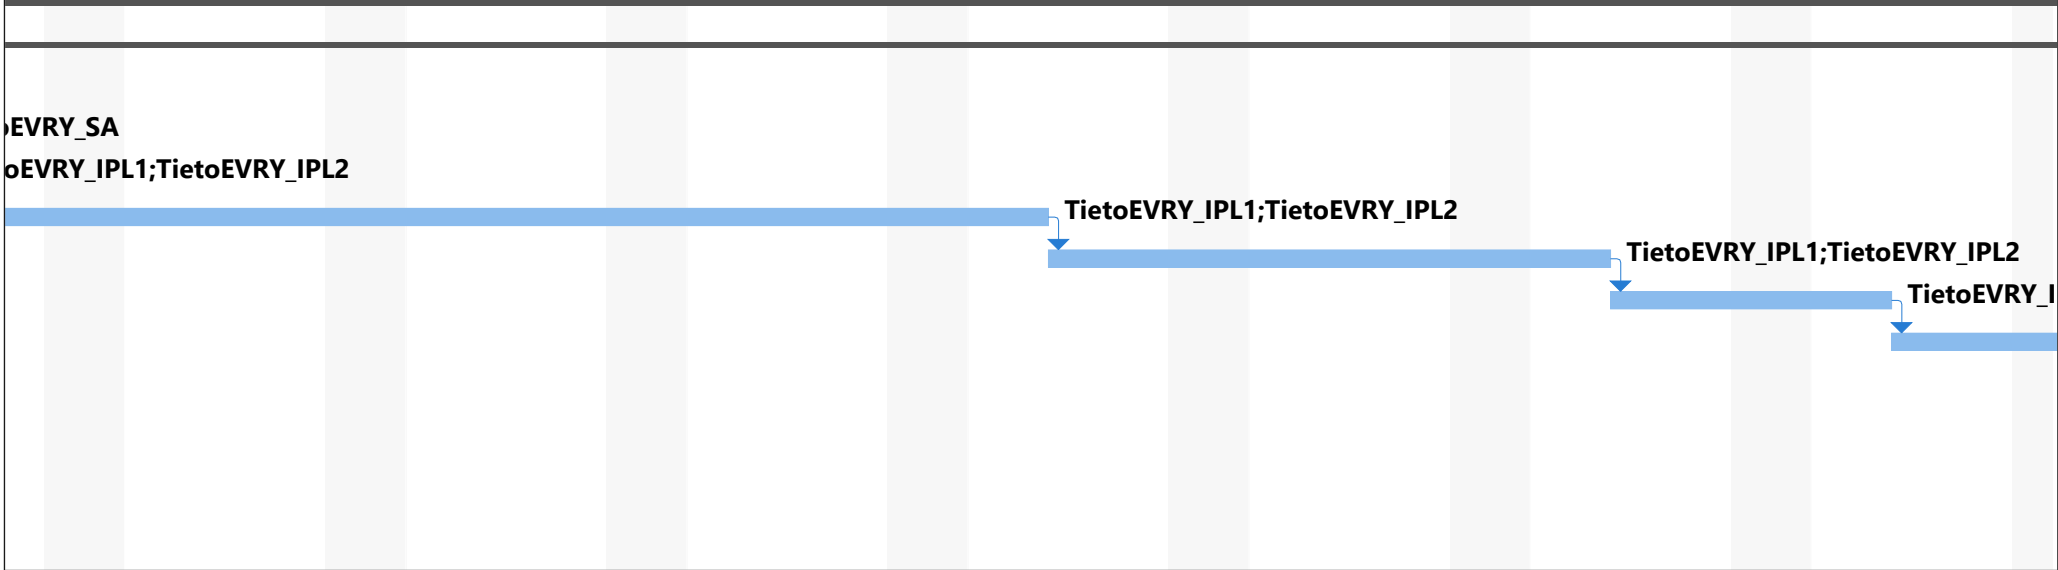








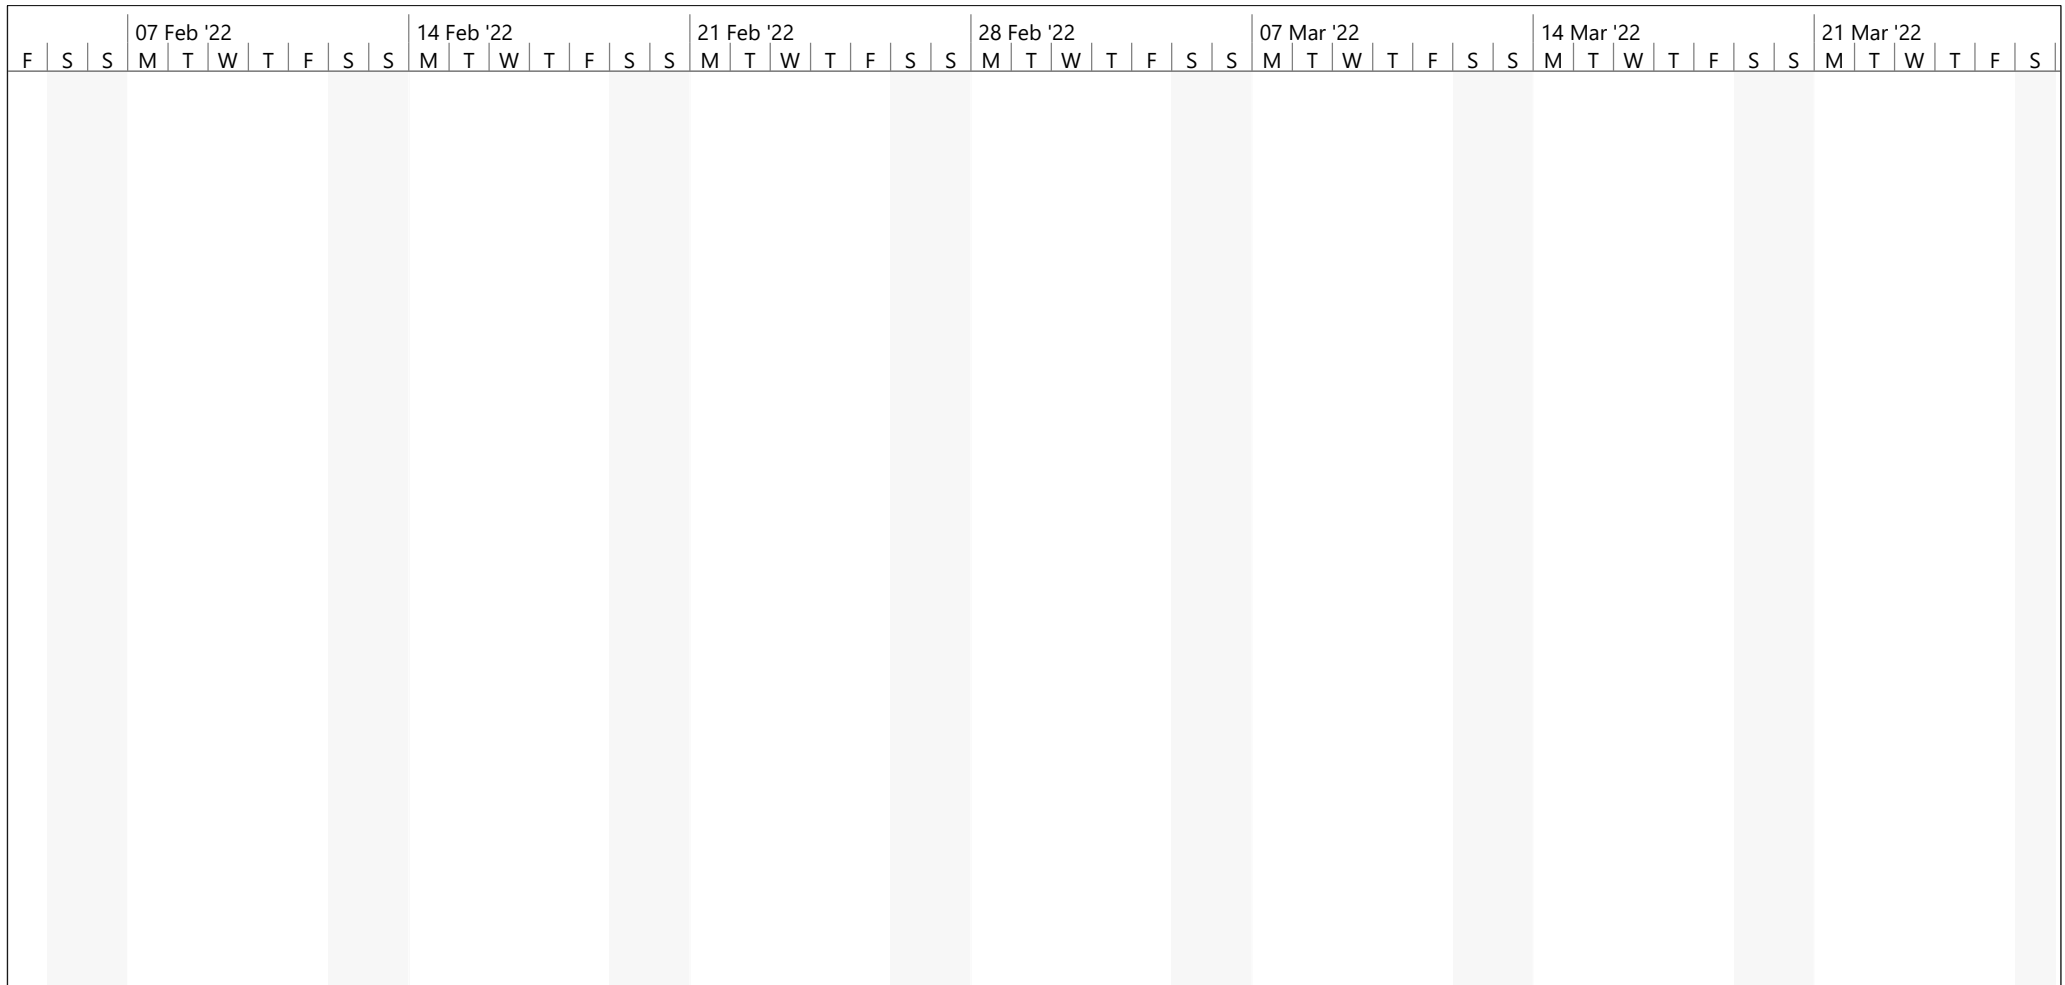












Project: IPL_Estimation_ips_Mol
 Date: Fri 11.06.21

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




Project: IPL_Estimation_ips_Mol
Date: Fri 11.06.21

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			





Project: IPL_Estimation_ips_Mol Date: Fri 11.06.21	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

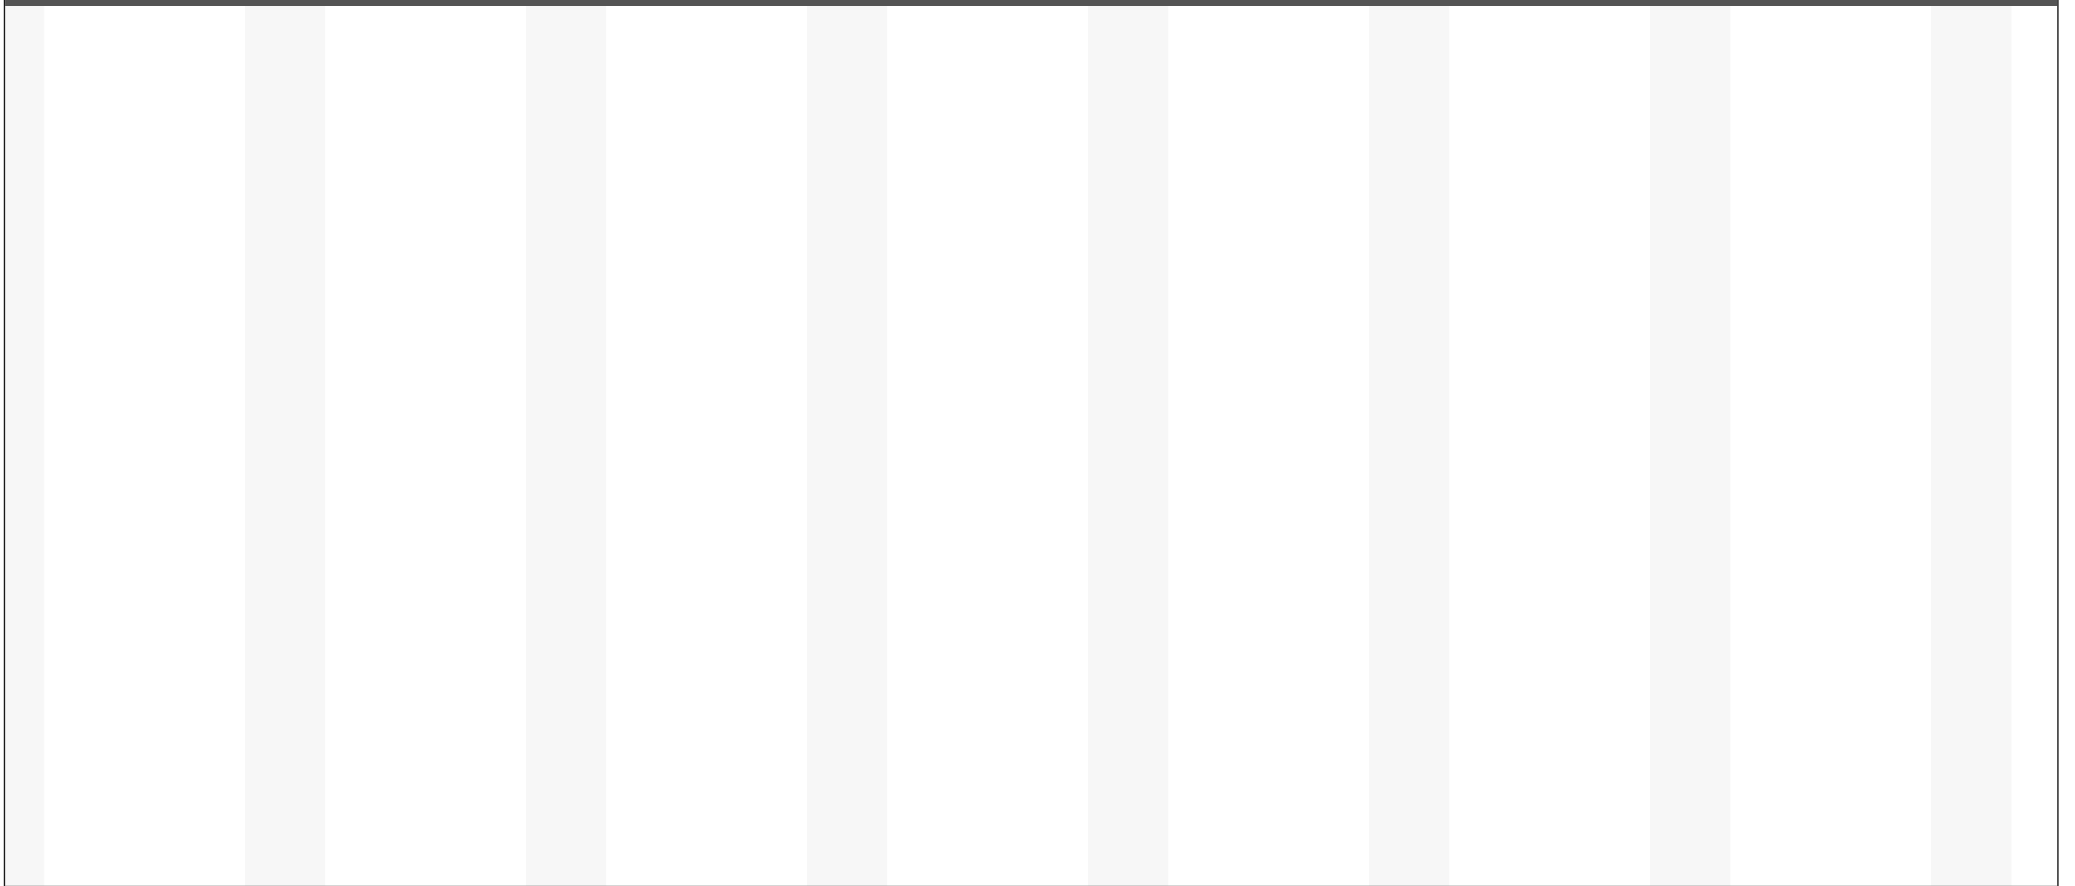


Project: IPL_Estimation_ips_Mol
Date: Fri 11.06.21

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

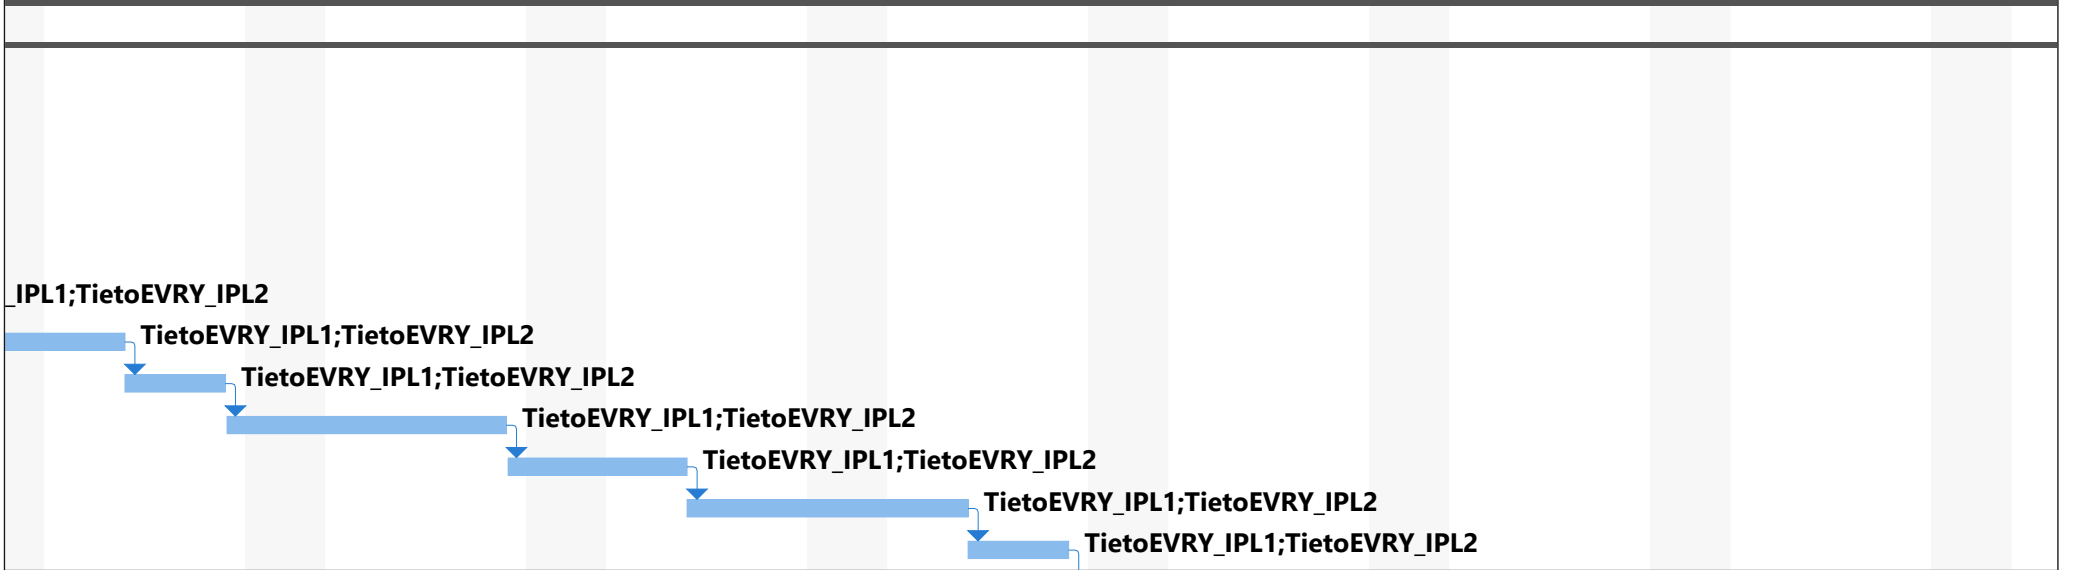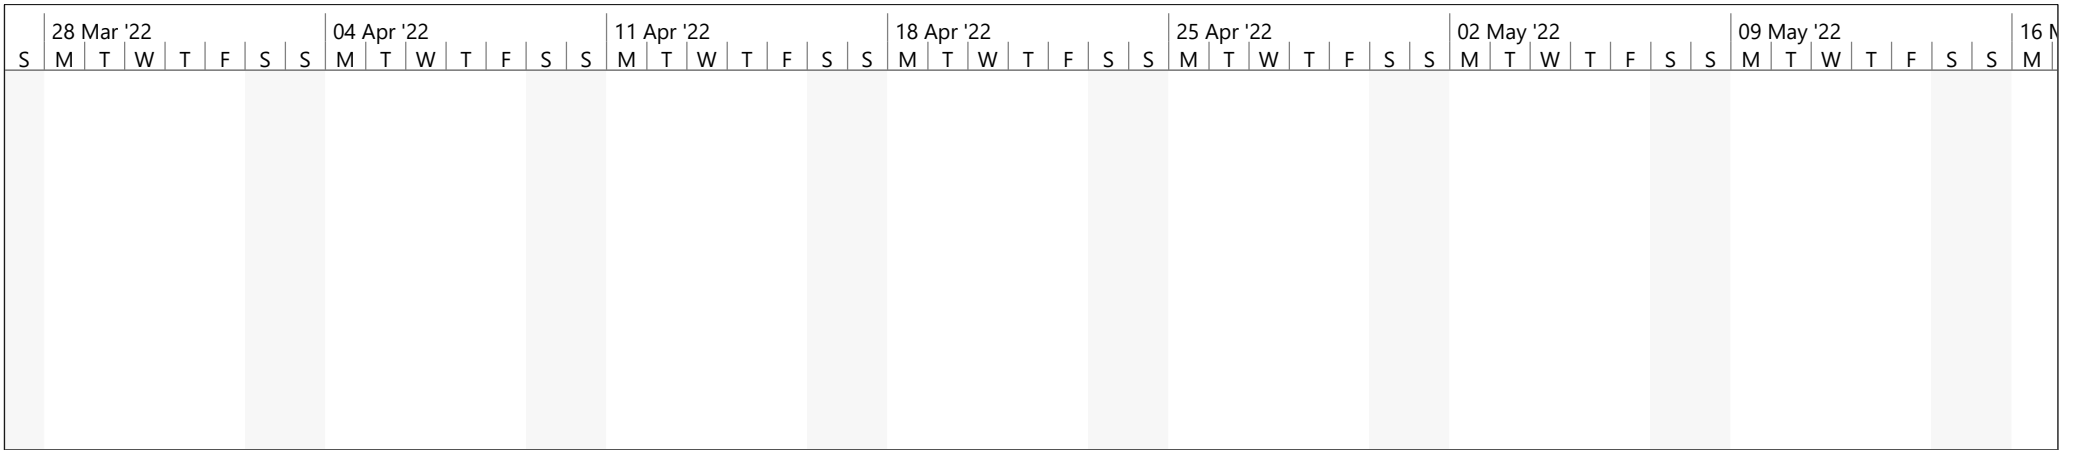


Project: IPL_Estimation_ips_Mol
Date: Fri 11.06.21

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

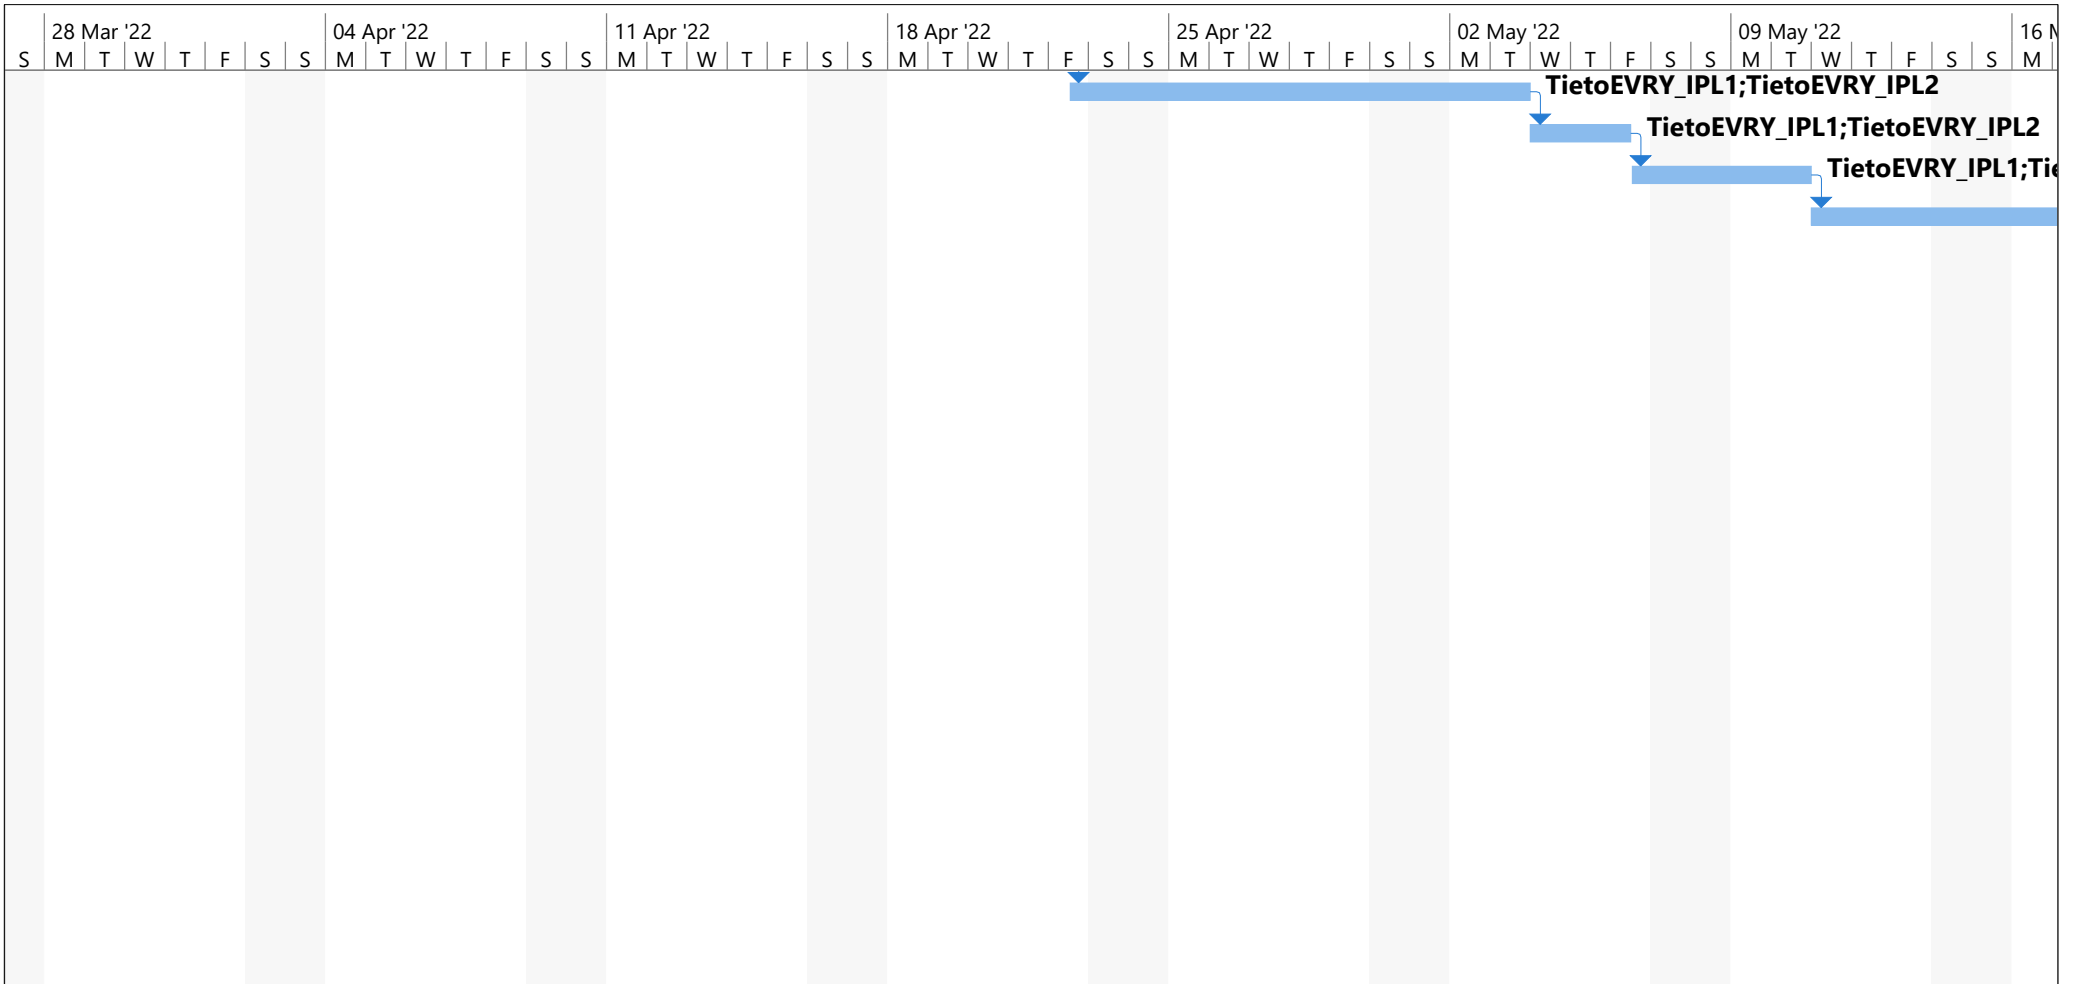


Project: IPL_Estimation_ips_Mol
Date: Fri 11.06.21

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




Project: IPL_Estimation_ips_Mol Date: Fri 11.06.21	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

May '22	23 May '22	30 May '22	06 Jun '22	13 Jun '22	20 Jun '22	27 Jun '22	04 Jul '22
T W T F S S	M T W T F S S	M T W T F S S	M T W T F S S	M T W T F S S	M T W T F S S	M T W T F S S	M T W

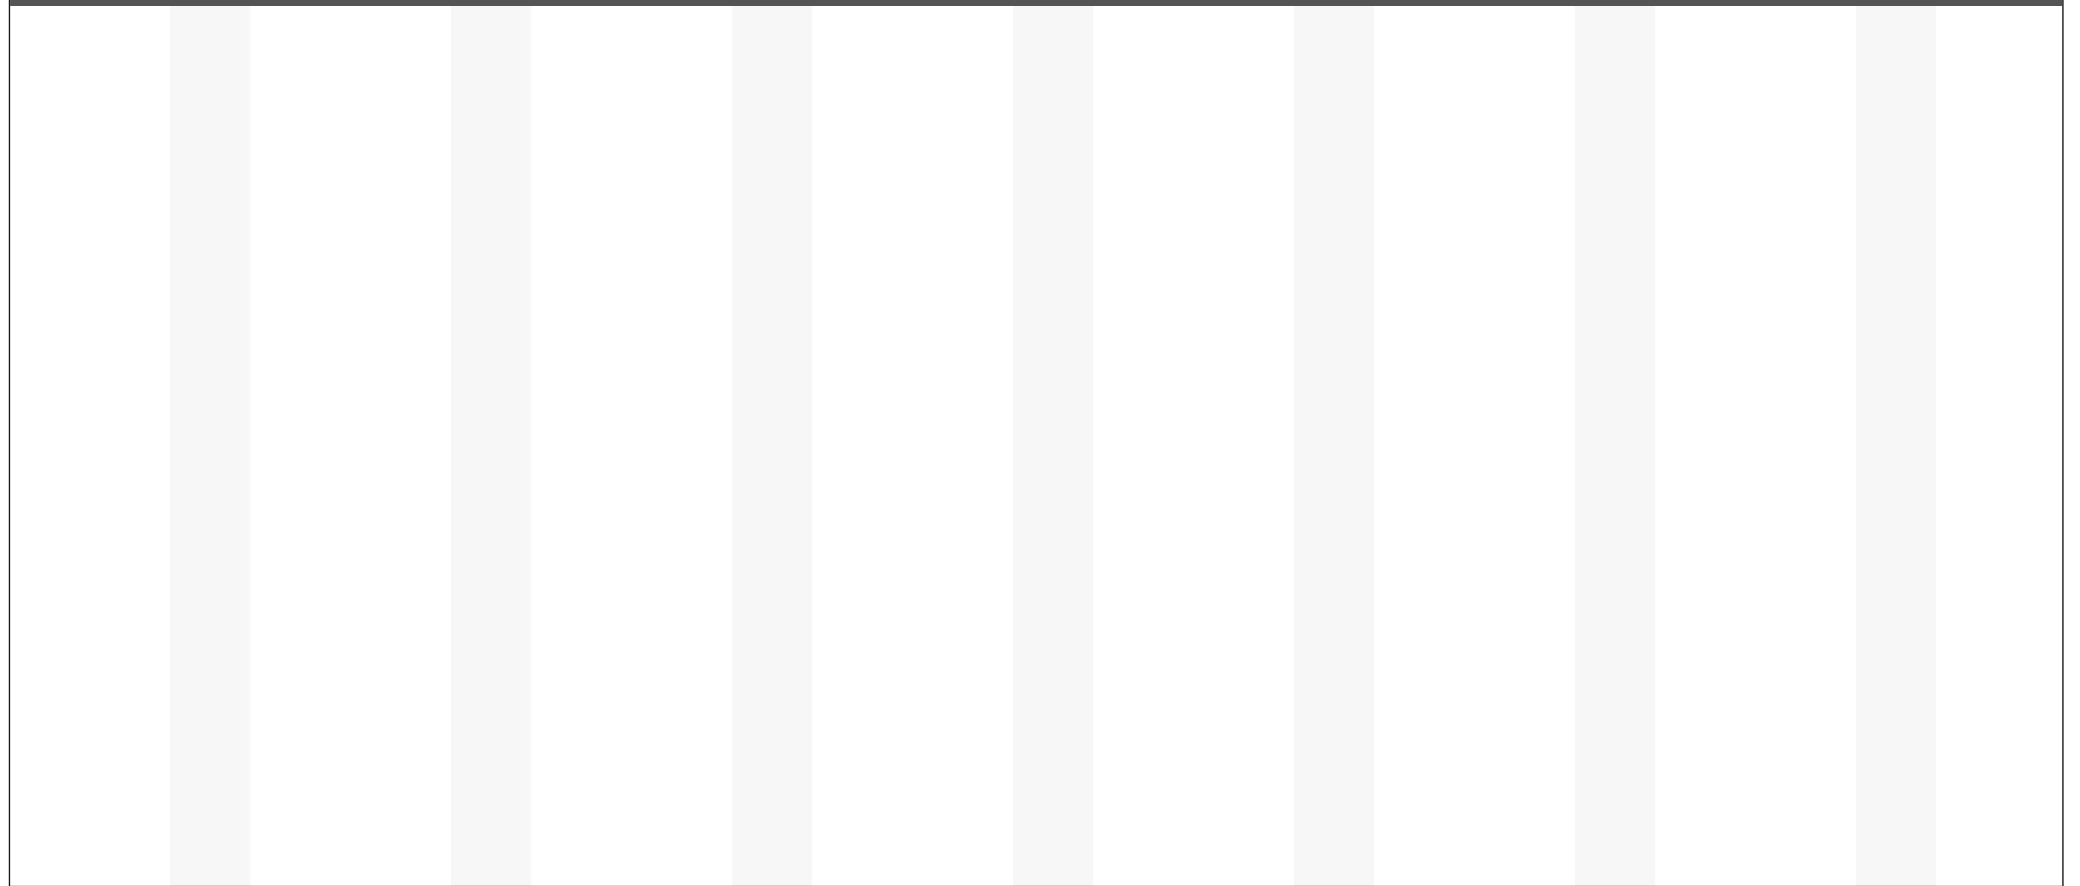

Project: IPL_Estimation_ips_Mol
Date: Fri 11.06.21

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

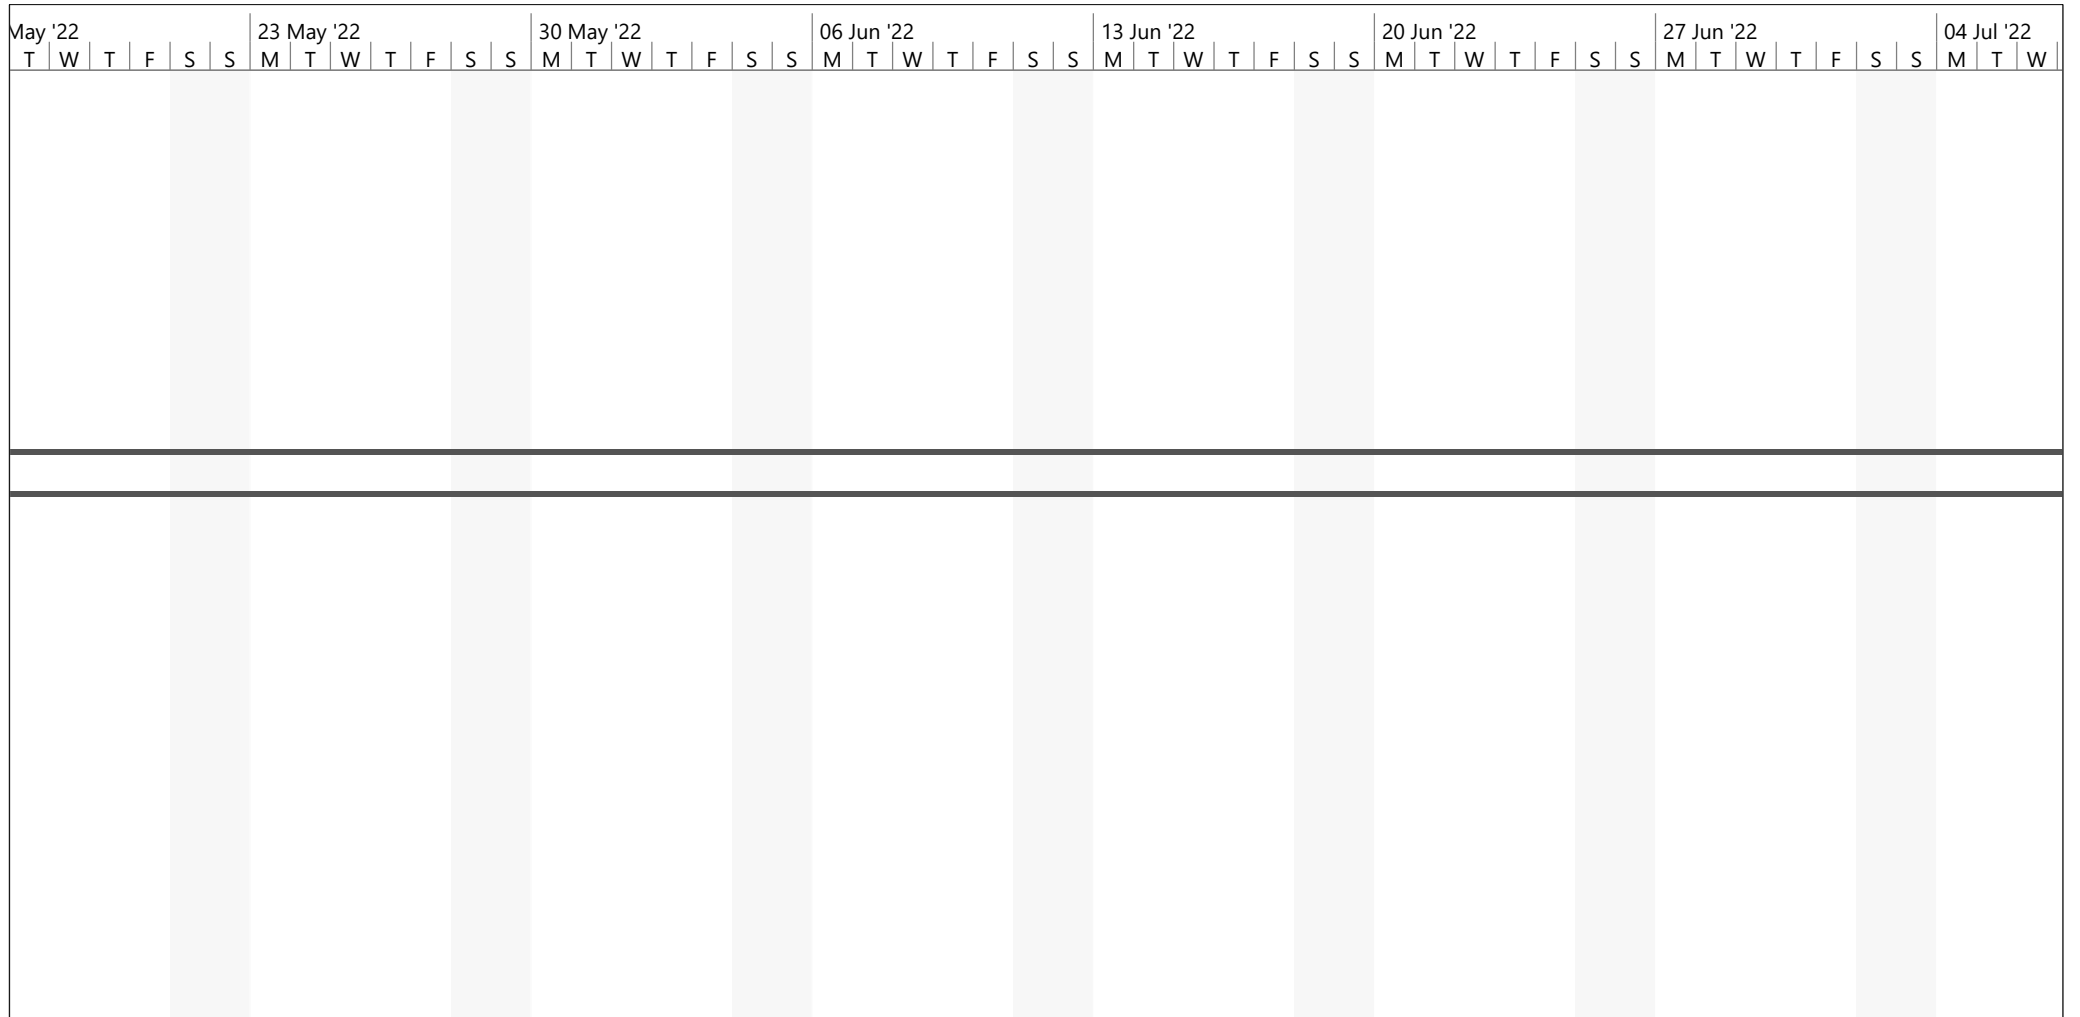


Project: IPL_Estimation_ips_Mol
Date: Fri 11.06.21

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




Project: IPL_Estimation_ips_Mol
Date: Fri 11.06.21

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




Project: IPL_Estimation_ips_Mol Date: Fri 11.06.21	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

T	F	S	S	11 Jul '22	M	T	W	T	F	S	S	18 Jul '22	M	T	W	T	F	S	S	25 Jul '22	M	T	W	T	F	S	S	01 Aug '22	M	T	W	T	F	S	S	08 Aug '22	M	T	W	T	F	S	S	15 Aug '22	M	T	W	T	F	S	S	22 Aug '22	M	T	W	T	F	S	S
---	---	---	---	------------	---	---	---	---	---	---	---	------------	---	---	---	---	---	---	---	------------	---	---	---	---	---	---	---	------------	---	---	---	---	---	---	---	------------	---	---	---	---	---	---	---	------------	---	---	---	---	---	---	---	------------	---	---	---	---	---	---	---

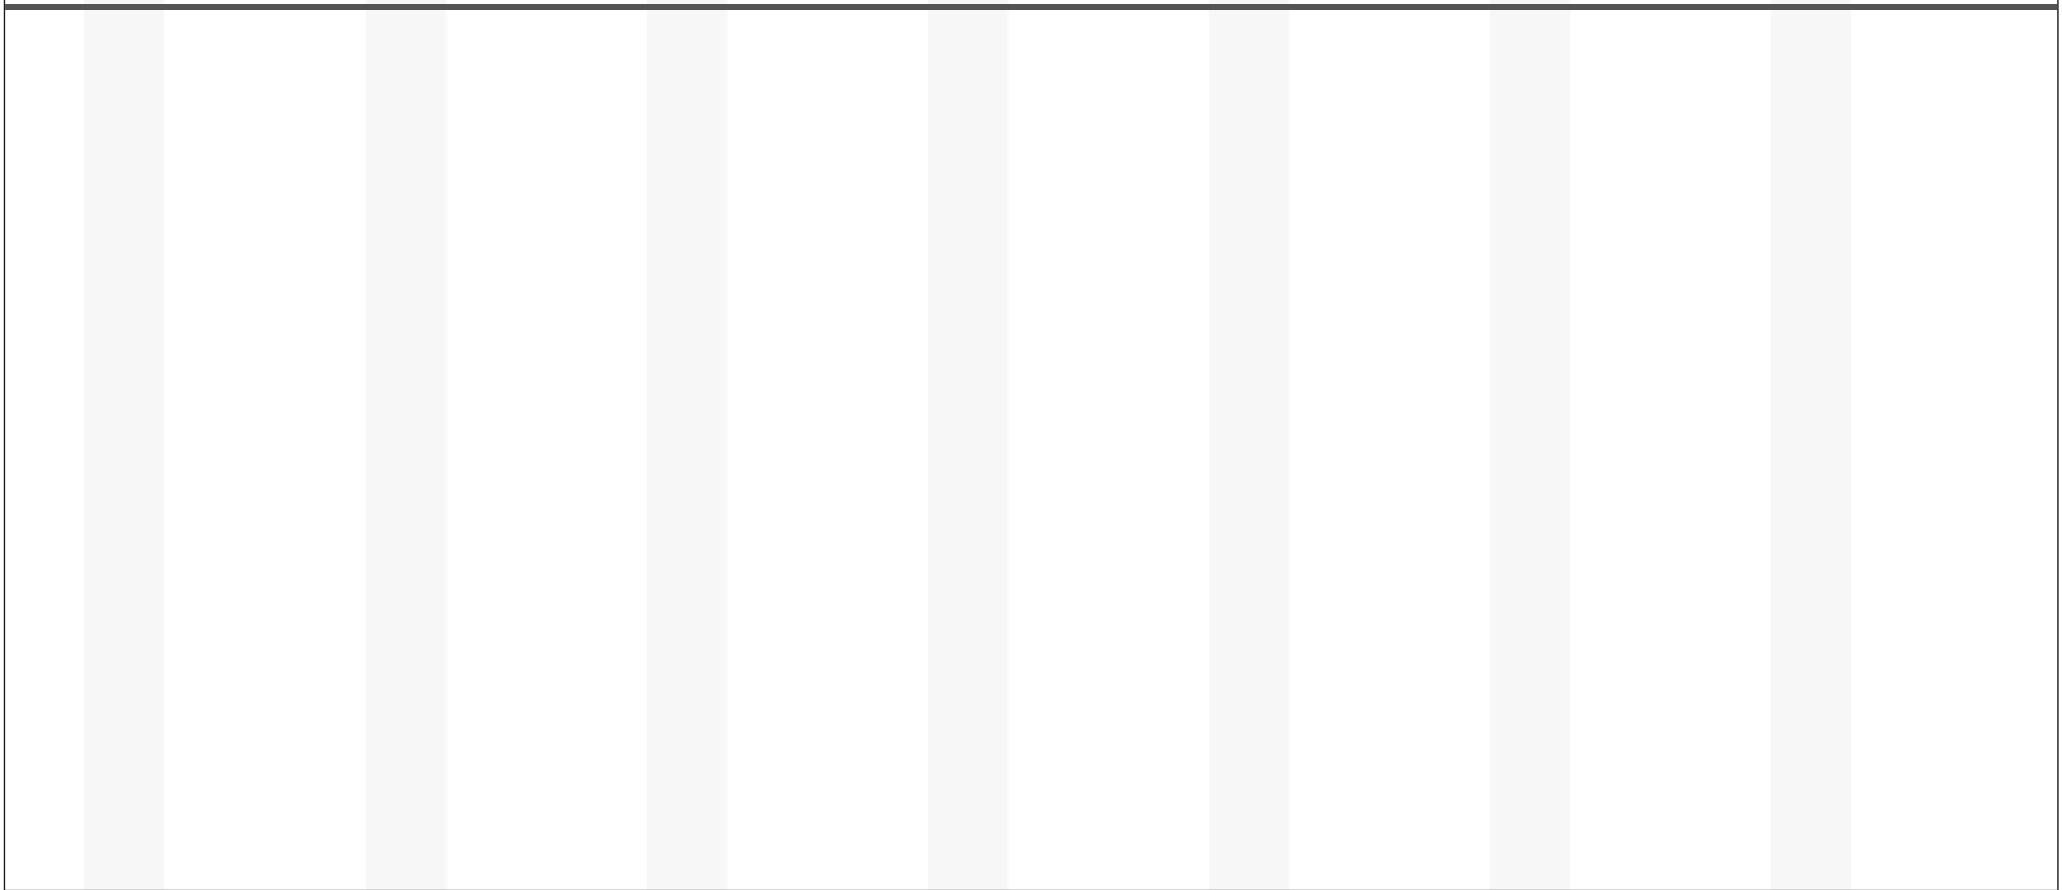


Project: IPL_Estimation_ips_Mol Date: Fri 11.06.21	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

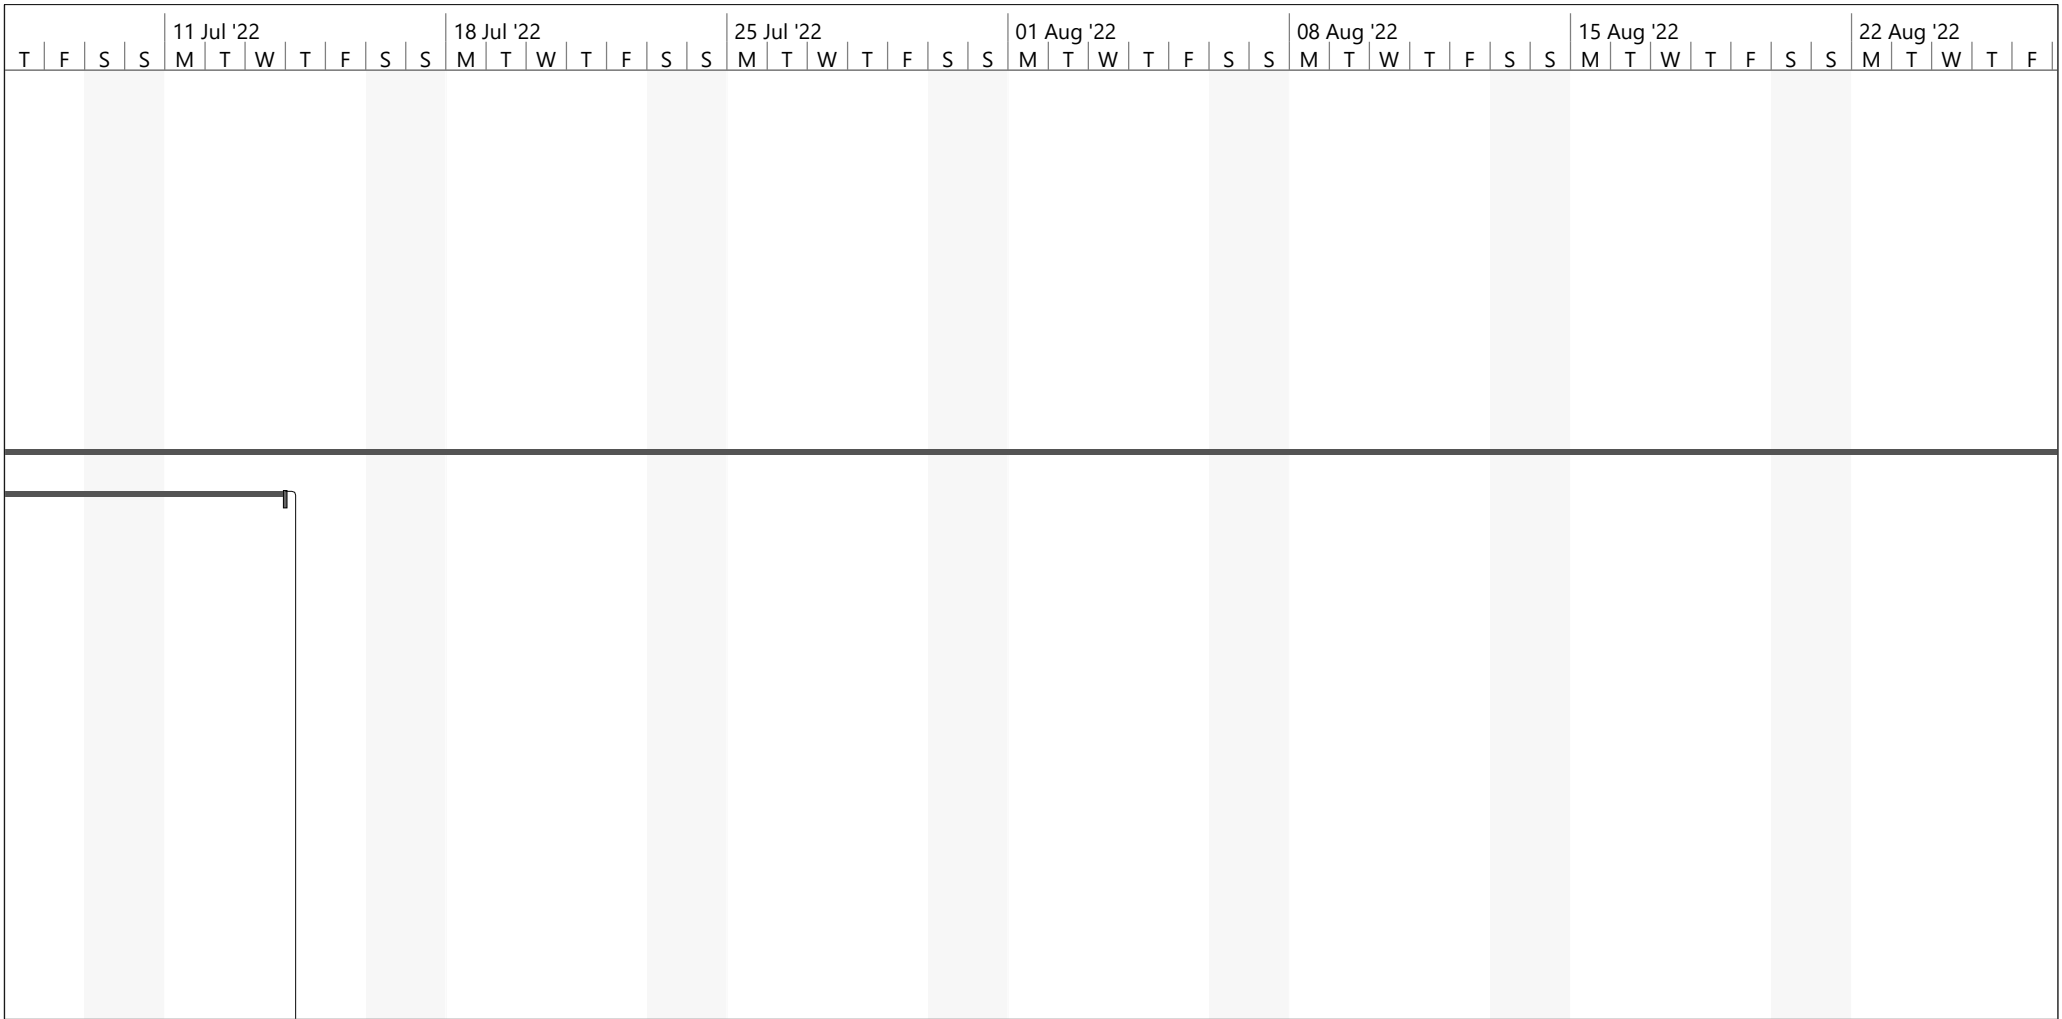

Project: IPL_Estimation_ips_Mol
Date: Fri 11.06.21

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

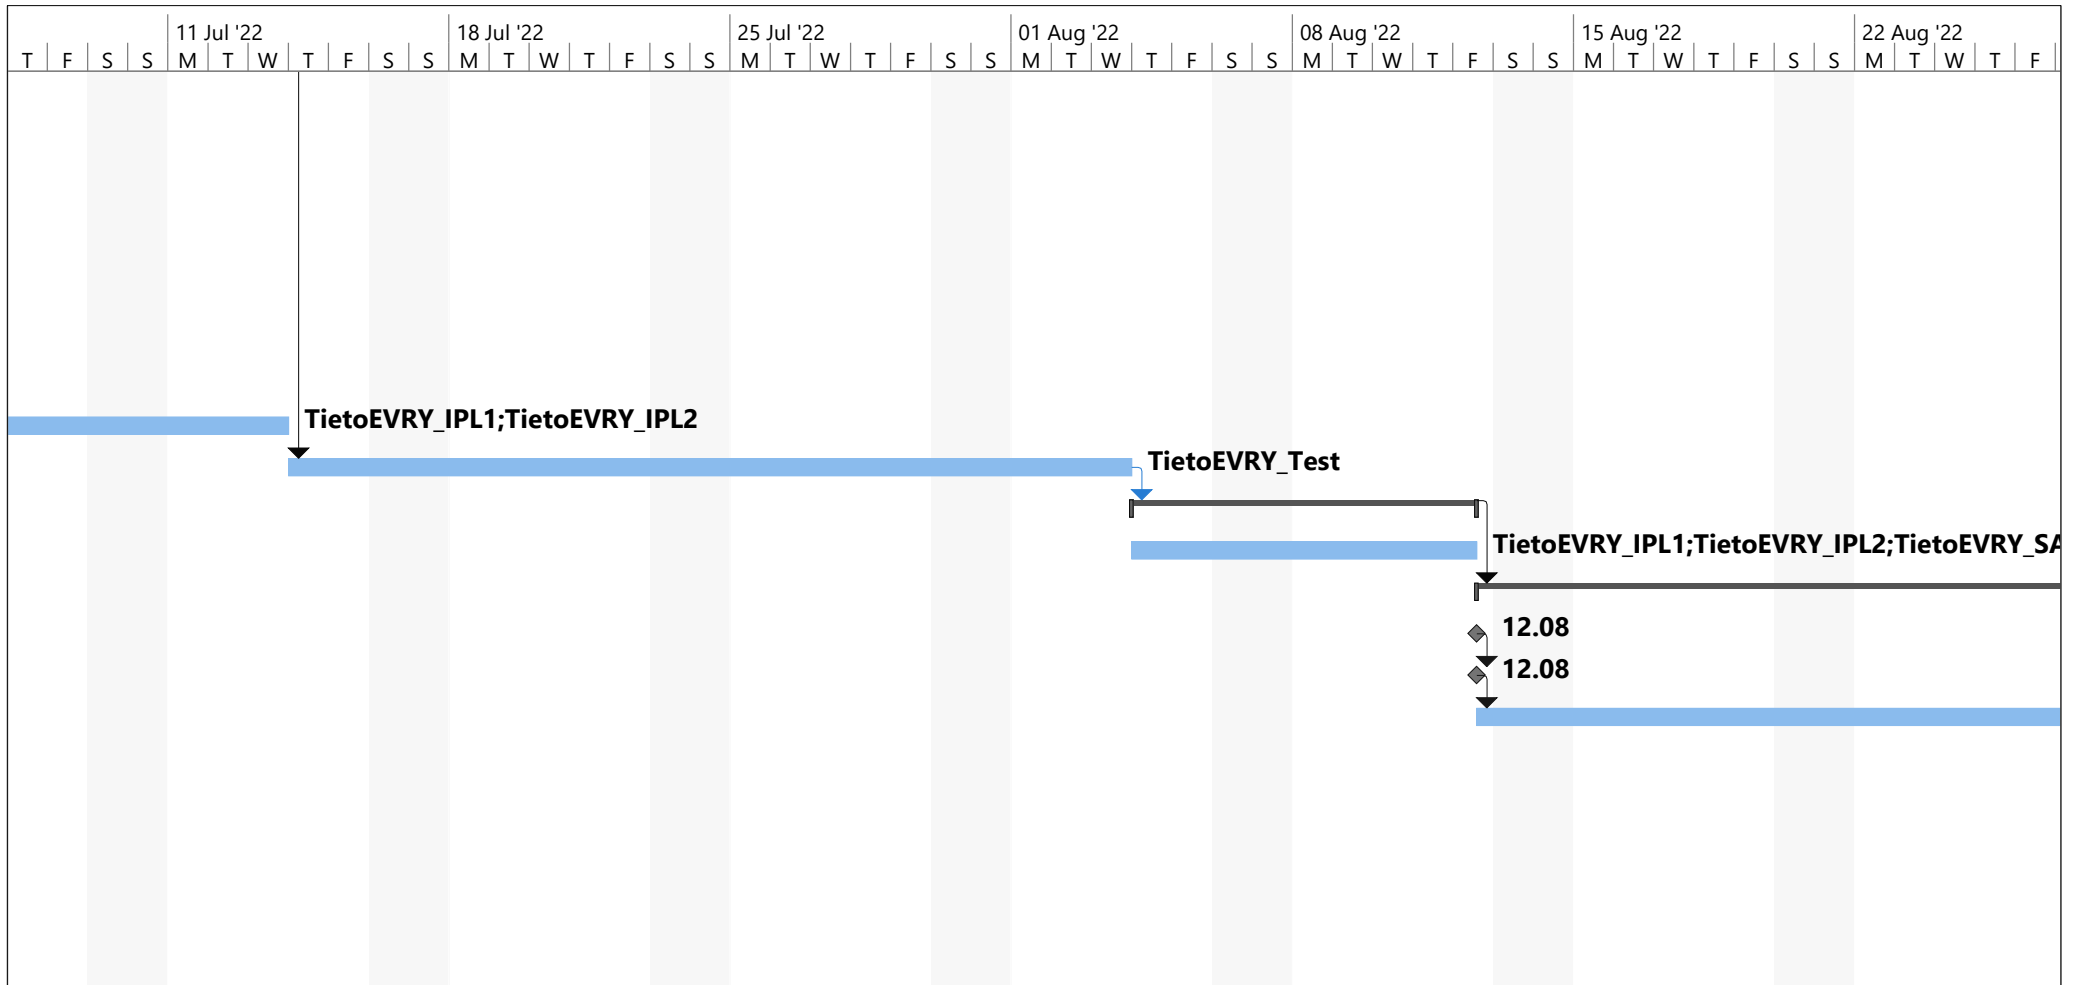


Project: IPL_Estimation_ips_Mol
Date: Fri 11.06.21

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




Project: IPL_Estimation_ips_Mol Date: Fri 11.06.21	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

S S | 29 Aug '22 | M T W T F S S | 05 Sep '22 | M T W T F S S | 12 Sep '22 | M T W T F S S | 19 Sep '22 | M T W T F S S | 26 Sep '22 | M T W T F S S | 03 Oct '22 | M T W T F S S | 10 Oct '22 | M T W T F S S

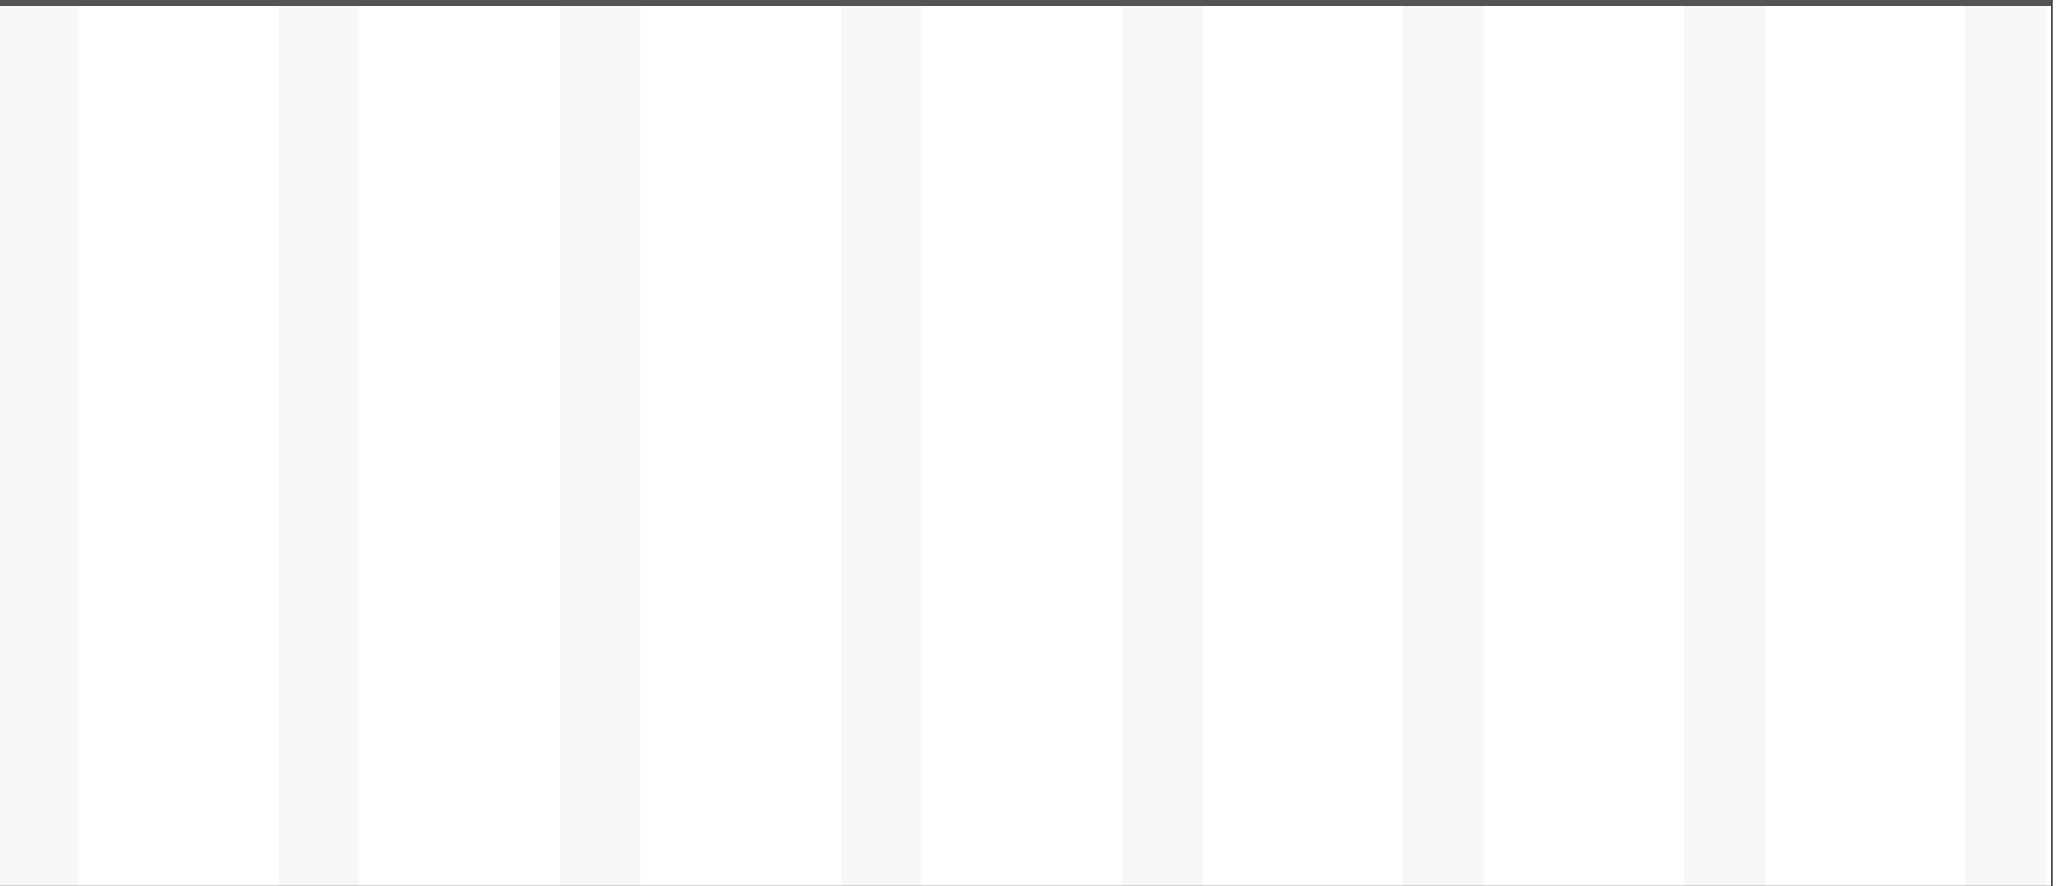


Project: IPL_Estimation_ips_Mol
Date: Fri 11.06.21

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

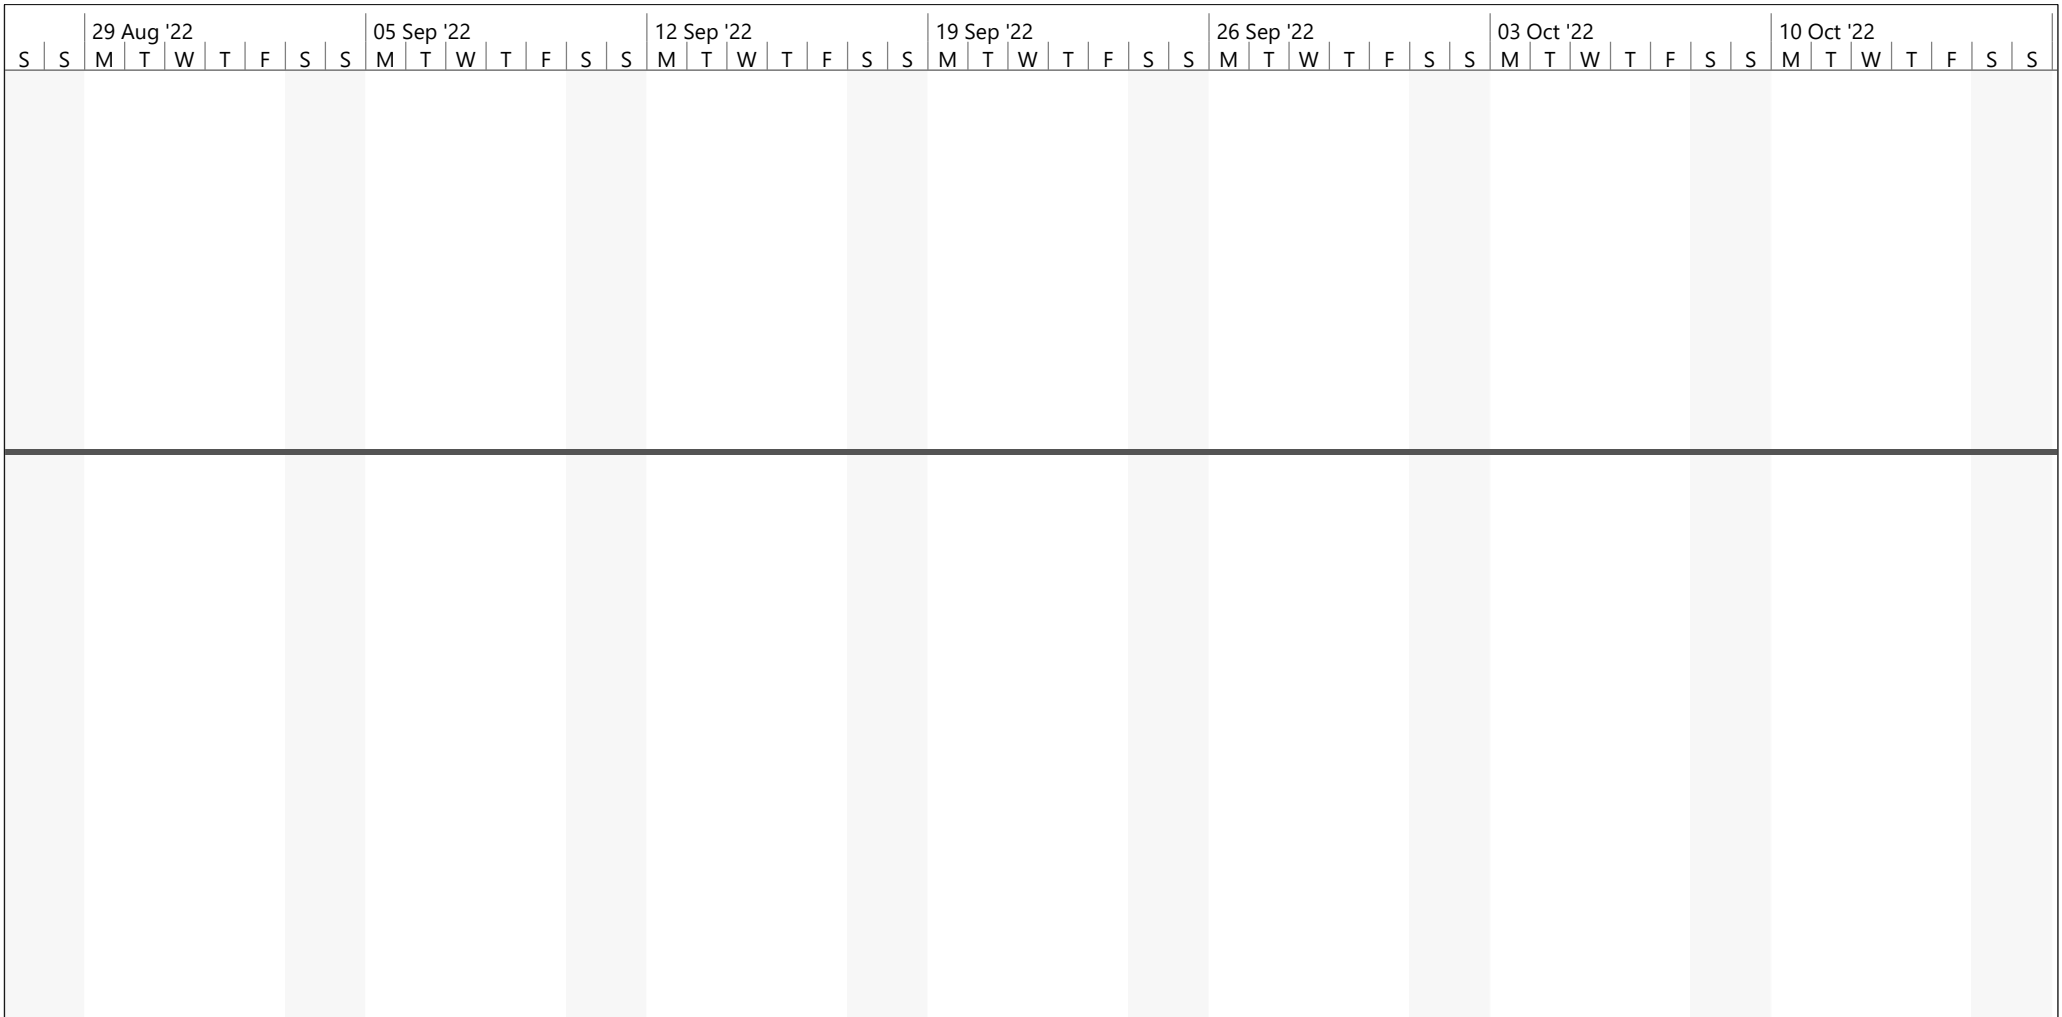


Project: IPL_Estimation_ips_Mol
Date: Fri 11.06.21

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			



SA

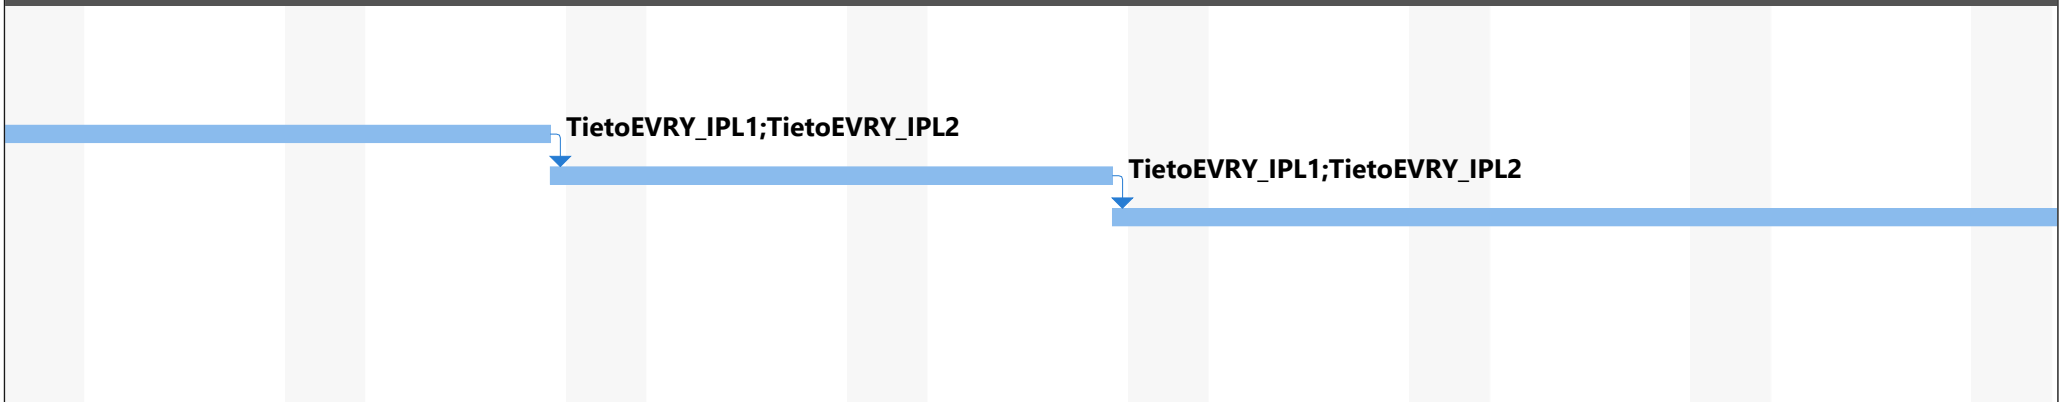


Project: IPL_Estimation_ips_Mol Date: Fri 11.06.21	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			




Project: IPL_Estimation_ips_Mol Date: Fri 11.06.21	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

17 Oct '22	24 Oct '22	31 Oct '22	07 Nov '22	14 Nov '22	21 Nov '22	28 Nov '22	05 Dec '22
M T W T F S S	M T W T F S S	M T W T F S S	M T W T F S S	M T W T F S S	M T W T F S S	M T W T F S S	M T

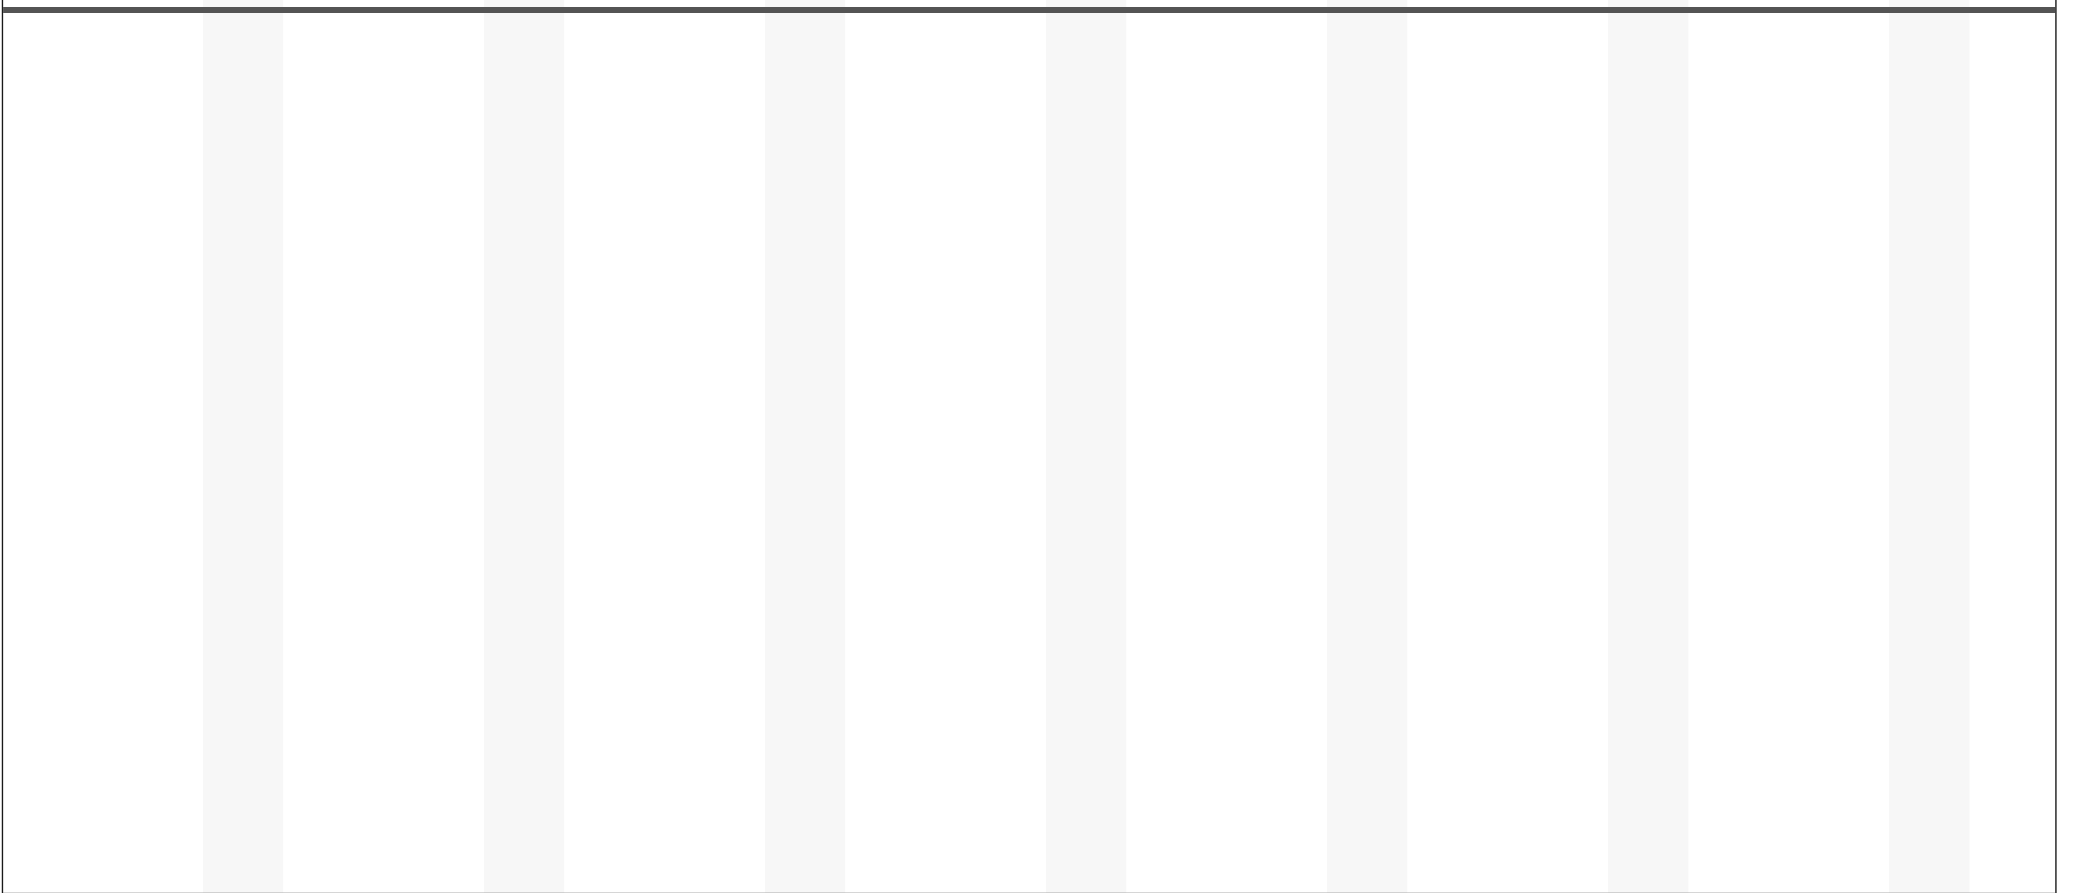

Project: IPL_Estimation_ips_Mol
Date: Fri 11.06.21


Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

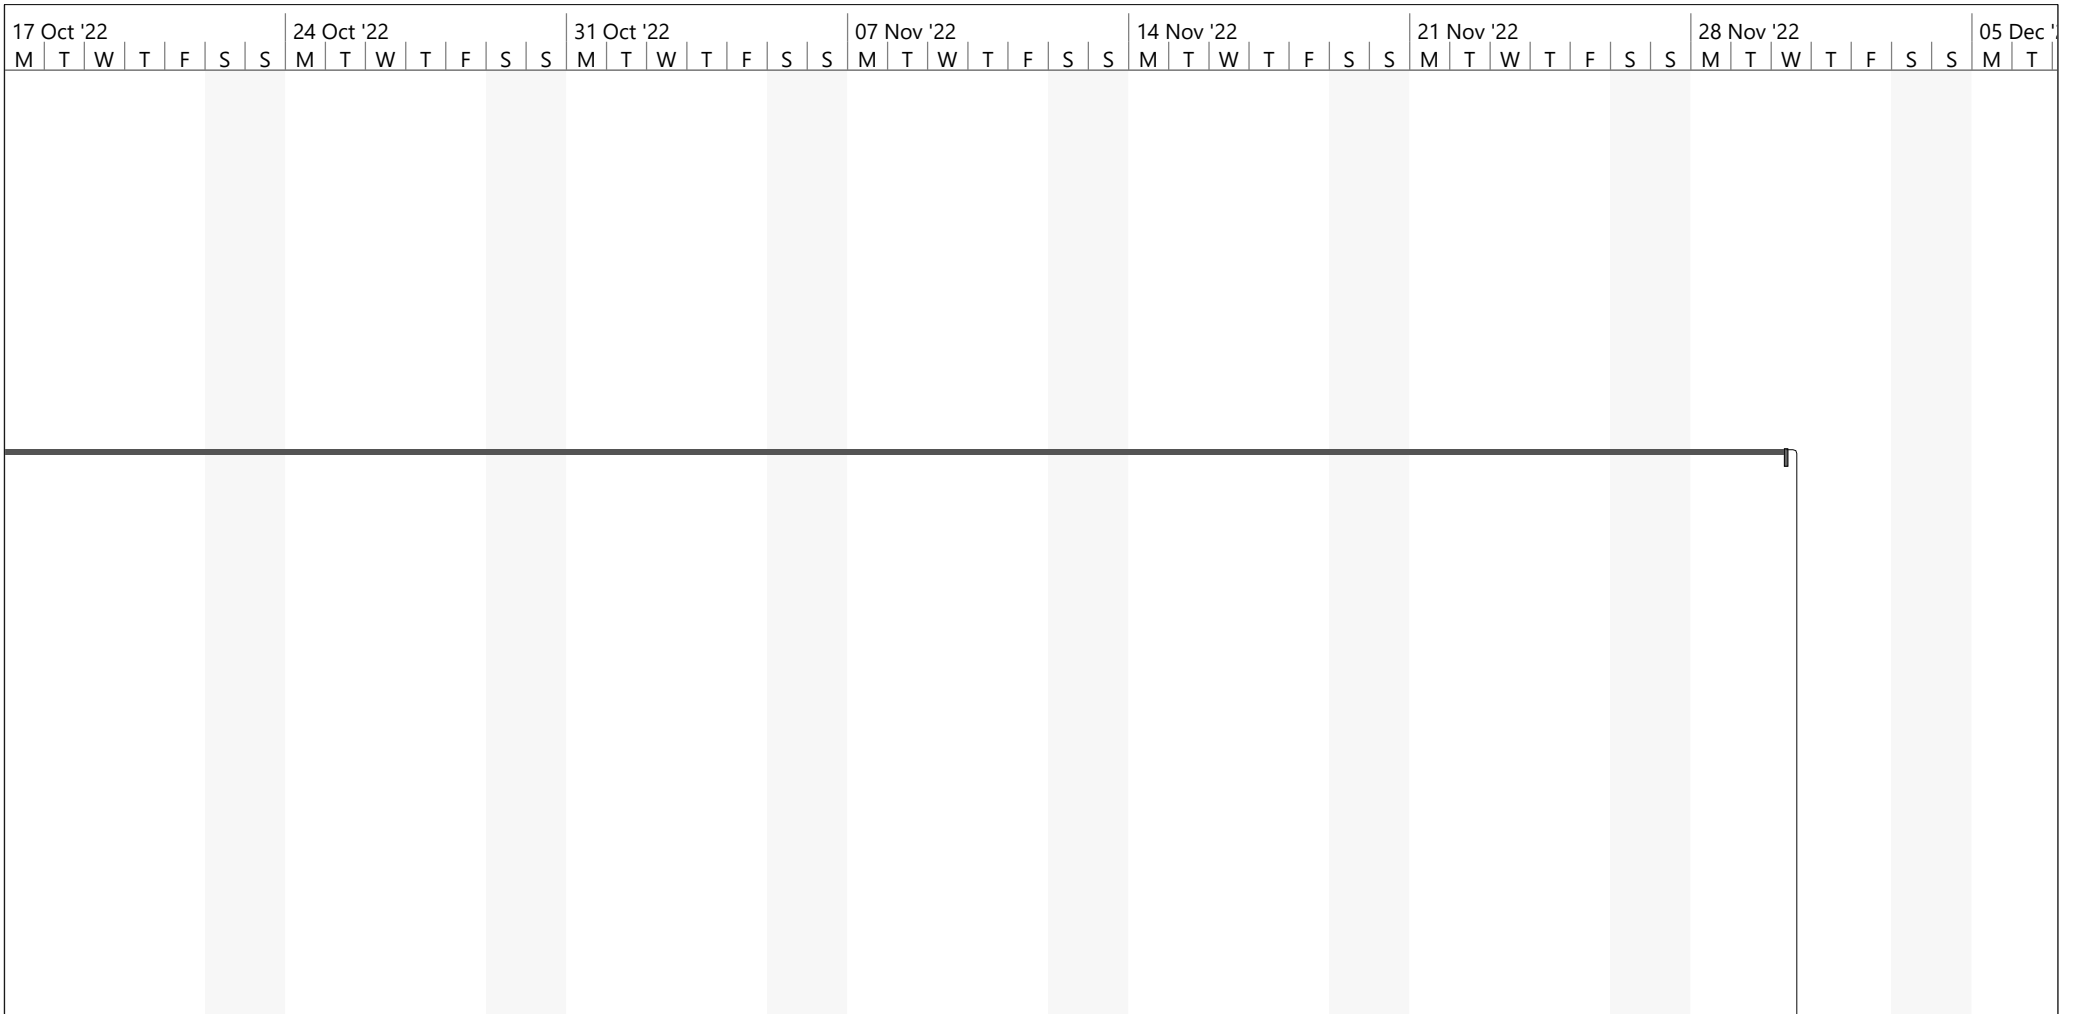

Project: IPL_Estimation_ips_Mol
Date: Fri 11.06.21


Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

17 Oct '22 24 Oct '22 31 Oct '22 07 Nov '22 14 Nov '22 21 Nov '22 28 Nov '22 05 Dec '22

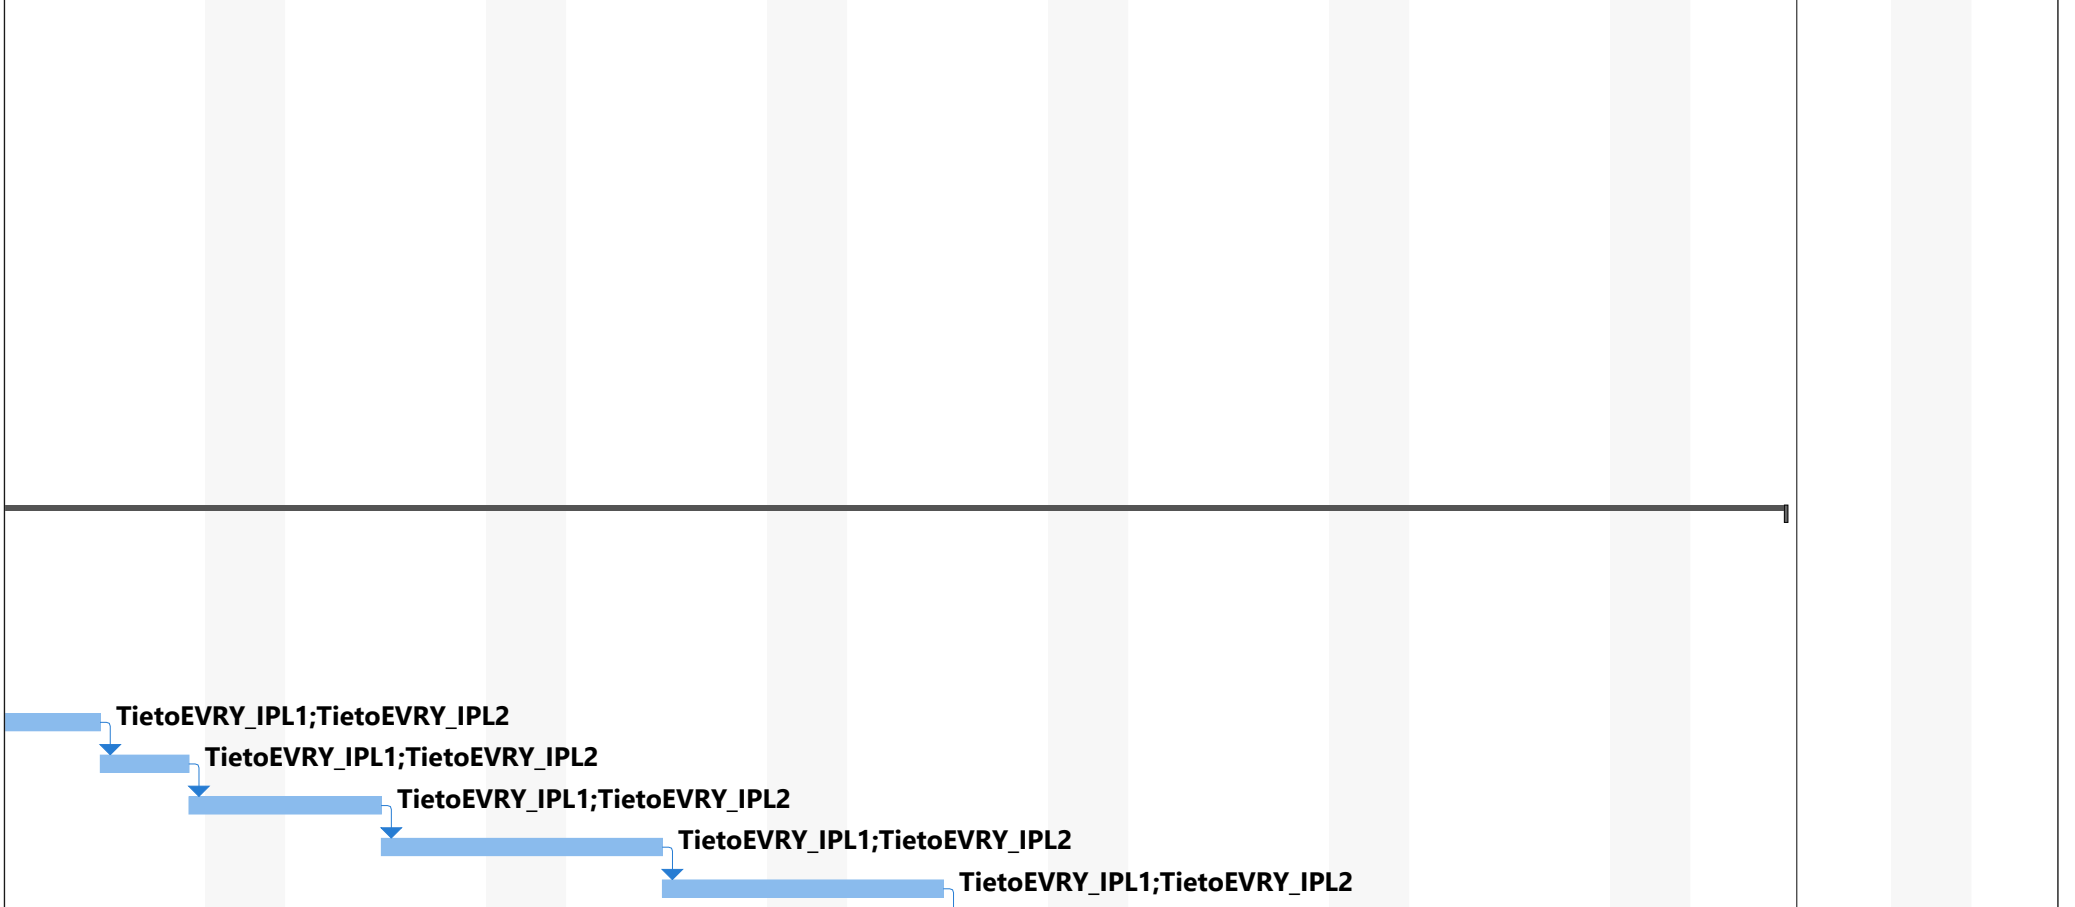


Project: IPL_Estimation_ips_Mol
Date: Fri 11.06.21

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

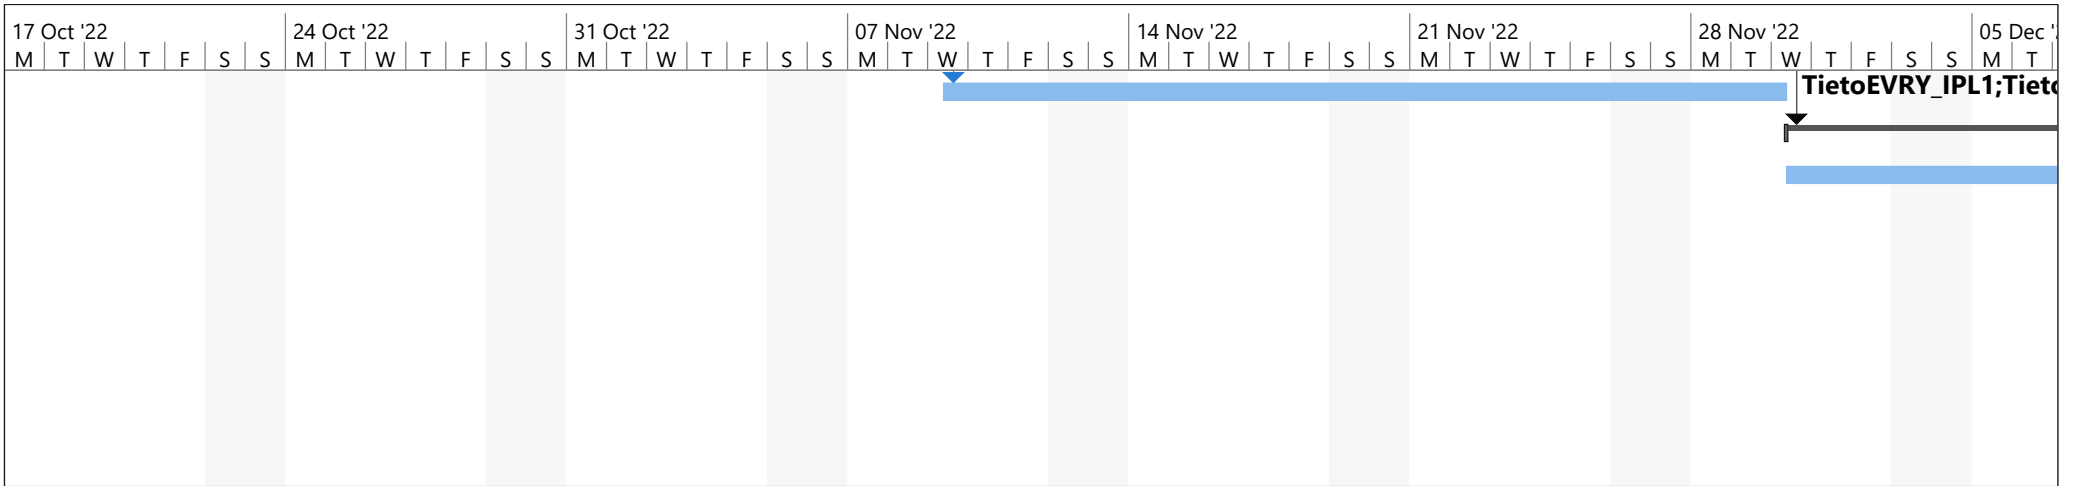


Project: IPL_Estimation_ips_Mol
Date: Fri 11.06.21

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

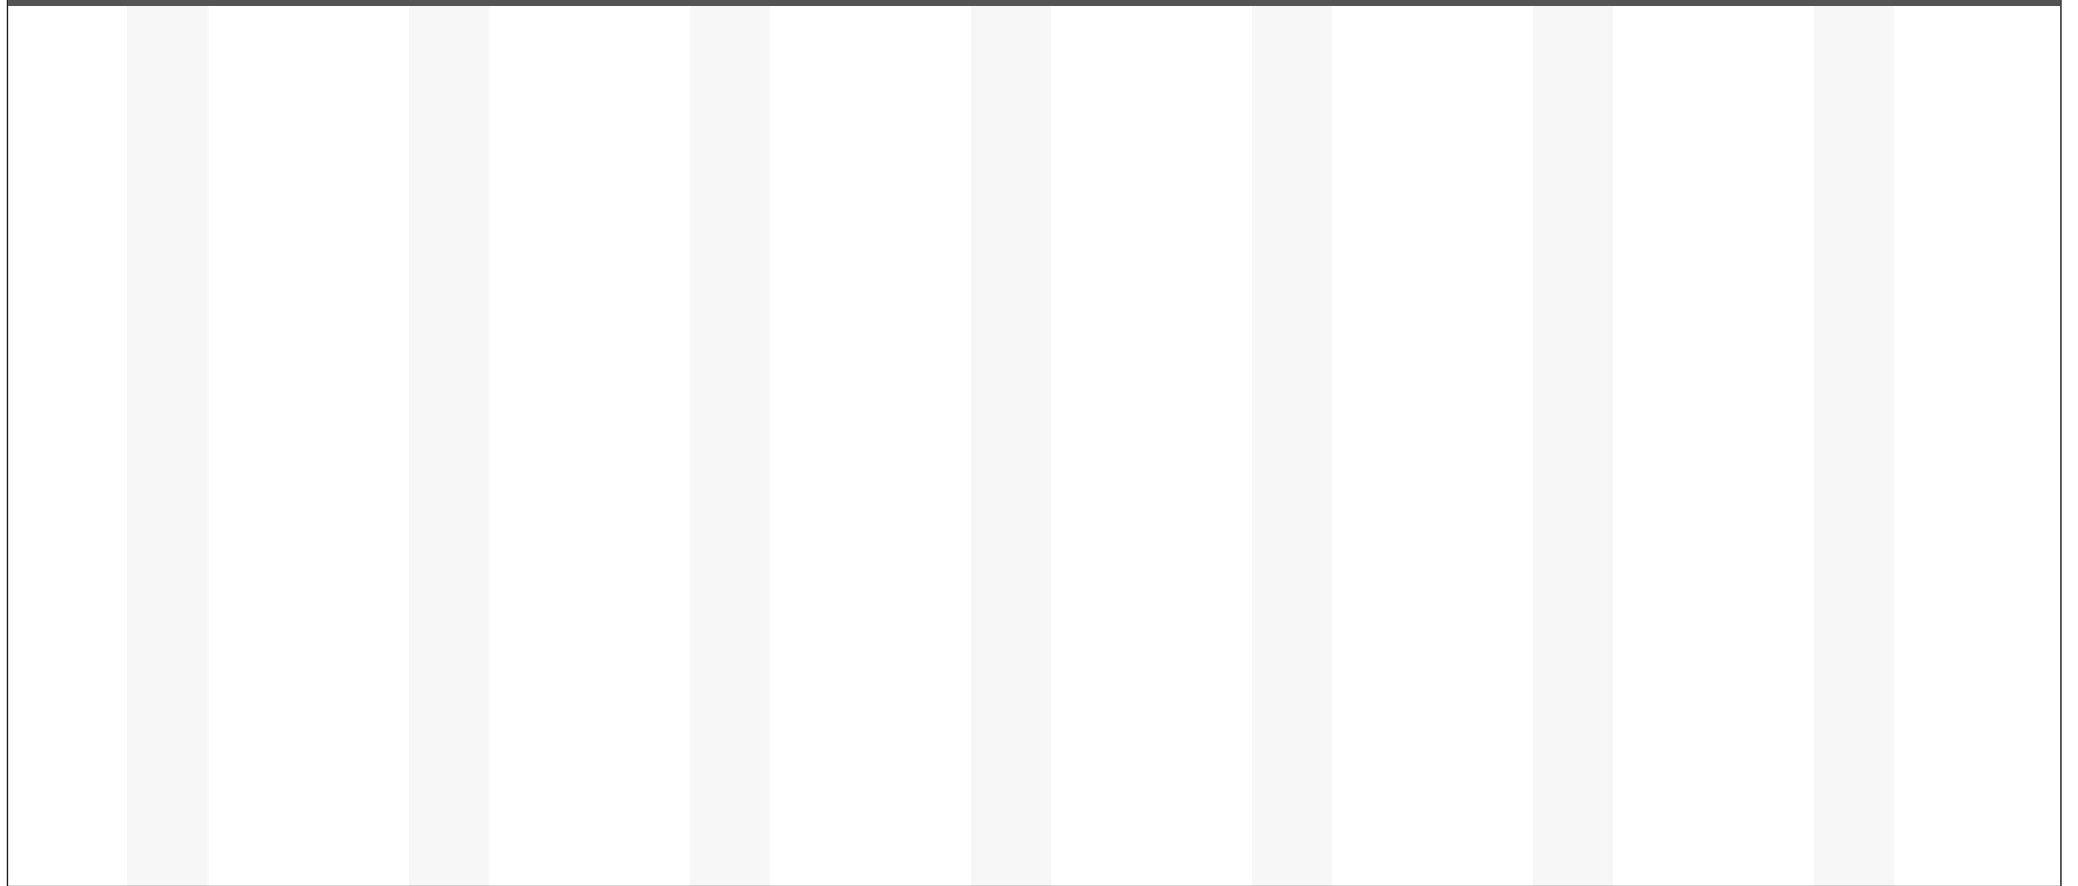


Project: IPL_Estimation_ips_Mol
Date: Fri 11.06.21

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

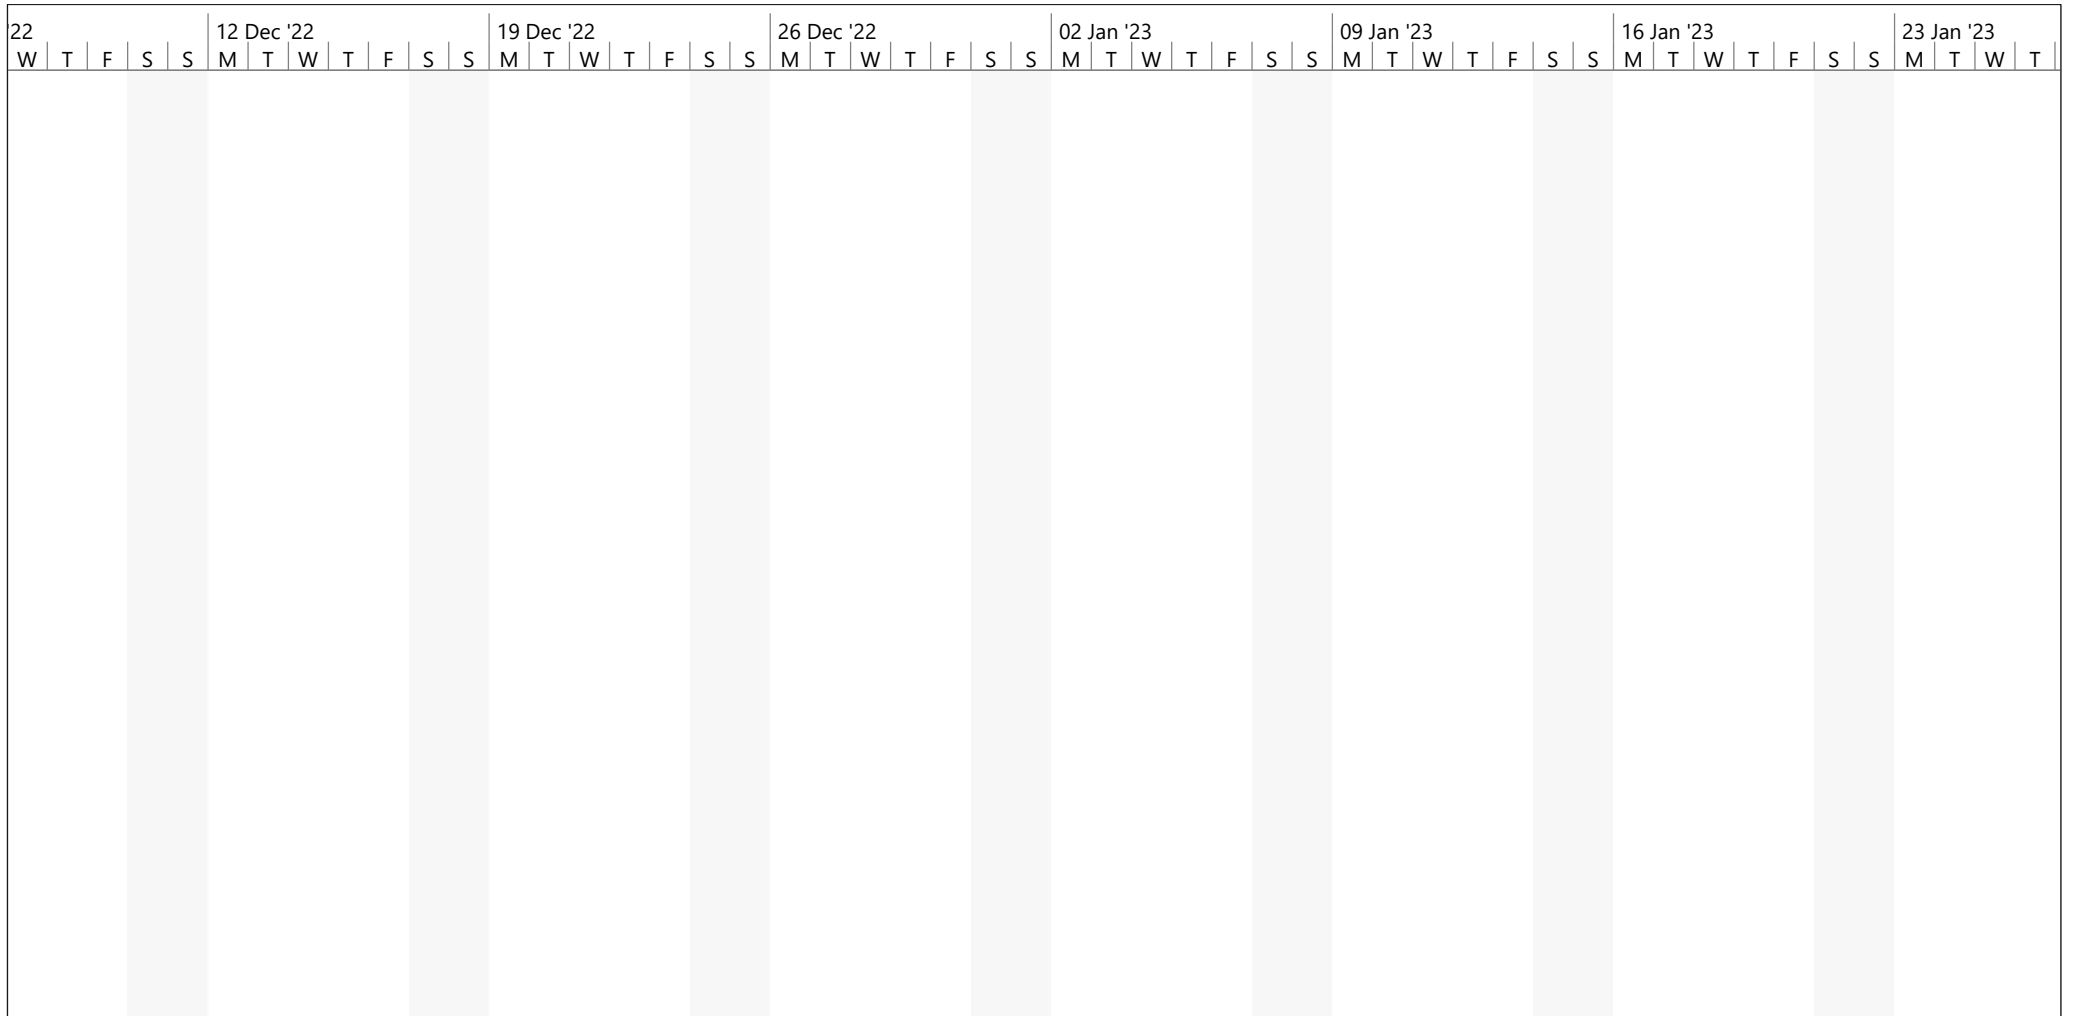


Project: IPL_Estimation_ips_Mol
Date: Fri 11.06.21

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

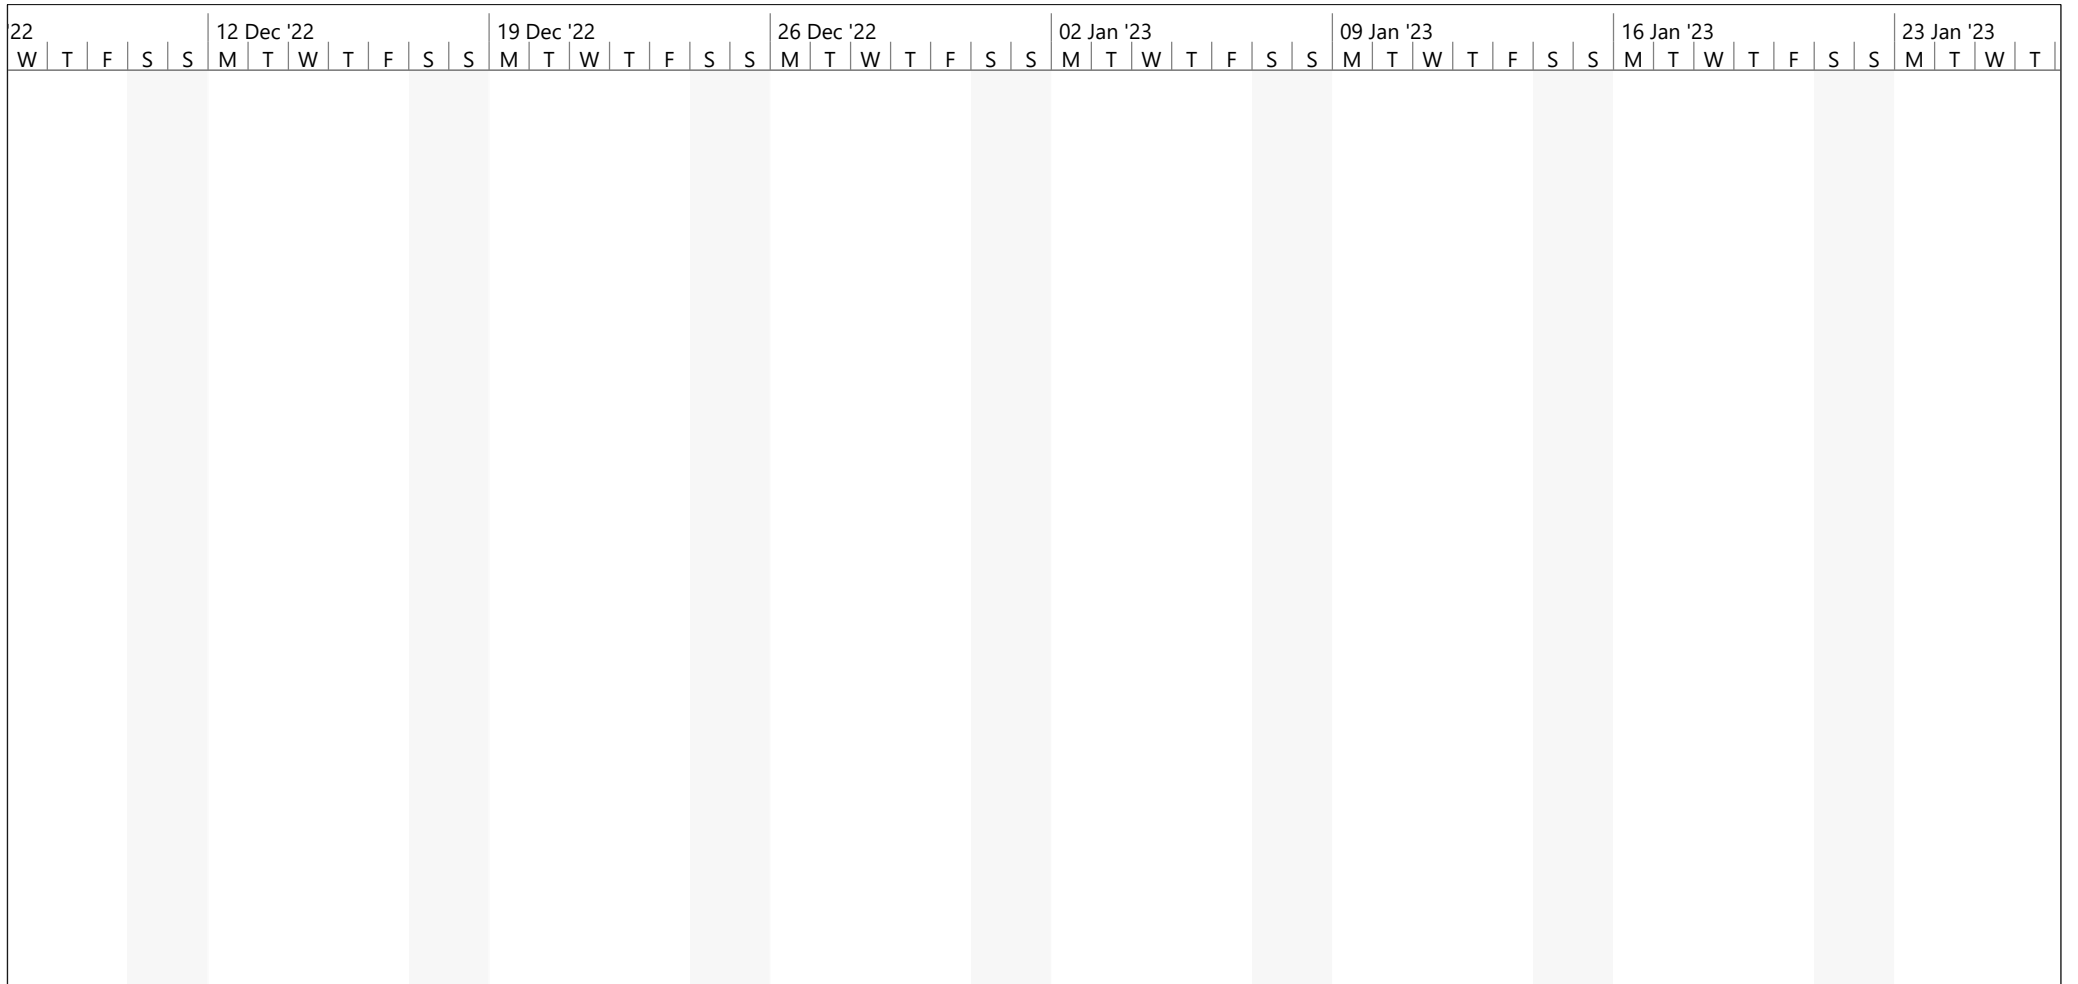


Project: IPL_Estimation_ips_Mol
Date: Fri 11.06.21

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

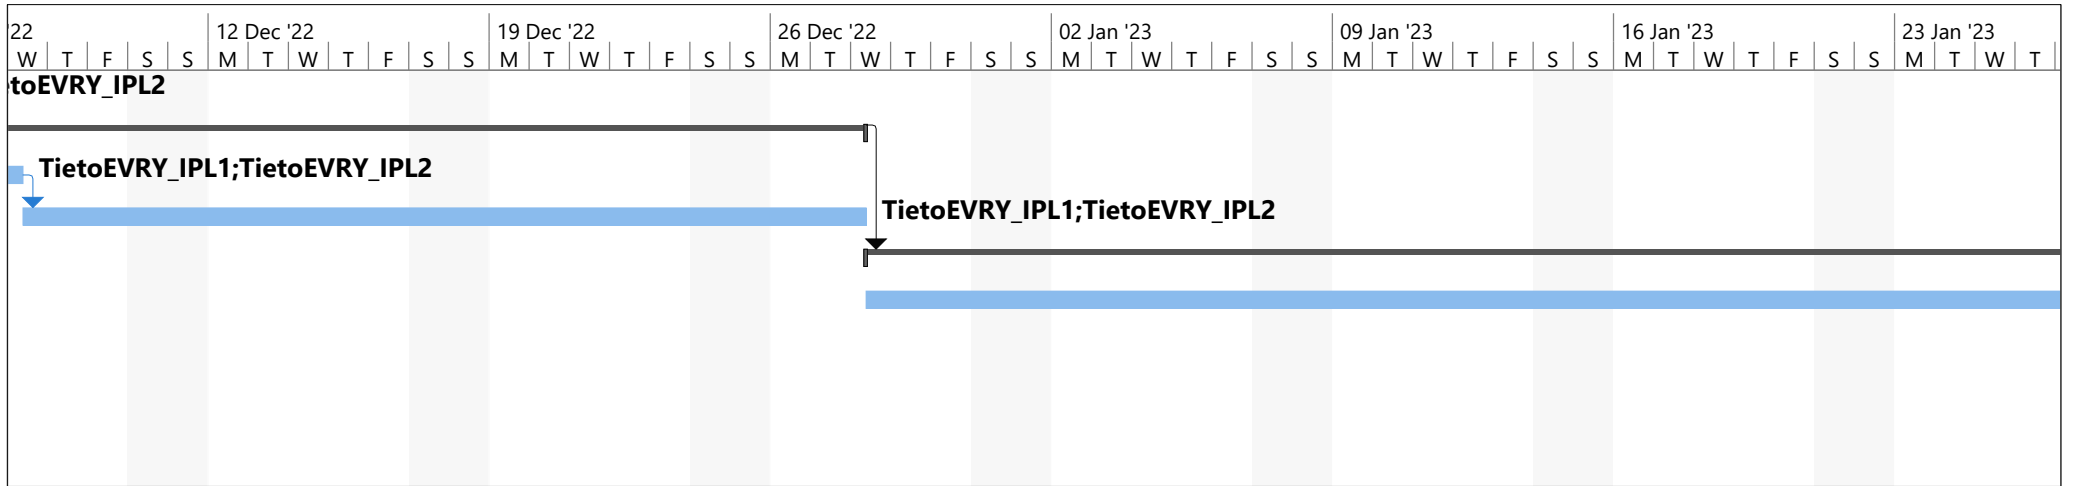


Project: IPL_Estimation_ips_Mol
Date: Fri 11.06.21

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

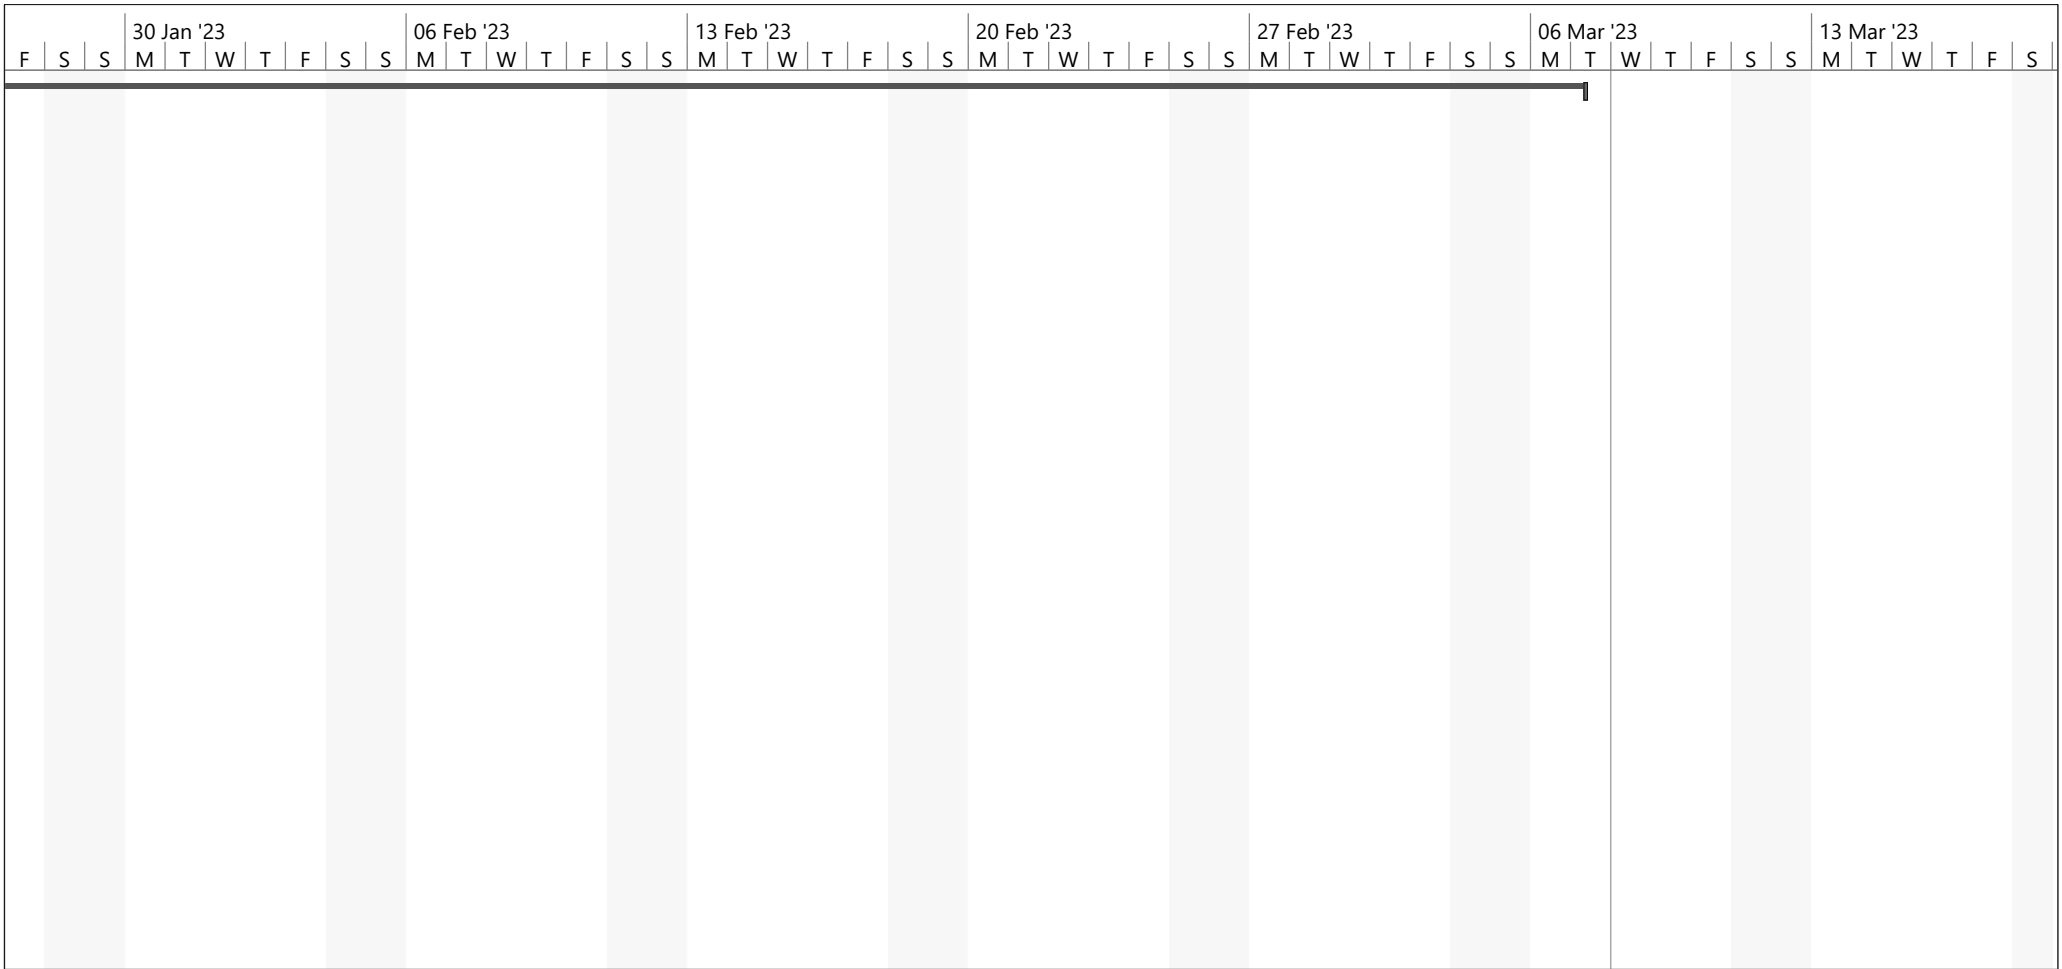


Project: IPL_Estimation_ips_Mol
Date: Fri 11.06.21

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

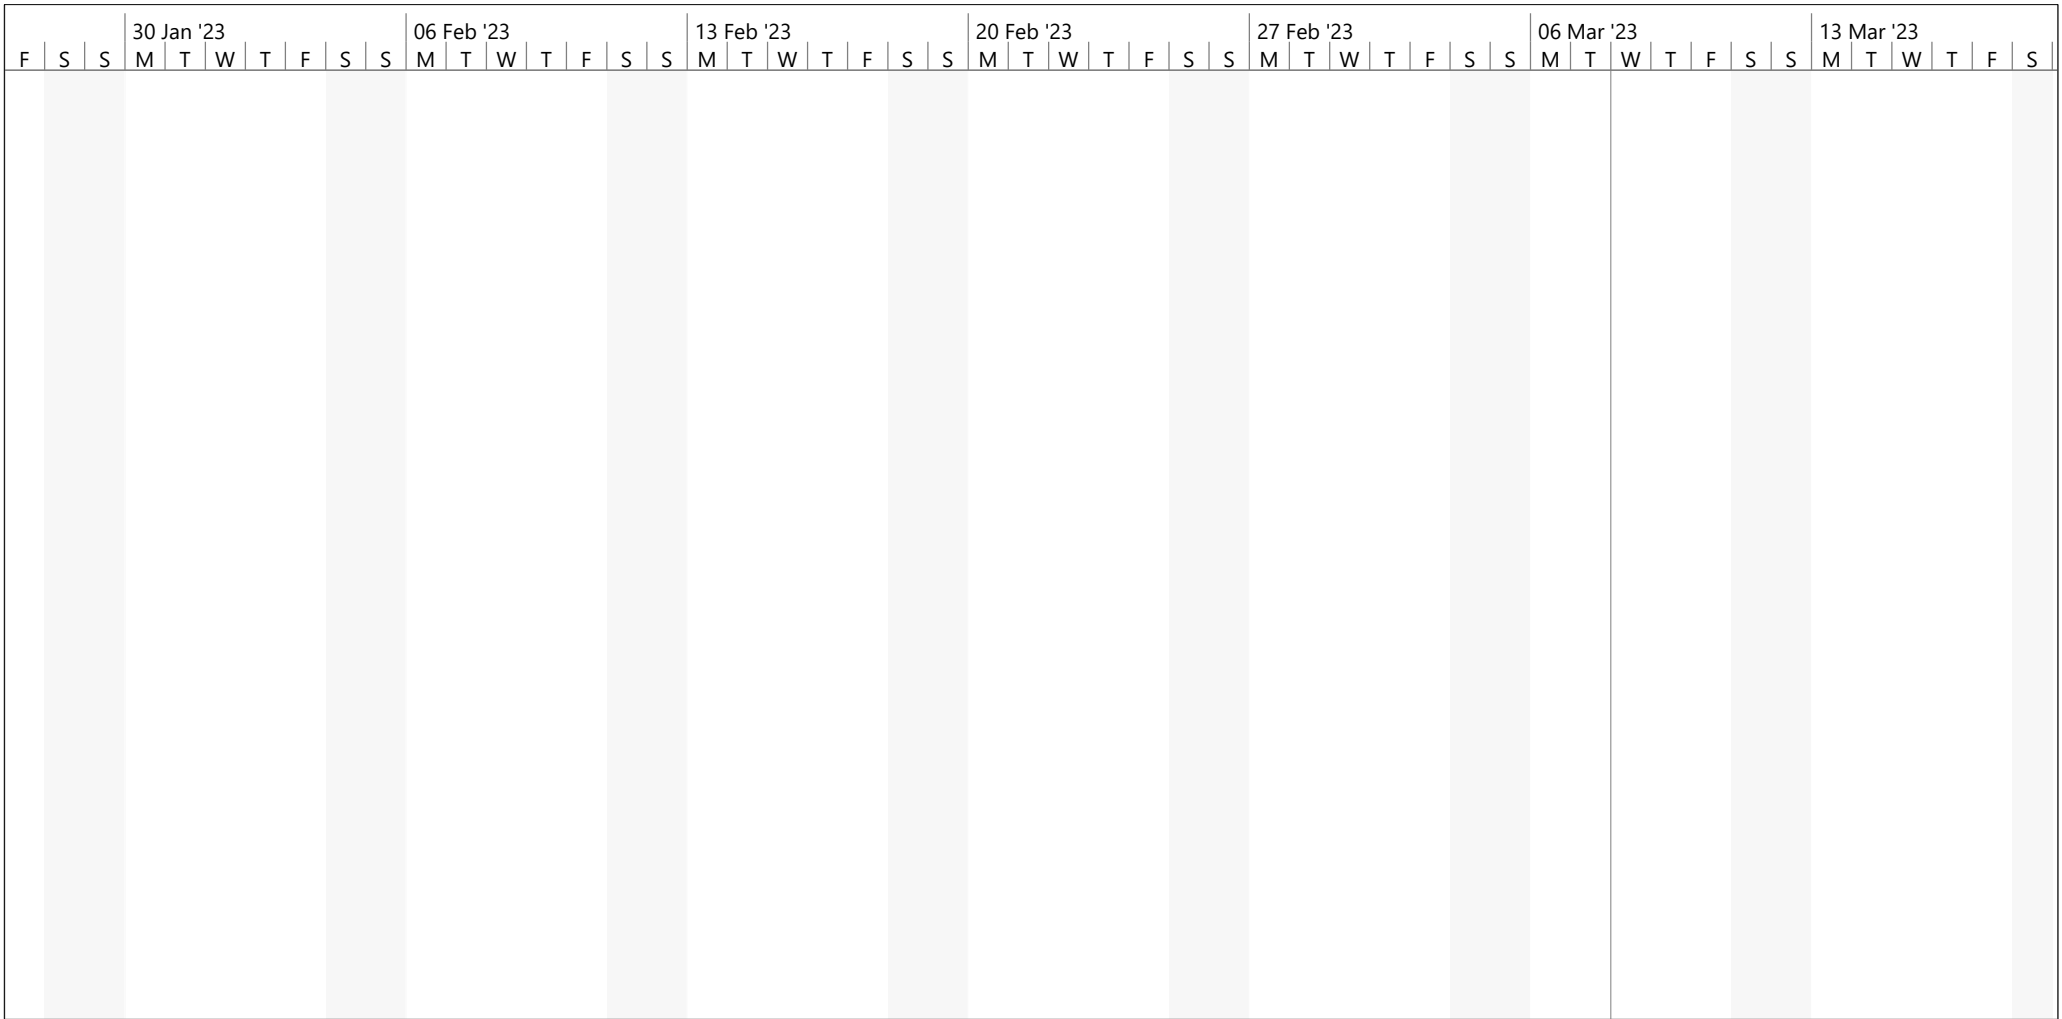


Project: IPL_Estimation_ips_Mol
Date: Fri 11.06.21

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

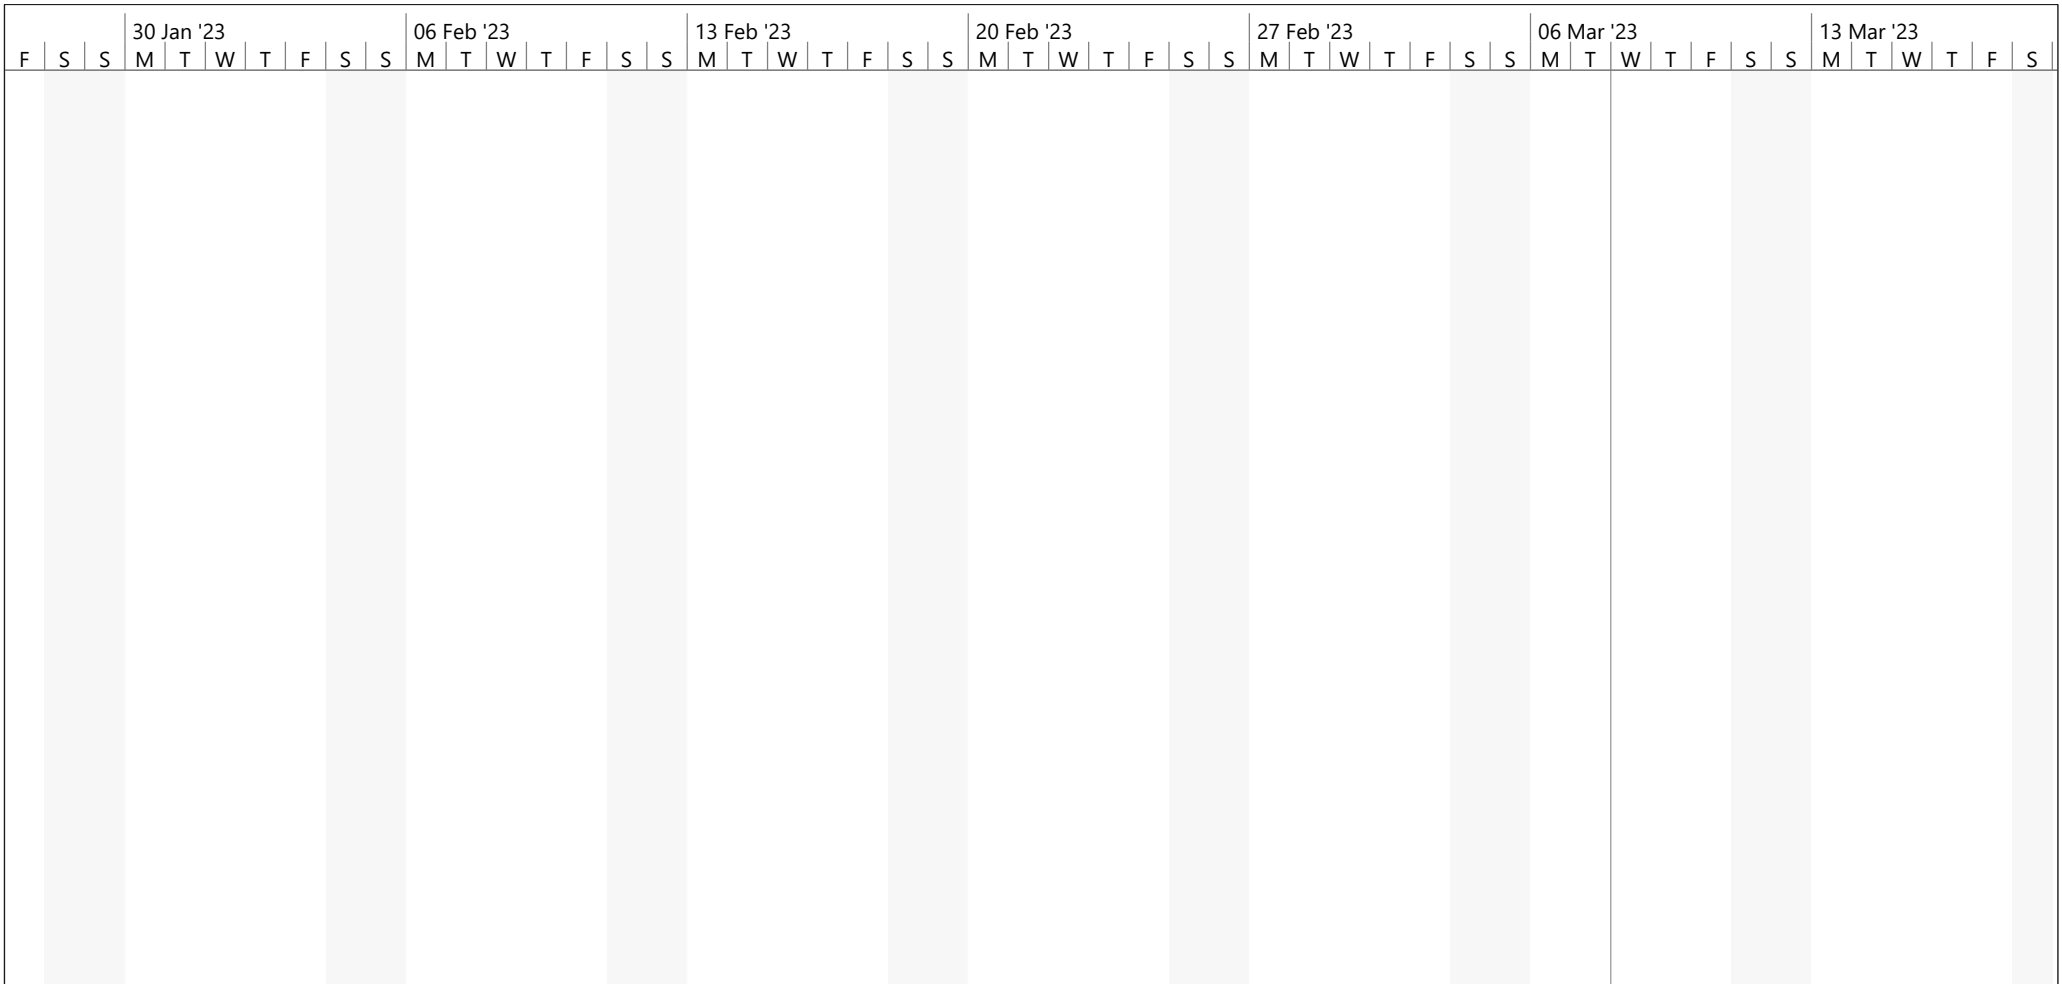

Project: IPL_Estimation_ips_Mol
Date: Fri 11.06.21

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

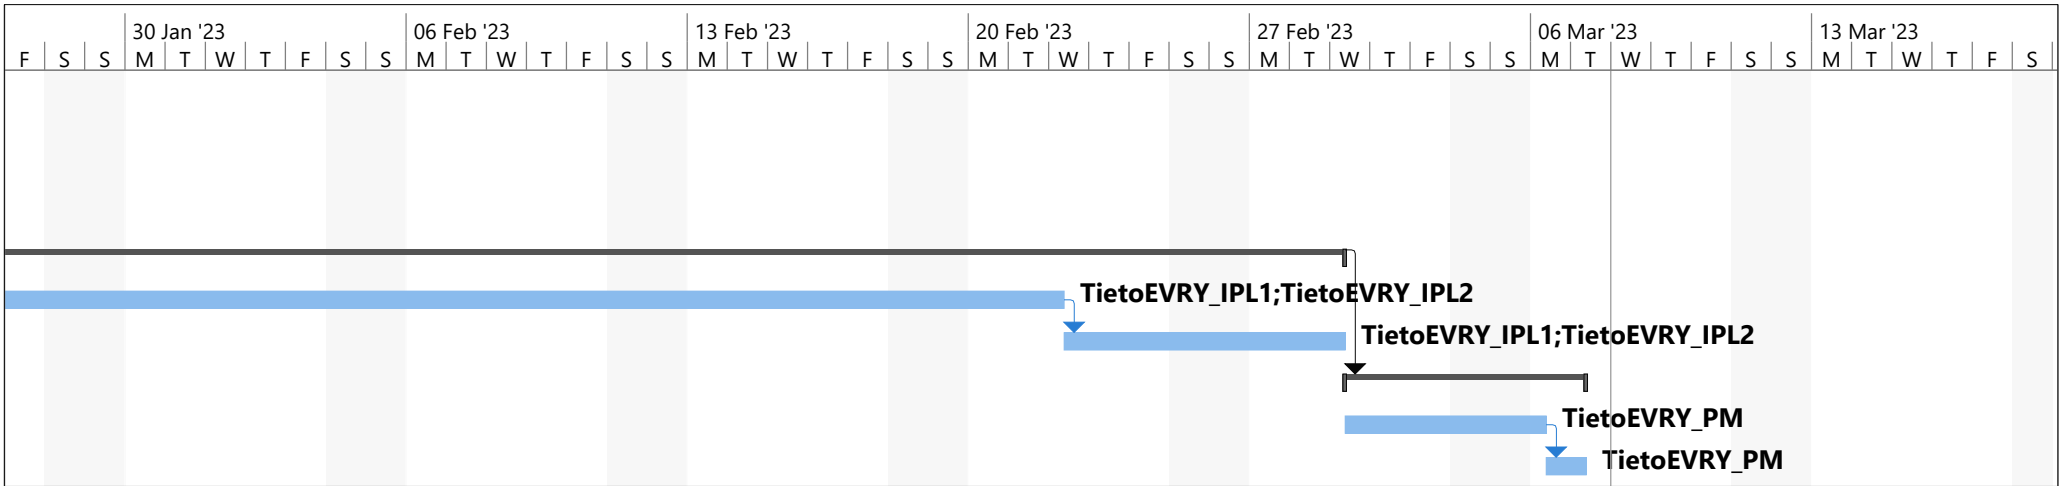

Project: IPL_Estimation_ips_Mol
Date: Fri 11.06.21

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			
