ID	Task Mode	Predece	Success	WBS	Task Name	Duration	Start	Finish	Resource Names	Valoare servicii (MLD) fara TVA
1					*****Decizie atribuire procedura*****	**0 days**	**Fri 24/07/26**	**Fri 24/07/26**		
2					**SERVICII DE CONSULTANȚĂ PRIVIND ELABORAREA PLANULUI DE REGIONALIZARE A SERVICIILOR SPITALICEȘTI DIN REPLUBLICA MOLDOVA 2030**	**137 days**	**Wed 05/08/26**	**Sat 19/12/26**		
3		8			START PROIECT: Emitere Ordin Administrativ de Incepere a Serviciilor de Consultanta	0 days	Wed 05/08/26	Wed 05/08/26		
4		9			FINALIZARE ETAPA 0 - INITIERE	0 days	Tue 01/09/26	Tue 01/09/26		
5		11			FINALIZARE ETAPA 1 - ANALIZA SITUAȚIEI EXISTENTE (AS-SI)	0 days	Tue 13/10/26	Tue 13/10/26		
6		13			FINALIZARE ETAPA 2 - MODELARE ȘI PROGNOZĂ	0 days	Mon 09/11/26	Mon 09/11/26		
7		15			FINALIZARE ETAPA 3 -SCENARII ȘI PLAN FINAL	0 days	Sat 19/12/26	Sat 19/12/26		
8			**11,9,3**		*****Ordin Administrativ de Incepere a Serviciilor de Consultanta*****	**0 days**	**Wed 05/08/26**	**Wed 05/08/26**	**Autoritata contractanta**	
9		**8**	**10,4**	**1**	**ETAPA 0 - INITIERE**	**28 days**	**Wed 05/08/26**	**Tue 01/09/26**	**Exp cheie,Exp non-cheie**	**632.000,00**
10		9		2	Livrabilul 1 - Raport inițial	0 days	Tue 01/09/26	Tue 01/09/26	Ech. Backstopping,Exp cheie,Exp non-cheie	
11		**8**	**12,13SS days,5**	**3**	**ETAPA 1 - Analiza situatiei existente (AS-SI)**	**70 days**	**Wed 05/08/26**	**Tue 13/10/26**	**Ech. Backstopping,Exp cheie,Exp non-cheie**	**3.160.000,00**
12		11		4	Livrabilul 2 – Raport de analiză (AS-IS):	0 days	Tue 13/10/26	Tue 13/10/26	Ech. Backstopping,Exp cheie,Exp non-cheie	
13		**11SS+7 days**	**14,15SS days,6**	**5**	**ETAPA 2 - Modelare si prognoză**	**90 days**	**Wed 12/08/26**	**Mon 09/11/26**	**Ech. Backstopping,Exp cheie,Exp non-cheie**	**948.000,00**
14		13		6	Livrabilul 3 - Model de progrnoză	0 days	Mon 09/11/26	Mon 09/11/26	Ech. Backstopping,Exp cheie,Exp non-cheie	
15		**13SS+4 days**	**16SS+5 days,1**	**7**	**ETAPA 3 - Scenarii și plan final**	**85 days**	**Sat 26/09/26**	**Sat 19/12/26**	**Ech. Backstopping,Exp cheie,Exp non-cheie**	
16		15SS+5 days		8	Livrabilul 4 – Raport privind scenariile	0 days	Sat 14/11/26	Sat 14/11/26	Ech. Backstopping,Exp cheie,Exp non-cheie	632.000,00
17		15SS+7 days		9	Livrabilul 5 – Proiect Plan de regionalizare	0 days	Thu 10/12/26	Thu 10/12/26	Ech. Backstopping,Exp cheie,Exp non-cheie	758.400,00
18		15SS+8 days		10	Livrabilul 6 – Plan final și plan de implementare	0 days	Sat 19/12/26	Sat 19/12/26	Ech. Backstopping,Exp cheie,Exp non-cheie	189.600,00
19					**TOTAL VALOARE SERVICII**					**6.320.00,00**

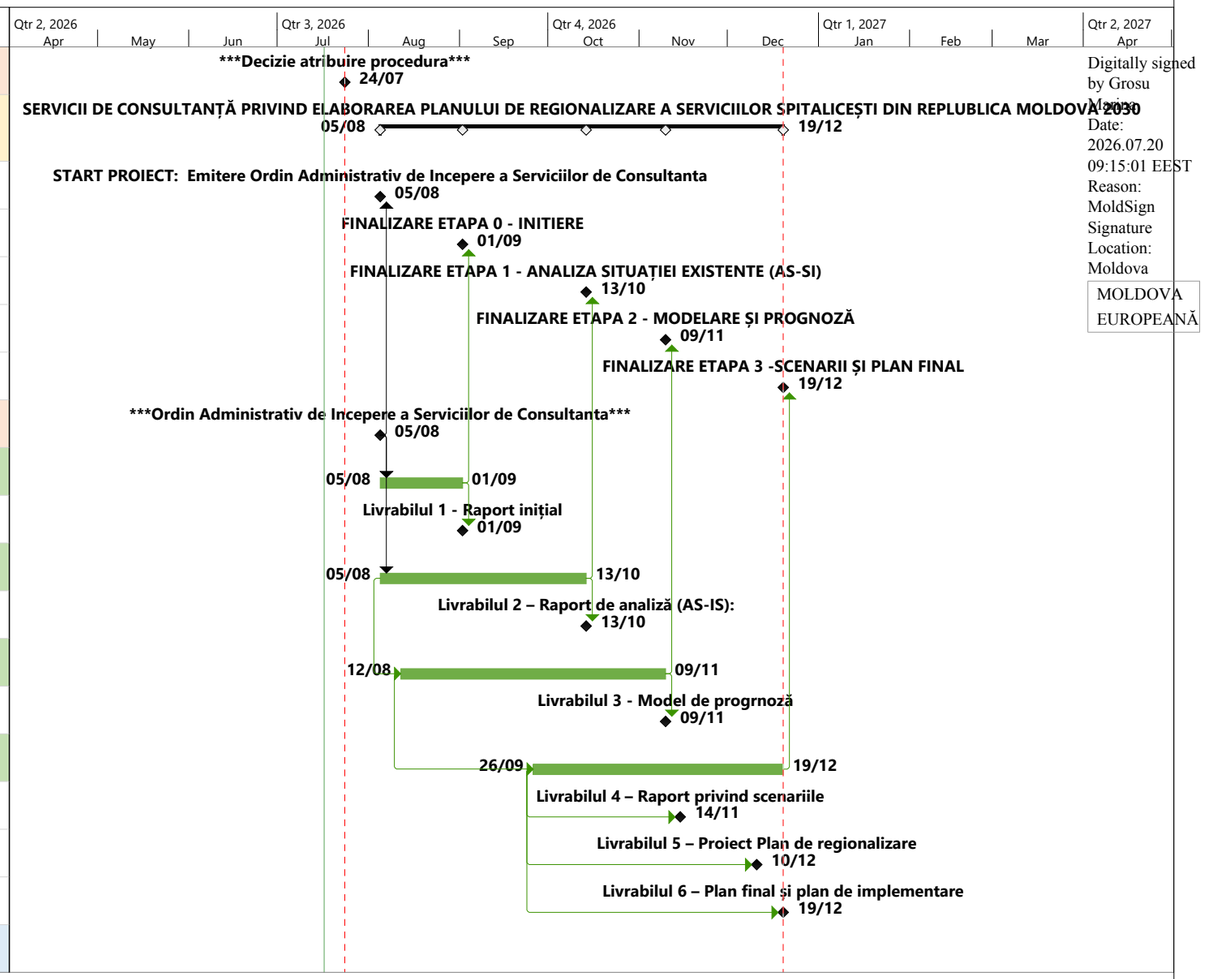

Digitally signed by Grosu Marina
Date: 2026.07.20 09:15:01 EEST
Reason: MoldSign Signature
Location: Moldova

MOLDOVA EUROPEANĂ

Task | Split | Milestone | Summary | Project Summary | Inactive Task | Inactive Milestone | Inactive Summary | Manual Task | Duration-only | Manual Summary Rollup | Manual Summary | Start-only | Finish-only | External Tasks | External Milestone | Deadline | Progress | Manual Progress
