Formularul F3.3

GRAFIC DE REALIZAREA A SERVICIILOR SI A LUCRARILOR - 24 LUNI

"Lucrari de constructie a Centrului Integrat de Pregatire pentru Aplicarea Legii al MAI"

ID	Task Name	Duration
1	**Lucrari de constructie a Centrului Integrat de Pregatire pentru Aplicarea Legii al MAI**	**731 days?**
2	Semnarea contractului+ordin de incepere	0 days
3	Lucrari de mobilizare	10 days
4	**Obiectiv 1**	**140 days**
5	Lucrari de demolare a cladirilor existente si pregatirea terenului	140 days
6	**Obiectiv 2**	**395 days**
7	Masuri contra deformatiilor de teren	395 days
8	**Obiectiv 3**	**380 days**
9	Complex sportiv acoperit (nr.10-PG)	380 days
10	**Obiectiv 4**	**65 days**
11	Complex sportiv exterior (nr.8-PG)	65 days
12	**Obiectiv 5**	**365 days**
13	Poligon tactic cu tir subteran (nr. 11-PG)	365 days
14	**Obiectiv 6**	**27 days**
15	Tir pentru trageri descoperit (nr. 30-PG)	27 days
16	**Obiectiv 7**	**45 days**
17	Retele electrice exterioare (in interiorul santierului de constructie)	45 days
18	**Obiectiv 8**	**110 days**
19	Complex logistic, garaje, statiile de deservire tehnica (nr.7-PG)	110 days
20	**Obiectiv 9**	**30 days**
21	Retele de comunicatii exterioare (in interiorul santierului de constru	30 days
22	**Obiectiv 10**	**40 days**
23	Centrala termica nr. 2 (nr. 26-PG)	40 days
24	**Obiectiv 11**	**25 days**
25	Retea termica RT2	25 days
26	**Obiectiv 12**	**20 days**
27	Statia de purificare a apelor pluviale (nr. 24a, nr. 24b-PG)	20 days
28	**Obiectiv 13**	**14 days**
29	Statia de pompare a apelor uzate nr. 1 (nr. 28-PG)	14 days
30	**Obiectiv 14**	**90 days**
31	Canalizarea pluviale (in interiorul santierului de constructie)	90 days
32	**Obiectiv 15**	**30 days**
33	Retele de gaze exterioare (in interiorul santierului de constructie)	30 days
34	**Obiectiv 16**	**30 days**
35	Amenajarea terenului	30 days
36	Probe si teste	20 days
37	Receptie la terminarea lucrarilor	15 days?

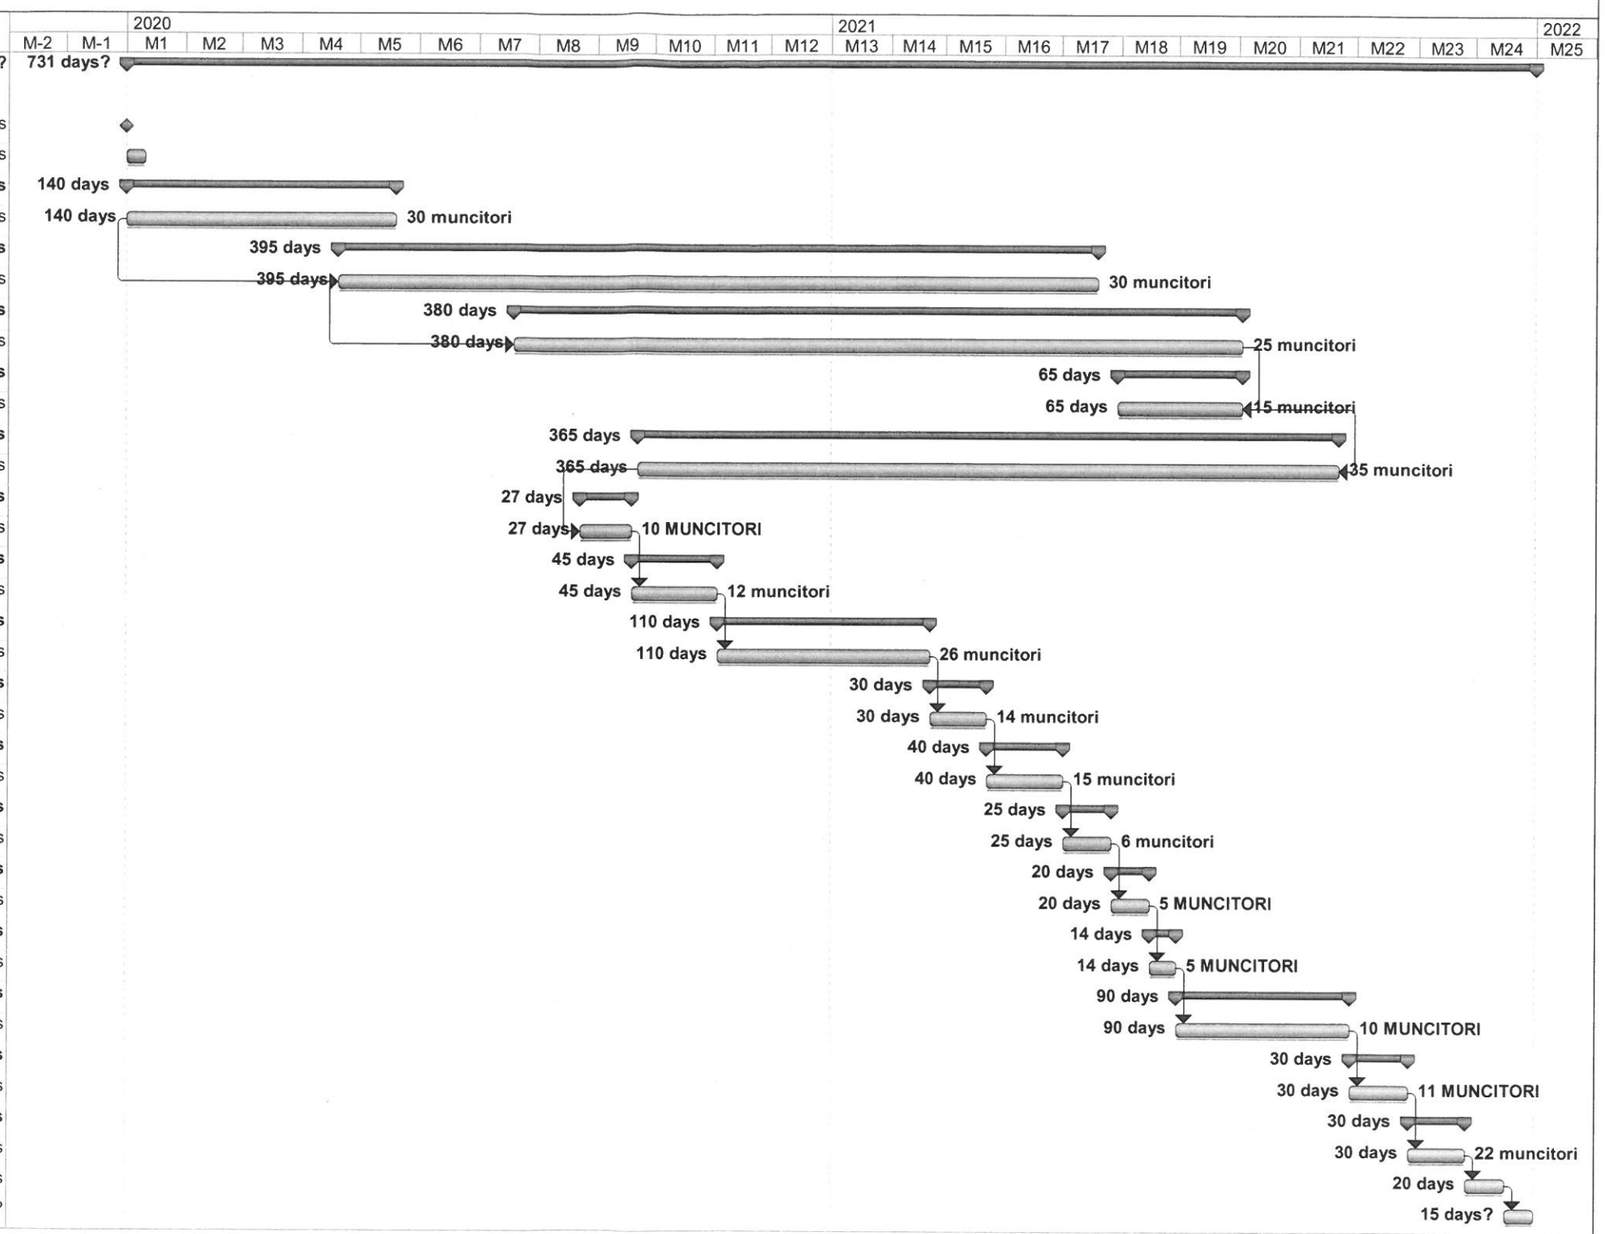

OFERTANT,

Digitally signed by Malaciuc Liuba
Date: 2019.10.31 21:03:07 EET
Reason: MoldSign Signature
Location: Moldova

Task | Milestone | Rolled Up Critical Task | Split | Group By Summary
Progress | Summary | Rolled Up Milestone | External Tasks | Deadline
Rolled Up Task | Rolled Up Progress | Project Summary
