

VOLUME 1


SECTION 4

FORM 4.6.3

WORK PLAN AND PROGRAMME


4.6.3.1 State the proposed location of your main office on the site, stations (steel/concrete/asphalt structures), warehouses, laboratories, accommodation, etc. (sketches to be attached as required).

WE PROPOSE THE FOLLOWING APPROXIMATION OF OBJECTS LOCATION:

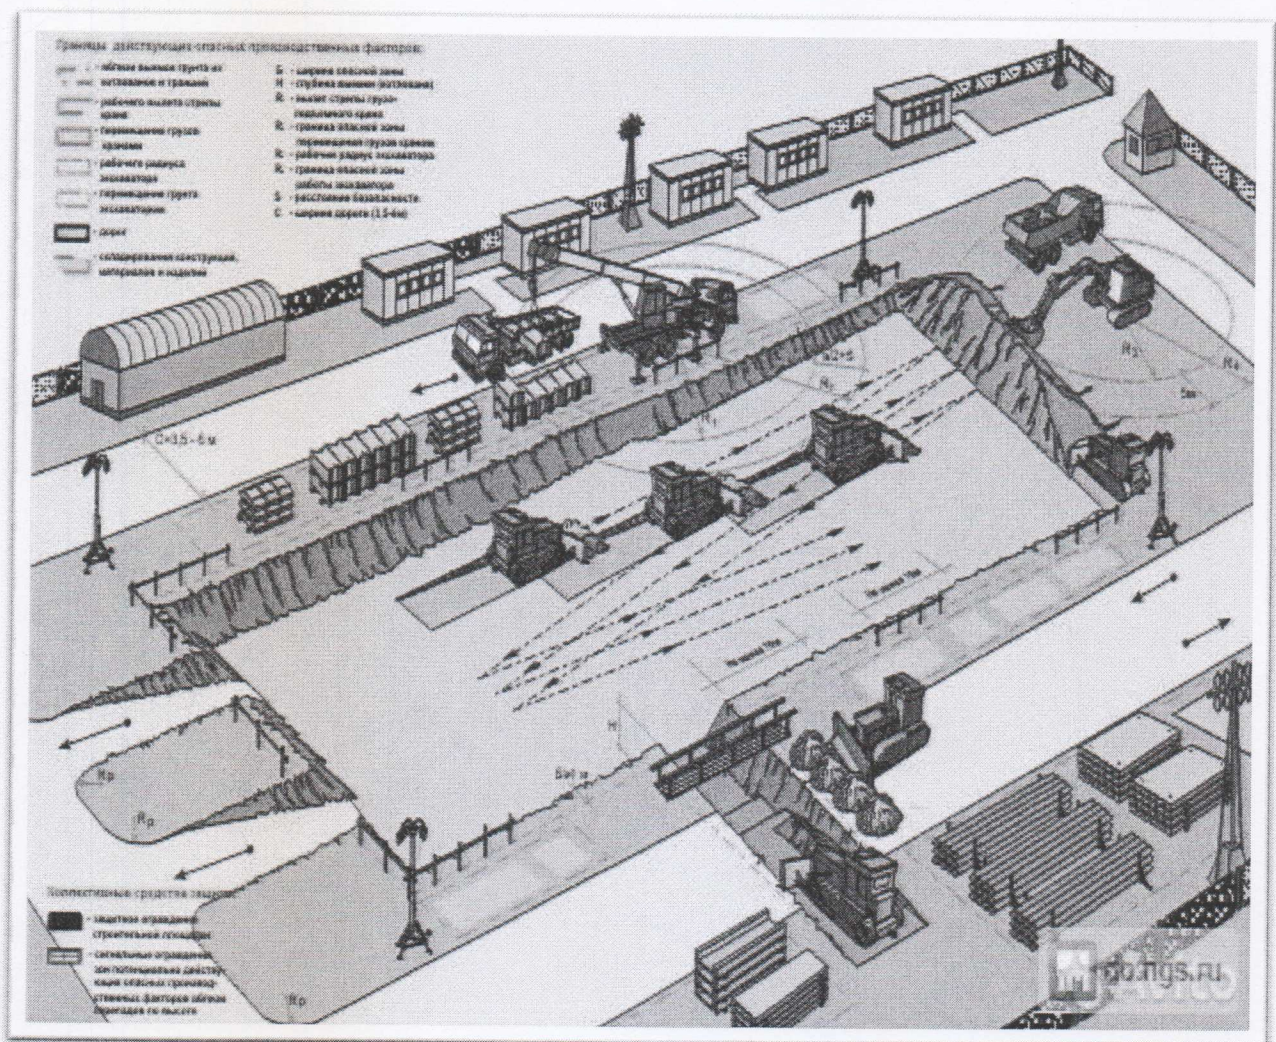


4.6.3.2 Give a brief outline of your programme for completing the works in accordance with the required method of construction and stated time of completion.


SCHEDULE OF EXECUTION OF WORKS:




Contractor Name: General Police Inspectorate, 11/1, Tiraspol street, Chisinau, MD2069 Contract: THOR/4.3/1 – Activity 7.2				Reconstruction of Police Stations											
REF	TRADE	START DATE	FINISH DATE	TIME PERIOD											
				M1	M2	M3	M4	M5	M6	M7	M8	M9	M10	M11	M12
1	SITE PREPARATION	2020	2021												
2	DEMOLITION	2020	2021												
3	CONCRETE WORKS	2020	2021												
4	PROTECTION WORKS	2020	2021												
5	LIGHT STEEL FRAMING	2020	2021												
6	TIMBER CONSTRUCTION	2020	2021												
7	BLOCK CONSTRUCTION	2020	2021												
8	ROOFING	2020	2021												
9	DOORS AND WINDOWS	2020	2021												
10	CLADDING AND LININGS	2020	2021												
11	SUSPENDED CEILINGS	2020	2021												
12	PLASTERING	2020	2021												
13	JOINERY AND FIXTURES	2020	2021												
14	WATER/GAS SERVICES	2020	2021												
15	FINISHES	2020	2021												
16	PAINTING	2020	2021												
17	PLUMBING AND DRAINAGE	2020	2021												
18	ELECTRICAL INSTALLATIONS	2020	2021												
19	MECHANICAL INSTALLATIONS	2020	2021												
20	EXTERNAL WORKS	2020	2021												
21	LANDSCAPING	2020	2021												
22	FINAL CLEAN	2020	2021												
23	RECEPTION OF OBJECTS	2020	2021												




4.6.3.3 Attach a critical milestone bar chart (schedule of execution) representing the construction programme and detailing relevant activities, dates, allocation of labour and plant resources, etc.

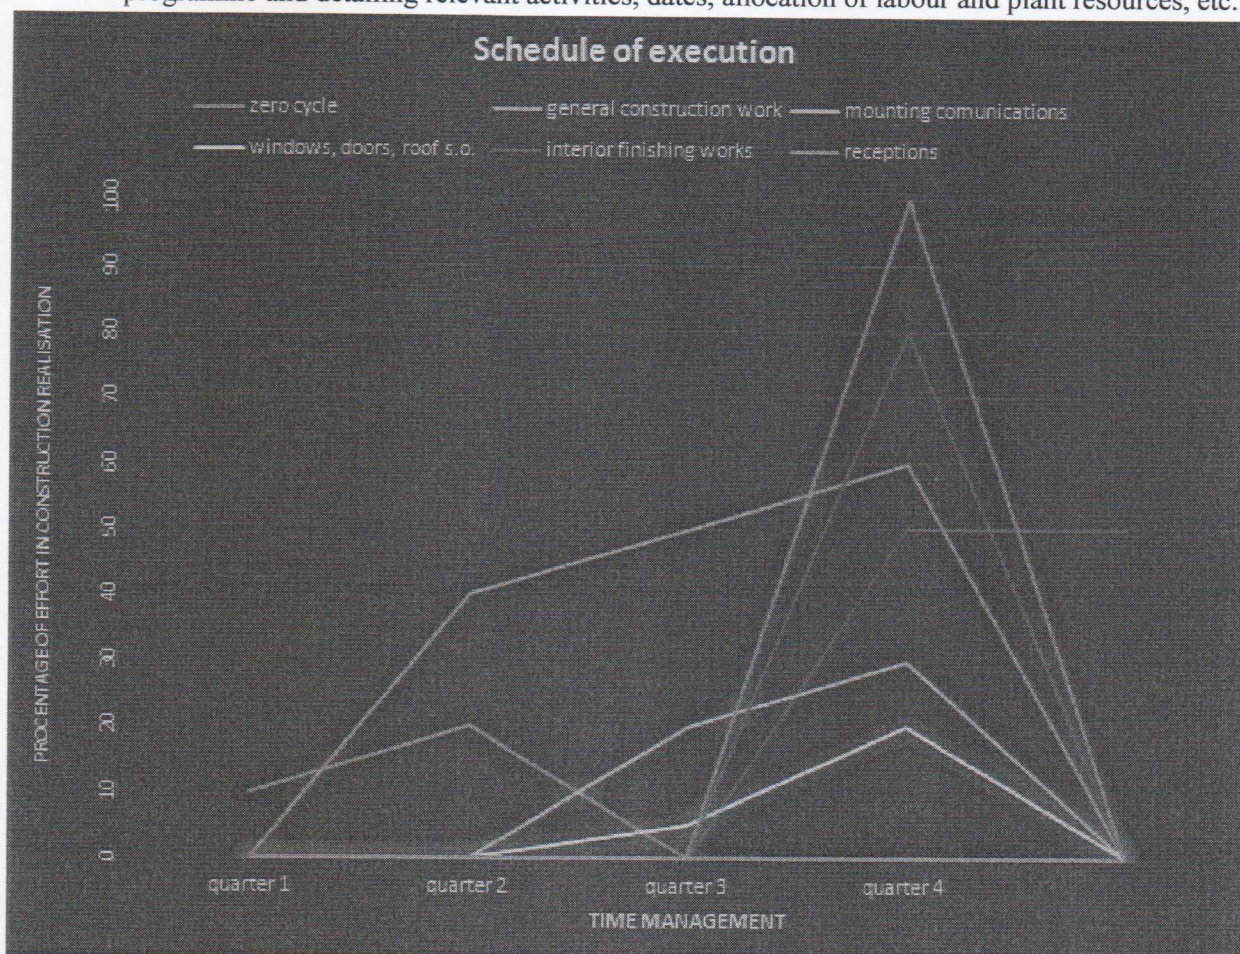

CONSTRUCTION PROCESS ACCORDING TO WEATHER CONDITIONS:

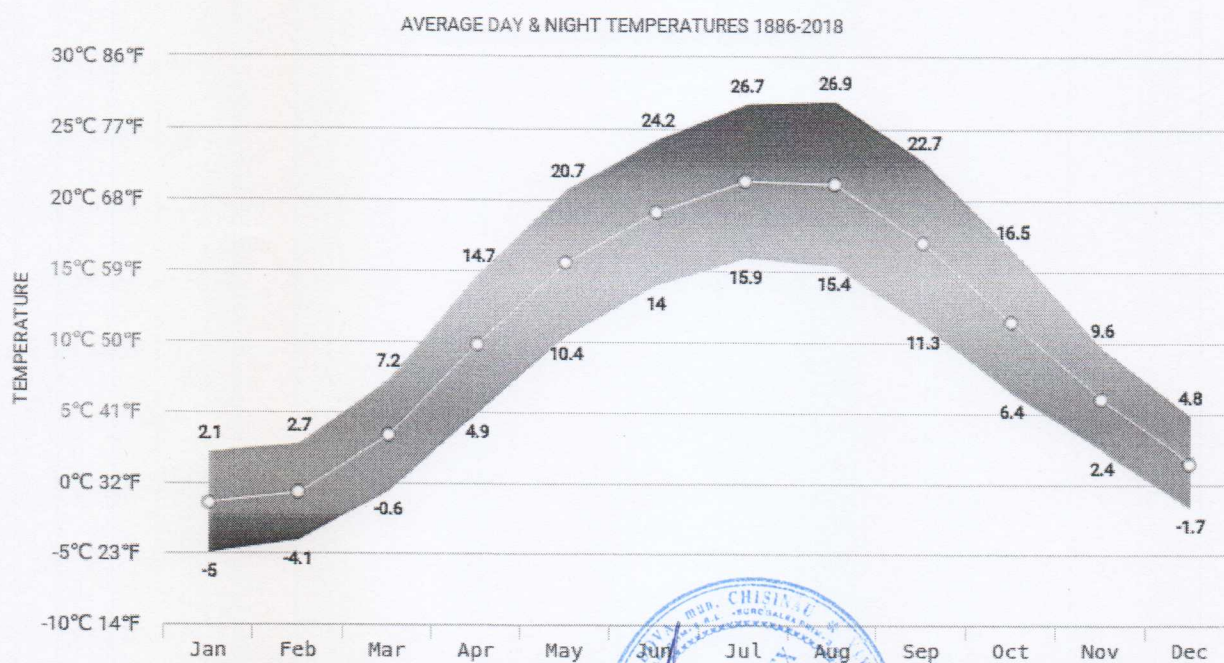

ESTIMATIONS OF THE MAN/HOURS ATTRACTED:

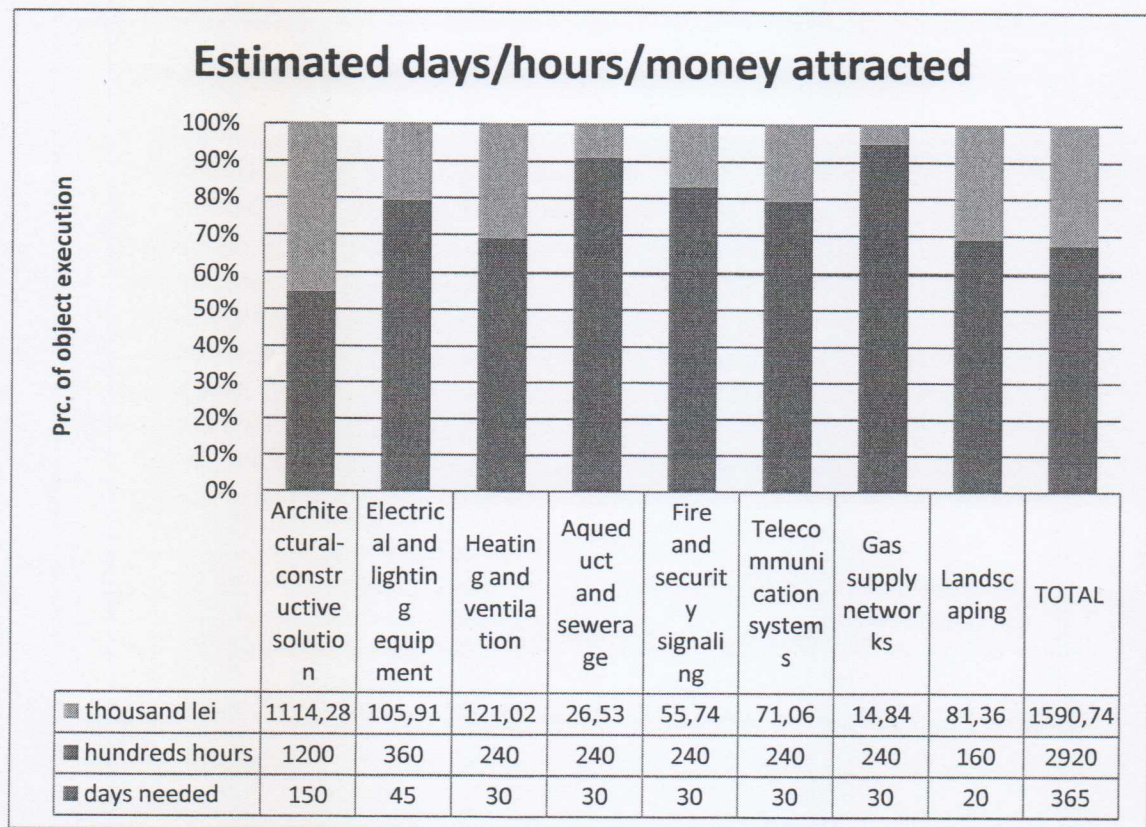

4.6.3.4 If the tenderer plans to subcontract part of the works, he must provide the following details:

WE DONT INTEND TO SUBCONTRACTE CONSTRUCTION WORKS

Work intended to be subcontracted	Name and details of subcontractors	Value of subcontracting as percentage of the total cost of the project	Experience in similar work (details to be specified)
-----------------------------------	------------------------------------	--	--

Signature: DIRECTOR DMITRY CIOCOI

Date: Tuesday, 02 June 2020

