

VOLUME 1


SECTION 4

FORM 4.6.3

WORK PLAN AND PROGRAMME

4.6.3.1 State the proposed location of your main office on the site, stations (steel/concrete/asphalt structures), warehouses, laboratories, accommodation, etc. (sketches to be attached as required).

WE PROPOSE THE FOLLOWING APPROXIMATION OF OBJECTS LOCATION:

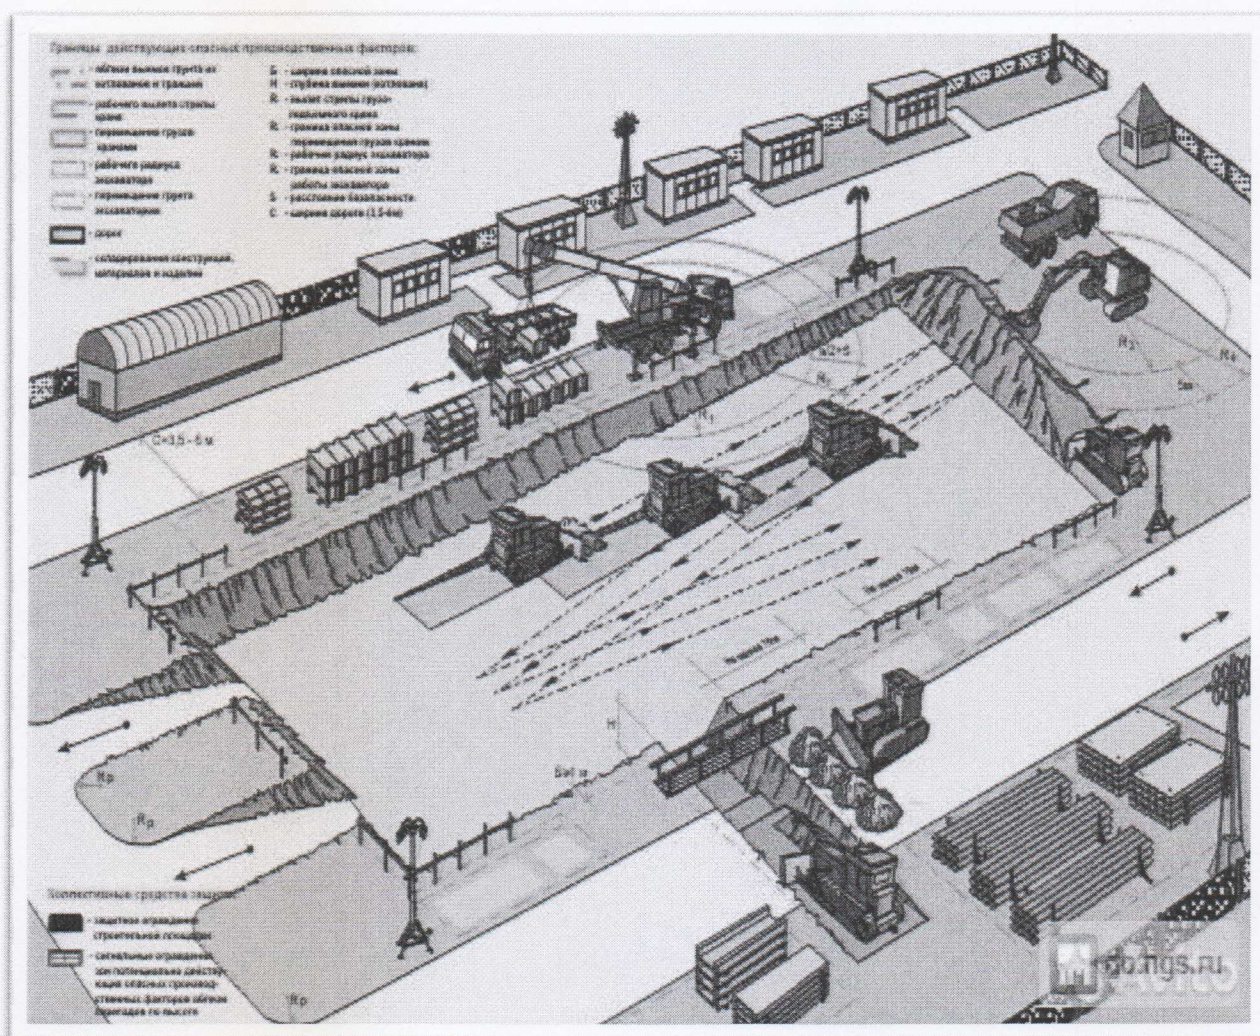

4.6.3.2 Give a brief outline of your programme for completing the works in accordance with the required method of construction and stated time of completion.


SCHEDULE OF EXECUTION OF WORKS:




| Contractor Name: General Police Inspectorate, 11/1, Tiraspol street, Chisinau, MD2069 Contract: THOR/4.3/1 – Activity 7.2 | | | | Reconstruction of Police Stations | | | | | | | | | | | |
|---|--------------------------|---------------|----------------|-----------------------------------|----|----|----|----|----|----|----|----|-----|-----|-----|
| REF | TRADE | START DATE | FINISH DATE | TIME PERIOD | | | | | | | | | | | |
| | | | | M1 | M2 | M3 | M4 | M5 | M6 | M7 | M8 | M9 | M10 | M11 | M12 |
| 1 | SITE PREPARATION | 2020 | 2021 | | | | | | | | | | | | |
| 2 | DEMOLITION | 2020 | 2021 | | | | | | | | | | | | |
| 3 | CONCRETE WORKS | 2020 | 2021 | | | | | | | | | | | | |
| 4 | PROTECTION WORKS | 2020 | 2021 | | | | | | | | | | | | |
| 5 | LIGHT STEEL FRAMING | 2020 | 2021 | | | | | | | | | | | | |
| 6 | TIMBER CONSTRUCTION | 2020 | 2021 | | | | | | | | | | | | |
| 7 | BLOCK CONSTRUCTION | 2020 | 2021 | | | | | | | | | | | | |
| 8 | ROOFING | 2020 | 2021 | | | | | | | | | | | | |
| 9 | DOORS AND WINDOWS | 2020 | 2021 | | | | | | | | | | | | |
| 10 | CLADDING AND LININGS | 2020 | 2021 | | | | | | | | | | | | |
| 11 | SUSPENDED CEILINGS | 2020 | 2021 | | | | | | | | | | | | |
| 12 | PLASTERING | 2020 | 2021 | | | | | | | | | | | | |
| 13 | JOINERY AND FIXTURES | 2020 | 2021 | | | | | | | | | | | | |
| 14 | WATER/GAS SERVICES | 2020 | 2021 | | | | | | | | | | | | |
| 15 | FINISHES | 2020 | 2021 | | | | | | | | | | | | |
| 16 | PAINTING | 2020 | 2021 | | | | | | | | | | | | |
| 17 | PLUMBING AND DRAINAGE | 2020 | 2021 | | | | | | | | | | | | |
| 18 | ELECTRICAL INSTALLATIONS | 2020 | 2021 | | | | | | | | | | | | |
| 19 | MECHANICAL INSTALLATIONS | 2020 | 2021 | | | | | | | | | | | | |
| 20 | EXTERNAL WORKS | 2020 | 2021 | | | | | | | | | | | | |
| 21 | LANDSCAPING | 2020 | 2021 | | | | | | | | | | | | |
| 22 | FINAL CLEAN | 2020 | 2021 | | | | | | | | | | | | |
| 23 | RECEPTION OF OBJECTS | 2020 | 2021 | | | | | | | | | | | | |




4.6.3.3 Attach a critical milestone bar chart (schedule of execution) representing the construction programme and detailing relevant activities, dates, allocation of labour and plant resources, etc.

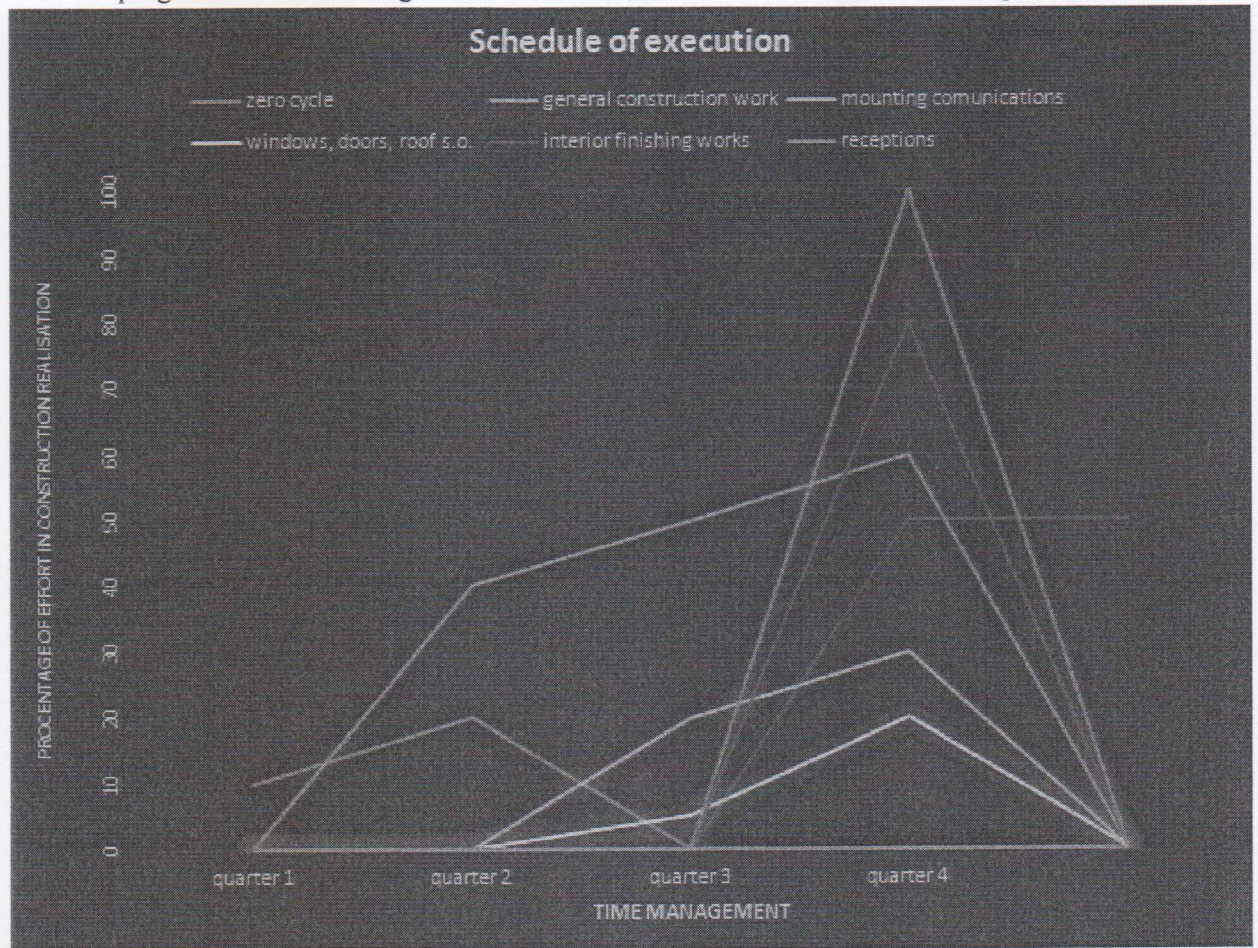

CONSTRUCTION PROCESS ACCORDING TO WEATHER CONDITIONS:

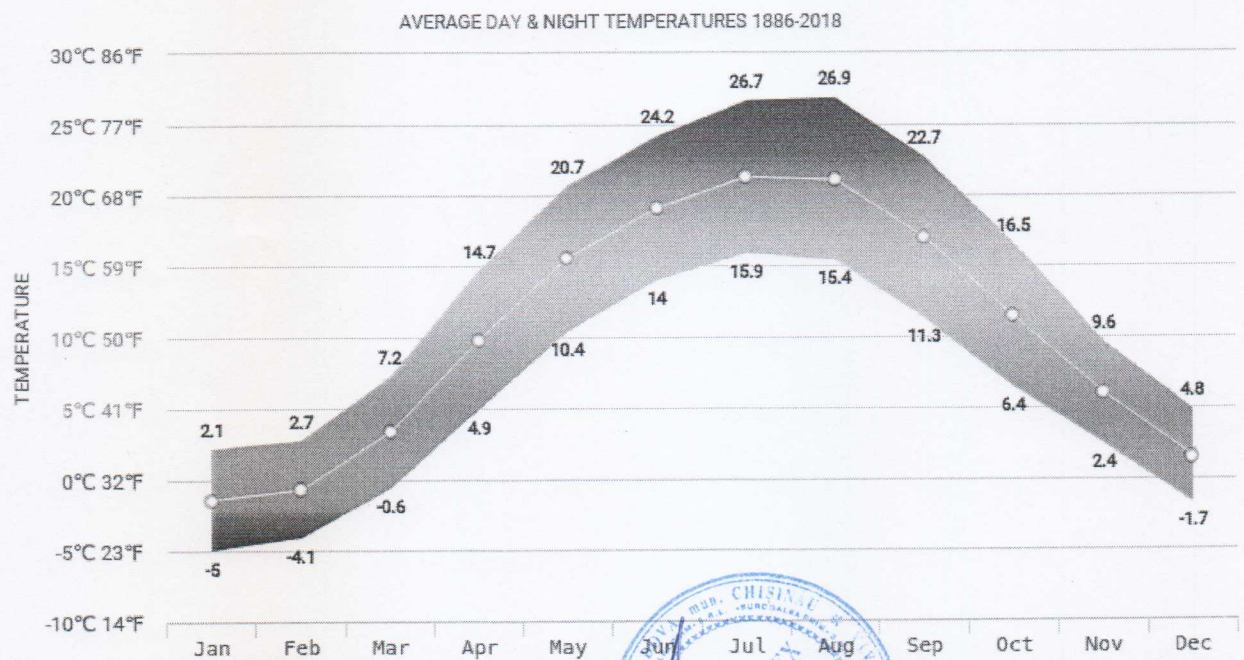

ESTIMATIONS OF THE MAN/HOURS ATTRACTED:

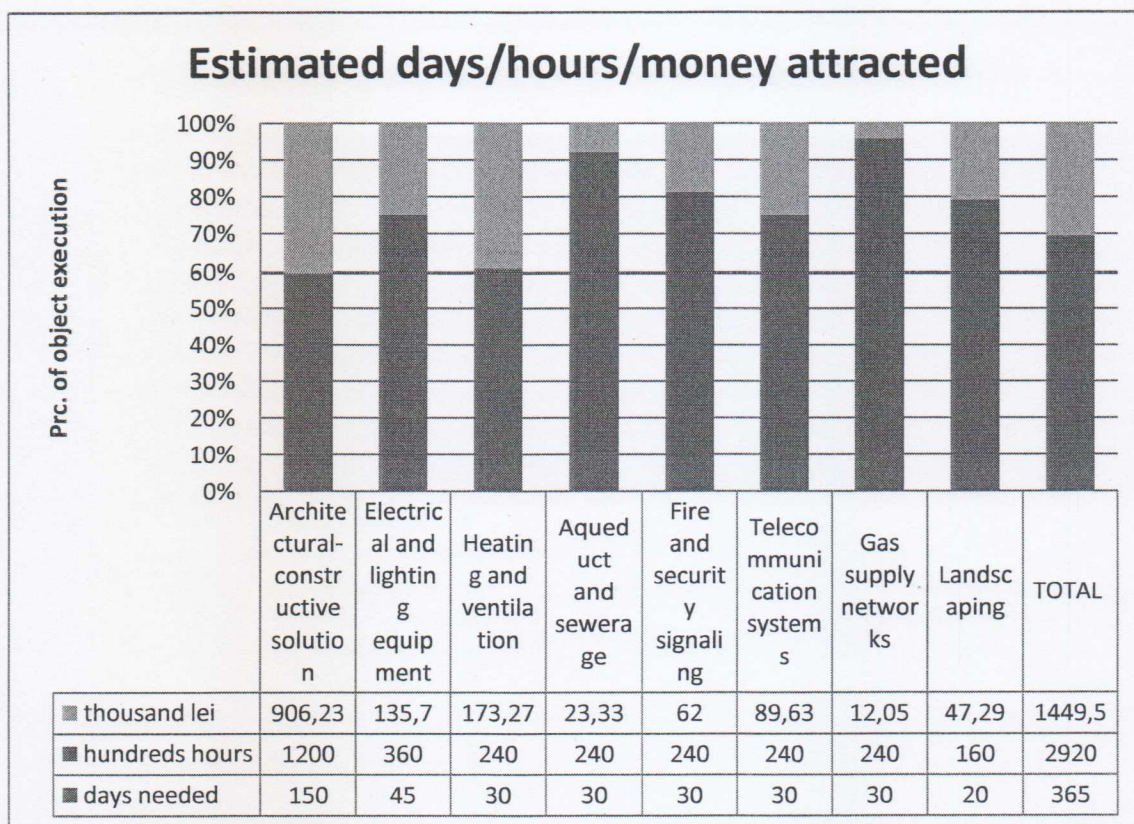

4.6.3.4 If the tenderer plans to subcontract part of the works, he must provide the following details:

WE DONT INTEND TO SUBCONTRACTE CONSTRUCTION WORKS

| Work intended to be subcontracted | Name and details of subcontractors | Value of subcontracting as percentage of the total cost of the project | Experience in similar work (details to be specified) |
|-----------------------------------|------------------------------------|--|--|
|-----------------------------------|------------------------------------|--|--|

Signature: DIRECTOR DMITRY CIOCOI

Date: Monday, 01 June 2020

