

EXPERIENȚĂ SIMILARĂ

I.

1. Denumirea și obiectul contractului: **Reparații capitale a sediului din s. Răzeni, rl Ialoveni, în cadrul proiectului „Creșterea protecției populației în situațiile de urgență cauzate de dezastre naturale în zona transfrontalieră” și Reparații capitale a sediului din s. Răzeni, rl Ialoveni, în cadrul proiectului ”Îmbunătățirea timpului de reacție pentru situații de urgență în zona transfrontalieră prin renovarea infrastructurii pentru instruirea populației”.**

2. Numărul și data contractelor: Nr. 46 din 24.11.2021 și Nr. 47 din 24.11.2021

3. Denumirea/numele beneficiarului Primăria s. Răzeni, rl Ialoveni

4. Adresa beneficiarului s. Răzeni, rl Ialoveni

5. Țara Republica Moldova

6. Calitatea în care a participat la îndeplinirea contractului:

- antreprenorul sau antreprenorul general (lider de asociație)
- antreprenor asociat
- subantreprenor

7. Valoarea contractului exprimată în moneda în care s-a încheiat contractul:

a) inițială (la data semnării contractului) 10 814 152,76 MDL

b) finală (la data finalizării contractului) 10 814 152,76 MDL

8. Dacă au fost litigii privind îndeplinirea contractului, natura acestora și modul lor de soluționare: nu

9. Perioada de executare a lucrării (luni)

a) contractată: _____,

b) efectiv realizată: _____

c) motivul de decalare a termenului contractat (dacă este cazul), care va fi susținut pe bază de acte adiționale încheiate cu beneficiarul _____

10. Nr/data procesului-verbal: PV RTL nr.1 din 21.12.2022 și PV RTL nr. 2 din 21.12.2022;

11. Principalele remedieri și completări înscrise în procesul-verbal de recepție _____

12. Alte aspecte relevante prin care ofertantul își susține experiența similară, cu referire în mod special la suprafețe sau volume fizice ale principalelor capacități și categorii de lucrări prevăzute în contracte _____

II.

1. Denumirea și obiectul contractului: **"Reconstrucția și modernizarea bazinului Dinamo din str. Gh. Asachi, 23a, mun. Chișinău".**
2. Numărul și data contractului: Contractul Ref:ITB 20/02152 din 21.12.2020;
3. Denumirea/numele beneficiarului: Pretura sectorului Centru, mun. Chișinău;
4. Adresa beneficiarului: str. Bulgară, 43, Chișinău;
5. Țara: Republica Moldova
6. Calitatea în care a participat la îndeplinirea contractului:
 - antreprenorul sau antreprenorul general
 - antreprenor asociat
 - subantreprenor
7. Valoarea contractului exprimată în moneda în care s-a încheiat contractul:
 - a) inițială (la data semnării contractului) 438 417,63 USD;
 - b) finală (la data finalizării contractului) 475 385,16 USD
8. Dacă au fost litigii privind îndeplinirea contractului, natura acestora și modul lor de soluționare: nu.
9. Perioada de executare a lucrării (luni)
 - contractată _____,
 - efectiv realizată: _____
 - motivul de decalare a termenului contractat (dacă este cazul), care va fi susținut pe bază de acte adiționale încheiate cu beneficiarul _____
10. Numărul și data procesului-verbal de recepție la terminarea lucrărilor: nr. 1 din 18.05.2022.
11. Principalele remedieri și completări înscrise în procesul-verbal de recepție _____
12. Alte aspecte relevante prin care ofertantul își susține experiența similară, cu referire în mod special la suprafețe sau volume fizice ale principalelor capacități și categorii de lucrări prevăzute în contracte _____

III.

1. Denumirea și obiectul contractului: **"Lucrări de construcții și renovare. Anexa la blocul central al construcției IET nr. 10 din or. Fălești"**.

2. Numărul și data contractului: Contractul N3319120C0006 din 21.07.2020;

3. Denumirea/numele beneficiarului: Primăria or. Fălești

4. Adresa beneficiarului: str. 31 August 1989, nr.131, Chișinău;

5. Țara: Republica Moldova

6. Calitatea în care a participat la îndeplinirea contractului:

- antreprenorul sau antreprenorul general
- antreprenor asociat
- subantreprenor

7. Valoarea contractului exprimată în moneda în care s-a încheiat contractul:

a) inițială (la data semnării contractului) 271.242,00 USD

b) finală (la data finalizării contractului) 271.242,00 USD

8. Dacă au fost litigii privind îndeplinirea contractului, natura acestora și modul lor de soluționare: nu.

9. Perioada de executare a lucrării (luni)

- contractată _____-

- efectiv realizată: _____

- motivul de decalare a termenului contractat (dacă este cazul), care va fi susținut pe bază de acte adiționale încheiate cu beneficiarul _____

10. Numărul și data procesului-verbal de recepție finală: nr. 01 din 18.01.2023.

11. Principalele remedieri și completări înscrise în procesul-verbal de recepție _____

—

12. Alte aspecte relevante prin care ofertantul își susține experiența similară, cu referire în mod special la suprafețe sau volume fizice ale principalelor capacități și categorii de lucrări prevăzute în contracte _____

IV.

1. Denumirea și obiectul contractului: **"Reparația capitală și replanificarea saloanelor etajul II al blocului curativ cu 5 nivele al IMSP Spitalul raional Ștefan Vodă".**
2. Numărul și data contractului: Contractul N3319120C0006 din 17.05.2021;
3. Denumirea/numele beneficiarului: IMSP SR Ștefan Vodă.
4. Adresa beneficiarului: strada 31 August 1989, Ștefan Vodă;
5. Țara: Republica Moldova
6. Calitatea în care a participat la îndeplinirea contractului:
 - antreprenorul
 - antreprenor asociat
 - subantreprenor
7. Valoarea contractului exprimată în moneda în care s-a încheiat contractul:
 - a) inițială (la data semnării contractului) 201600,00 USD
 - b) finală (la data finalizării contractului) 201600,00 USD
8. Dacă au fost litigii privind îndeplinirea contractului, natura acestora și modul lor de soluționare: nu.
9. Perioada de executare a lucrării (luni)
 - contractată _____
 - efectiv realizată: _____
 - motivul de decalare a termenului contractat (dacă este cazul), care va fi susținut pe bază de acte adiționale încheiate cu beneficiarul _____
10. Numărul și data procesului-verbal de recepție: PV RTL Nr. 1 din 20.12.2022.
11. Principalele remedieri și completări înscrise în procesul-verbal de recepție _____
12. Alte aspecte relevante prin care ofertantul își susține experiența similară, cu referire în mod special la suprafețe sau volume fizice ale principalelor capacități și categorii de lucrări prevăzute în contracte _____

V.

1. Denumirea și obiectul contractului: **”Renovarea interioară a etajului doi, blocul perinatal IMSP Spitalul raional Cahul”.**

2. Numărul și data contractului: Contractul N3319121C0001 din 04.03.2021;

3. Denumirea/numele beneficiarului: IMSP SR Cahul;

4. Adresa beneficiarului: str. Ștefan cel Mare, 120, Cahul;

5. Țara: Republica Moldova

6. Calitatea în care a participat la îndeplinirea contractului:

- antreprenorul
- antreprenor asociat
- subantreprenor

7. Valoarea contractului exprimată în moneda în care s-a încheiat contractul:

a) inițială (la data semnării contractului) 265 000,00 USD

b) finală (la data finalizării contractului) 4 946 154,08 MDL

8. Dacă au fost litigii privind îndeplinirea contractului, natura acestora și modul lor de soluționare: nu.

9. Perioada de executare a lucrării (luni)

- contractată: _____,-

- efectiv realizată: _____

- motivul de decalare a termenului contractat (dacă este cazul), care va fi susținut pe bază de acte adiționale încheiate cu beneficiarul _____

10. Numărul și data procesului-verbal de recepție: PV RTL f/n din 28.09.2023.

11. Principalele remedieri și completări înscrise în procesul-verbal de recepție _____

12. Alte aspecte relevante prin care ofertantul își susține experiența similară, cu referire în mod special la suprafețe sau volume fizice ale principalelor capacități și categorii de lucrări prevăzute în contracte _____

VI.

1. Denumirea și obiectul contractului: **"Lucrari de renovare a aripiei de sud și de est al etajului 3, IMSP Spitalul raional Taraclia "**.

2. Numărul și data contractului: Contractul N3319120C0009 din 05.08.2020;

3. Denumirea/numele beneficiarului: IMSP SR Taraclia;

4. Adresa beneficiarului: str. Cioban Valeriu, 1, Taraclia ;

5. Țara: Republica Moldova

6. Calitatea în care a participat la îndeplinirea contractului:

- antreprenorul
- antreprenor asociat
- subantreprenor

7. Valoarea contractului exprimată în moneda în care s-a încheiat contractul:

a) inițială (la data semnării contractului) 280 000,00 USD.

b) finală (la data finalizării contractului) 280 000,00 USD;

8. Dacă au fost litigii privind îndeplinirea contractului, natura acestora și modul lor de soluționare: nu.

9. Perioada de executare a lucrării (luni)

- contractată _____,-

- efectiv realizată: _____

- motivul de decalare a termenului contractat (dacă este cazul), care va fi susținut pe bază de acte adiționale încheiate cu beneficiarul _____

10. Numărul și data procesului-verbal de recepție: PV RTL nr. 1 din 28.12.2023.

11. Principalele remedieri și completări înscrise în procesul-verbal de recepție _____

—

12. Alte aspecte relevante prin care ofertantul își susține experiența similară, cu referire în mod special la suprafețe sau volume fizice ale principalelor capacități și categorii de lucrări prevăzute în contracte _____

VII.

1. Denumirea și obiectul contractului: **”Construcția și reparația depozitelor de muniții din cadrul bazei păstrare tehnică, armament și patrimoniu militar al Ministerului Apărării al Republicii Moldova (Floresti, Cahul)”**.

2. Numărul și data contractului: Contractul N3319120C0009 din 05.08.2023;

3. Denumirea/numele beneficiarului: Ministerul Apărării RM;

4. Adresa beneficiarului: Șoseaua Hîncești, 84, Chișinău;

5. Țara: Republica Moldova

6. Calitatea în care a participat la îndeplinirea contractului:

- antreprenorul
- antreprenor asociat
- subantreprenor

7. Valoarea contractului exprimată în moneda în care s-a încheiat contractul:

a) inițială (la data semnării contractului) 519.311,16 USD;

b) finală (la data finalizării contractului) 519.311,16 USD;

8. Dacă au fost litigii privind îndeplinirea contractului, natura acestora și modul lor de soluționare: nu.

9. Perioada de executare a lucrării (luni)

- contractată _____,-

- efectiv realizată: _____

- motivul de decalare a termenului contractat (dacă este cazul), care va fi susținut pe bază de acte adiționale încheiate cu beneficiarul _____

10. Nr/data procese-verbale: PV RF nr. 12 din 01.09.2022; PV RF nr. 138/1 din 02.09.2022;

11. Principalele remedieri și completări înscrise în procesul-verbal de recepție _____

12. Alte aspecte relevante prin care ofertantul își susține experiența similară, cu referire în mod special la suprafețe sau volume fizice ale principalelor capacități și categorii de lucrări prevăzute în contracte _____

Lista lucrărilor executate în ultimul an de activitate

Nr crt	Obiectul contractului	Denumire beneficiar/Adresa	Preț contract/ valoare lucrări executate	Perioada de execuție a lucrării	Nr/data PV RTL
1	Renovarea interioară a etajului doi, blocul perinatal IMSP Spitalul raional Cahul.	IMSP Spitalul raional Cahul	4 946 154,08 MDL	04.03.2021- 28.09.2023	PV RTL f/n din 28.09.2023
2	Lucrari de renovare a aripii de sud și de est al etajului 3, IMSP Spitalul raional Taraclia	IMSP Spitalul raional Taraclia	280 000,00 USD	05.08.2020- 28.12.2023	PV RTL nr.1 din 28.12.2023

Nume: Ciobanu Sergiu

Funcția în cadrul firmei: Director

Denumirea firmei: SC “Prestigiu-Az” SRL



This project is funded by
the European Union



Romania-Republic of Moldova
ENI-CROSS BORDER COOPERATION

CONTRACT FORM
WORKS CONTRACT FOR EUROPEAN UNION EXTERNAL ACTIONS
NO. 2SOFT/4.2/71/LP-004

NO. 46 FROM 24.11 2021

FINANCED FROM THE EU GENERAL BUDGET
(PREPARED ACCORDING TO PRAG RULES)

Between

**Republican Training Center of the General Inspectorate for Emergency Situations of
Ministry of Internal Affairs from Republic of Moldova, MD-2060, Mun. Chişinău, 8/1,
Cuza-Vodă bd, E-mail: cri@dse.md, represented by Ghenadie DANILIUC**

("The Contracting Authority"),

of the one part,

and

**"Prestigiu-AZ" SRL, Fiscal code: 1005600037219, VAT number: 0404180, Legal address:
village Corjova, district Criuleni, Republic of Moldova, Address of head office: of. 409, 11/6,
Mircea cel Batrin str. MD-4817, Chisinau, Republic of Moldova, e-mail: presigiu@mail.ru,
represented by Sergiu CIOBANU**

("the Contractor")

of the other part,

have agreed as follows:

PROJECT "Increasing the protection of the population in emergency situation caused by
natural disasters in the cross-border area" (2SOFT/4.2/71)

CONTRACT TITLE:

**Renovation works for Republican Training Center in Razeni (infrastructure works) for
Republican Training Center of the General Inspectorate for Emergency Situation of the
Ministry of Internal Affairs from Republic of Moldova**

Identification number 2SOFT/4.2/71/LP-004

Whereas the Contracting Authority would like the Contractor to carry out the following works:

Construction works of Republican Training Center in Razeni, Republic of Moldova

and has accepted a tender by the Contractor for the execution and completion of such works and the remedying of any defects therein.

It is hereby agreed as follows:

- (1) In this Contract, words and expressions shall have the meanings assigned to them in the contractual conditions set out below.
- (2) The following documents shall be deemed to form and be read and construed as part of this Contract, in the following order of precedence:
 - (a) the Contract,
 - (b) the Special Conditions,
 - (c) the General Conditions,
 - (d) Forms F3, F5 and F7 from WinCmeta 2020, Neo, WinDoc
 - (e) the Technical and /or Performance Specifications,
 - (f) the Design Documentation (drawings),
 - (g) any other documents forming part of the Contract.

The various documents making up the contract shall be deemed to be mutually explanatory; in cases of ambiguity or divergence, they shall prevail in the order in which they appear above. Addenda shall have the order of precedence of the document they are amending.

(3) In consideration of the payments to be made by the Contracting Authority to the Contractor as hereinafter mentioned, the Contractor undertakes to execute and complete the works and remedy defects therein in full compliance with the provisions of the Contract.

(4) The Contracting Authority hereby agrees to pay the Contractor in consideration of the execution and completion of the works and remedying of defects therein the amount of:

- Contract price (excluding VAT/other taxes) **5.088.636,22 MDL** (five million, eighty-eight thousand, six hundred thirty-six,22 MDL).
- VAT taxes : 0 %

or such other sum as may become payable under the provisions of the Contract at the times and in the manner prescribed by the Contract. VAT will be paid in compliance with the binding regulations, national law and international agreements concerning the execution of the project. VAT and other taxes shall not be paid on the funds originating from EU funds.

(5) Other specific conditions applying to the Contract

Not the case

In witness whereof the parties hereto have signed the Contract. This Contract shall take effect on the date on which it is signed by the last party, namely the Contractor.

This contract, drawn up, shall enter into force upon its signing and shall act until the execution of each of the parties obligations assumed in accordance with this contract, being valid until **July 31, 2022.**

Done in English in three originals, two originals for the Contracting Authority, one and one original for the Contractor.

For the Contractor

Name: Sergiu CIOBANU

Title: Director

Signature:

Date:

**For the Contracting Authority**

Name: Ghenadie DANILIUC

Title: Head of the Republican Training Center of GIES

Signature:

Date:

**Payment dates of the parties****For the Contractor**

Name: "Prestigiu-AZ" SRL

Fiscal code 1005600037219

IBAN MD40AG000000022512217993

Bank Code AGRNMD2X

Bank Name MOLDOVA-AGROINDBANK SA

For the Contracting Authority

Name: Republican Training Center of the General Inspectorate for Emergency Situations of Ministry of Internal Affairs from Republic of Moldova

Fiscal code 1006601000576

IBAN: MD13TRPBAA311120A00651AD;
MD57TRPHAA311120C00651AB.a.u. 2021 cota RM - 445000,00 lei
UE - 1584000,00 lei

a.u. 2022 - 3056636,22 lei

Bank Code TREZMD2X

Bank Name Ministry of Finance - State Treasury





This project is funded by
the European Union



Romania-Republic of Moldova
ENI-CROSS BORDER COOPERATION

CONTRACT FORM

WORKS CONTRACT FOR EUROPEAN UNION EXTERNAL ACTIONS

NO. 2SOFT/4.2/85/

47 days 24.11.2021

FINANCED FROM THE EU GENERAL BUDGET

Between

Republican Training Center of the General Inspectorate for Emergency Situations of
Ministry of Internal Affairs from Republic of Moldova, MD-2060, Mun. Chişinău, 8/1,
Cuza-Vodă bd, E-mail: cri@dse.md, represented by Ghenadie DANILIU

("The Contracting Authority"),

of the one part,

and

"Prestigiu-AZ" SRL, Fiscal code: 1005600037219, VAT number: 0404180, Legal address:
village Corjova, district Criuleni, Republic of Moldova, Address of head office: of. 409, 11/6,
Mircea cel Batrin str. MD-4817, Chisinau, Republic of Moldova, e-mail: presigiu@mail.ru,
represented by Sergiu CIOBANU

("the Contractor")

of the other part,

have agreed as follows:

**PROJECT "Improving response time for emergency situations in the cross-border area by
renovating and equipping the infrastructure necessary for training and effectively
managing the population in the provision of the first aid" – 2SOFT/4.2/85**

**CONTRACT TITLE: Renovation works of the module for granting qualified first aid
within the Republican Training Center in Razeni (infrastructure works) for Republican
Training Center of the General Inspectorate for Emergency Situation of the Ministry of
Internal Affairs from Republic of Moldova (2SOFT/4.2/85)**

Identification number 2SOFT/4.2/85/

Whereas the Contracting Authority would like the Contractor to carry out the following works:
**Renovation works of the module for granting qualified first aid within the Republican
Training Center in Razeni (infrastructure works)** and has accepted a tender by the Contractor
for the execution and completion of such works and the remedying of any defects therein.

It is hereby agreed as follows:

- (1) In this Contract, words and expressions shall have the meanings assigned to them in the contractual conditions set out below.
- (2) The following documents shall be deemed to form and be read and construed as part of this Contract, in the following order of precedence:
- (a) the Contract,
 - (b) the Special Conditions,
 - (c) the General Conditions,
 - (d) Forms F3, F5 and F7 from WinCmeta 2020, Neo, WinDoc
 - (e) the Technical and /or Performance Specifications,
 - (f) the Design Documentation (drawings),
 - (g) any other documents forming part of the Contract.

The various documents making up the contract shall be deemed to be mutually explanatory; in cases of ambiguity or divergence, they shall prevail in the order in which they appear above. Addenda shall have the order of precedence of the document they are amending.

(3) In consideration of the payments to be made by the Contracting Authority to the Contractor as hereinafter mentioned, the Contractor undertakes to execute and complete the works and remedy defects therein in full compliance with the provisions of the Contract.

(4) The Contracting Authority hereby agrees to pay the Contractor in consideration of the execution and completion of the works and remedying of defects therein the amount of:

- Contract price (excluding VAT/other taxes) **5.725.516,54 MDL** (five million, seven hundred and twenty-five thousand, five hundred and sixteen,54 MDL).
- VAT taxes : 0 %

or such other sum as may become payable under the provisions of the Contract at the times and in the manner prescribed by the Contract. VAT will be paid in compliance with the binding regulations, national law and international agreements concerning the execution of the project. VAT and other taxes shall not be paid on the funds originating from EU funds.

(5) Other specific conditions applying to the Contract

Not the case

In witness whereof the parties hereto have signed the Contract. This Contract shall take effect on the date on which it is signed by the last party, namely the Contractor.

This contract, drawn up, shall enter into force upon its signing and shall act until the execution of each of the parties obligations assumed in accordance with this contract, being valid until **July 31, 2022**.

Done in English in three originals, two originals for the Contracting Authority, one and one original for the Contractor.

For the Contractor

Name: Sergiu CIOBANU

Title: Director

Signature:

Date:

**For the Contracting Authority**

Name: Ghenadie DANILIUC

Title: Head of the Republican Training Center of GIES

Signature:

Date:

**Payment dates of the parties****For the Contractor**

Name: "Prestigiu-AZ" SRL

Fiscal code 1005600037219

IBAN MD40AG000000022512217993

**For the Contracting Authority**

Name: Republican Training Center of the General Inspectorate for Emergency Situations of Ministry of Internal Affairs from Republic of Moldova

Fiscal code 1006601000576

IBAN MD13TRPBAA311120A00651AD
MD05TRPHAA311120B00651ABa. u 2021 cota RM - 494400,00 lei
ME - 1545600,00 lei

a. u 2022 - 3685516,54 lei

Bank Code AGRNMD2X

Bank Name MOLDOVA-AGROINDBANK SA

Bank Code TREZMD2X

Bank Name Ministry of Finance - State Treasury





This project is funded by
the European Union



Romania-Republic of Moldova
ENI-CROSS BORDER COOPERATION

ADDENDUM N ° 1 din 20.06. 2022
LA CONTRACTUL WORKS NR. 46 / 24.11.2021

Centrul Republican de Instruire al Inspectoratului General pentru Situații de Urgență al Ministerului Afacerilor Interne al Republicii Moldova, MD-2060, Mun. Chișinău, 8/1, bd Cuza-Vodă, e-mail: cri@dse.md, reprezentată de Victor MÎRZA

(„Autoritatea Contractantă”),

de o parte,

și

”Prestigu-AZ” SRL, Cod fiscal: 1005600037219, Nr. TVA: 0404180, Adresa legala: sat Corjova, raion Criuleni, Republica Moldova, Adresa sediului social: of. 409, 11/6, str. Mircea cel Batrin, MD-4817, Chișinău, Republica Moldova, e-mail: presigiu@mail.ru, reprezentat de Sergiu CIOBANU

(„antreprenorul”)

de cealalta parte,

au convenit după cum urmează:

PROIECTUL „Creșterea protecției populației în situație de urgență cauzată de dezastre naturale în zona transfrontalieră” (2SOFT/4.2/71)

TITLUL CONTRACTULUI:

**Lucrări de renovare pentru Centrul Republican de Instruire din s. Răzeni (lucrări de infrastructură)
Centrul Republican de Instruire al Inspectoratului General pentru Situații de Urgență al Ministerului
Afacerilor Interne din Republica Moldova
Număr de identificare 2SOFT/4.2/71/LP-004**

Următoarele prevederi ale contractului sunt serviciile indicate în oferta contractantului, încheiat între Autoritatea Contractantă și Contractant la 24.11.2021 („Contractul”), se înlocuiește după cum urmează:

Articolul 4:

- Prețul contractului (fără TVA/alte taxe) **5.088.636,22 MDL** (cinci milioane, optzeci și opt mii șase sute treizeci și șase, 22 MDL).

- TVA: 0%

De adăugat un subpunct nou,

- Suma contractului pentru anii 2022-2023 (fără TVA/alte taxe) este de **3.056.636,22 MDL** (trei milioane, cincizeci și șase mii șase sute treizeci și șase, 22 MDL).

- TVA: 0%

Articolul 5:

din,

”prezentul contract, fiind valabil până la data de **31 iulie 2022**”

în

”contractul actual este valabil pînă la data de **01 martie 2023**”

Toți ceilalți termeni și condiții ale contractului și ale anexelor anterioare ale acestuia rămân neschimbate. Acest act adițional va face parte integrantă din contract și va intra în vigoare la data ulterioară a semnării de către părți.



This project is funded by
the European Union



Romania-Republic of Moldova
ENI-CROSS BORDER COOPERATION

ADDENDUM N° 1 din 20.06.2022
LA CONTRACTUL WORKS NR. 46 / 24.11.2021

Întocmit în engleză în trei exemplare originale: un original pentru autoritatea contractantă, unul original pentru Comisia Europeană și un original pentru contractant.

Datele de plată ale părților

Pentru Antreprenor

Nume: Sergiu CIOBANU

Titlu: Director

Semnatura:

Data:



Pentru Autoritatea Contractantă

Nume: Victor MÎRZA

Titlu: Șef adjunct al Centrului
Republican de Instruire al IGSU

Semnatura:

Data:



Datele de plată ale părților

Pentru Antreprenor

Nume: "Prestigiu-AZ" SRL

Cod fiscal 1005600037219

IBAN MD40AG000000022512217993

Cod Bancar AGRNMD2X

Banca MOLDOVA-AGROINDBANK
SA

Pentru Autoritatea Contractantă

Name: Centrul Republican de
Instruire al Inspectoratului
General pentru Situații de
Urgență al MAI

Cod fiscal 1006601000576

IBAN: 2022 MD56TRPBAA311120A00651AF 1411280,35
MD03TRPHAA311120C00651AD 42470000

Cod Bancar TREZMD2X

Banca Ministerul Finanțelor — Trezoreria
de Stat

2021-0000014451 din 25.11.2021

Between

15 ianuarie 2016
Acord prelungire contract infrastructura soft 71



Pagină 2 de 5



This project is funded by
the European Union



Romania-Republic of Moldova
ENI-CROSS BORDER COOPERATION

ADDENDUM N° 1 din 20.06. 2022
LA CONTRACTUL WORKS NR. 47 / 24.11.2021

Centrul Republican de Instruire al Inspectoratului General pentru Situații de Urgență al Ministerului Afacerilor Interne al Republicii Moldova, MD-2060, Mun. Chișinău, 8/1, bd Cuza-Vodă, e-mail: cri@dse.md, reprezentată de Victor MÎRZA

(„Autoritatea Contractantă”),

de o parte,

și

„Prestigu-AZ” SRL, Cod fiscal: 1005600037219, Nr. TVA: 0404180, Adresa legala: sat Corjova, raion Criuleni, Republica Moldova, Adresa sediului social: of. 409, 11/6, str. Mircea cel Batrin, MD-4817, Chișinău, Republica Moldova, e-mail: presigiu@mail.ru, reprezentat de Sergiu CIOBANU

(„antreprenorul”)

de cealalta parte,

au convenit după cum urmează:

PROIECT” Îmbunătățirea timpului de răspuns pentru situații de urgență în zona transfrontalieră prin renovarea și dotarea infrastructurii necesare instruirii și gestionării efective a populației în acordarea primului ajutor” – 2SOFT/4.2/85

TITLUL CONTRACTULUI: Lucrări de renovare a modului de acordare a primului ajutor calificat din cadrul Centrului Republican de Instruire din Răzeni (lucrări de infrastructură) pentru Centrul Republican de Instruire al Inspectoratului General pentru Situații de Urgență al Ministerului Afacerilor Interne din Republica Moldova
Număr de identificare 2SOFT/4.2/85/

Următoarele prevederi ale contractului sunt serviciile indicate în oferta contractantului, încheiat între Autoritatea Contractantă și Contractant la 24.11.2021 („Contractul”), se înlocuiește după cum urmează:

Articolul 4:

- Prețul contractului (fără TVA/alte taxe) **5.725.516,54 MDL** (cinci milioane, șapte sute douăzeci și cinci mii cinci sute șaisprezece, 54 MDL).

- TVA: 0%

De adăugat un subpunct nou

- Suma contractului pentru anii 2022-2023 (fără TVA/alte taxe) **este de 3.685.516,54 MDL** (trei milioane, șase sute optzeci și cinci mii cinci sute șaisprezece, 54 MDL).

- TVA: 0%

Articolul 5:

din

”prezentul contract, fiind valabil până la data de **31 iulie 2022**”

în

”contractul este valabil pînă la data de **01 martie 2023**”



This project is funded by
the European Union



Romania-Republic of Moldova
ENI-CROSS BORDER COOPERATION

ADDENDUM N^o 1 din 20.06. 2022 LA CONTRACTUL WORKS NR. 47 / 24.11.2021

Toți ceilalți termeni și condiții ale contractului și ale anexelor anterioare ale acestuia rămân neschimbate. Acest act adițional va face parte integrantă din contract și va intra în vigoare la data ulterioară a semnării de către părți.

Întocmit în engleză în trei exemplare originale: un original pentru autoritatea contractantă, unul original pentru Comisia Europeană și un original pentru contractant.

Datele de plată ale părților

Pentru Antreprenor

Nume: Sergiu CIOBANU

Titlu: Director

Semnatura:

Data:



Pentru Autoritatea Contractantă

Nume: Victor MÎRZA

Titlu: Șef adjunct al Centrului
Republican de Instruire al IGSU

Semnatura:

Data:



Datele de plată ale părților

Pentru Antreprenor

Nume: "Prestigiu-AZ" SRL

Cod fiscal 1005600037219

IBAN MD40AG000000022512217993

Cod Bancar AGRNMD2X

Banca MOLDOVA-AGROINDBANK
SA

Pentru Autoritatea Contractantă

Name: Centrul Republican de
Instruire al Inspectoratului
General pentru Situații de
Urgență al MAI

Cod fiscal 1006601000576

IBAN: 2022 MD56TRPBAA311120A00651AF 1955019,65

Cod Bancar TREZMD2X

Banca Ministerul Finanțelor – Trezoreria
de Stat

2021-0000017456 din 25.11.21



This project is funded by
the European Union



Romania-Republic of Moldova
ENI-CROSS BORDER COOPERATION

ADDENDUM N ° 2 din 16.11. 2022
LA CONTRACTUL WORKS NR. 46 / 24.11.2021

Centrul Republican de Instruire al Inspectoratului General pentru Situații de Urgență al Ministerului Afacerilor Interne al Republicii Moldova, MD-2060, Mun. Chișinău, 8/1, bd Cuza-Vodă, e-mail: cri@dse.md, reprezentată de Victor MÎRZA

(„Autoritatea Contractantă”),

de o parte,

și

”Prestigu-AZ” SRL, Cod fiscal: 1005600037219, Nr. TVA: 0404180, Adresa legala: sat Corjova, raion Criuleni, Republica Moldova, Adresa sediului social: of. 409, 11/6, str. Mircea cel Batrin, MD-4817, Chișinău, Republica Moldova, e-mail: presigiu@mail.ru, reprezentat de Sergiu CIOBANU

(„antreprenorul”)

de cealalta parte,

au convenit după cum urmează:

PROIECTUL „Creșterea protecției populației în situație de urgență cauzată de dezastre naturale în zona transfrontalieră” (2SOFT/4.2/71)

TITLUL CONTRACTULUI:

Lucrări de renovare pentru Centrul Republican de Instruire din s. Răzeni (lucrări de infrastructură)
Centrul Republican de Instruire al Inspectoratului General pentru Situații de Urgență al Ministerului
Afacerilor Interne din Republica Moldova
Număr de identificare 2SOFT/4.2/71/LP-004

Următoarele prevederi ale contractului sunt serviciile indicate în oferta contractantului, încheiat între Autoritatea Contractantă și Contractant la 24.11.2021 („Contractul”), se înlocuiește după cum urmează:

Articolul 4:

- Prețul contractului (fără TVA/alte taxe) **5.088.636,22 MDL** (cinci milioane, optzeci și opt mii șase sute treizeci și șase, 22 MDL).

- TVA: 0%

De adăugat un subpunct nou,

- Suma contractului pentru anul 2022 (fără TVA/alte taxe) **este de 3.056.636,22 MDL** (trei milioane, cincizeci și șase mii șase sute treizeci și șase, 22 MDL).

- TVA: 0%

Articolul 5:

din,

”prezentul contract, fiind valabil până la data de **31 iulie 2022**”

în

”contractul actual este valabil pînă la data de **01 martie 2023**”

Toți ceilalți termeni și condiții ale contractului și ale anexelor anterioare ale acestuia rămân neschimbate. Acest act adițional va face parte integrantă din contract și va intra în vigoare la data ulterioară a semnării de către părți.



This project is funded by
the European Union



Romania-Republic of Moldova
ENI-CROSS BORDER COOPERATION

ADDENDUM N ° ____ din ____ 2022

LA CONTRACTUL WORKS NR. 46 / 24.11.2021

Întocmit în engleză în trei exemplare originale: un original pentru autoritatea contractantă, unul original pentru Comisia Europeană și un original pentru contractant.

Datele de plată ale părților

Pentru Antreprenor

Nume: Sergiu CIOBANU

Titlu: Director

Semnatura:

Data:



Pentru Autoritatea Contractantă

Nume: Victor MÎRZA

Titlu: Șef adjunct al Centrului
Republican de Instruire al IGSU

Semnatura:

Data:



Datele de plată ale părților

Pentru Antreprenor

Nume: "Prestigiu-AZ" SRL

Cod fiscal 1005600037219

IBAN MD40AG000000022512217993

Cod Bancar AGRNMD2X

Banca MOLDOVA-AGROINDBANK
SA

Pentru Autoritatea Contractantă

Name: Centrul Republican de
Instruire al Inspectoratului
General pentru Situații de
Urgență al MAI

Cod fiscal 1006601000576

IBAN: MD56TRPBAA311120A00651AF 2119430,57
MD03TRPHAA311120C00651AD 937205,65

Cod Bancar TREZMD2X

Banca Ministerul Finanțelor – Trezoreria
de Stat

Between





This project is funded by
the European Union



Romania-Republic of Moldova
ENI-CROSS BORDER COOPERATION

ADDENDUM N° 2 din 23.11.2022
LA CONTRACTUL WORKS NR. 47 / 24.11.2021

Between

Republican Training Center of the General Inspectorate for Emergency Situations of Ministry of Internal Affairs from Republic of Moldova, MD-2060, Mun. Chișinău, 8/1, Cuza-Vodă bd, E-mail: cri@dse.md, represented by Victor MÎRZA

("The Contracting Authority"),

of the one part,

and

"Prestigiu-AZ" SRL, Fiscal code: 1005600037219, VAT number: 0404180, Legal address: village Corjova, district Criuleni, Republic of Moldova, Address of head office: of. 409, 11/6, Mircea cel Batrin str. MD-4817, Chisinau, Republic of Moldova, e-mail: presigiu@mail.ru, represented by Sergiu CIOBANU

("the Contractor")

of the other part,

have agreed as follows:

PROJECT "Improving response time for emergency situations in the cross-border area by renovating and equipping the infrastructure necessary for training and effectively managing the population in the provision of the first aid" – 2SOFT/4.2/85

CONTRACT TITLE: Renovation works of the module for granting qualified first aid within the Republican Training Center in Razeni (infrastructure works) for Republican Training Center of the General Inspectorate for Emergency Situation of the Ministry of Internal Affairs from Republic of Moldova (2SOFT/4.2/85)

Identification number 2SOFT/4.2/85/

The following provisions of the contract are the services indicated in the contractor's tender, concluded between the Contracting Authority and the Contractor on 24.11.2021 ("the Contract"), shall be replaced as follows:

Article 4:

- Contract price (excluding VAT / other taxes) **5,725,516.54 MDL** (five million, seven hundred and twenty-five thousand five hundred and sixteen, 54 MDL).

- VAT: 0%

To add sub-points

- Increasing the amount of the contract for the year 2022 by **1,730,496.89 MDL** (one million seven hundred thirty thousand four hundred ninety-six, 89 MDL) expected for the year 2023, with payment of the outstanding amount in the current year.

- The amount of the contract for the year 2022 (without VAT/other taxes), after the increase, will constitute **3,685,516.54 MDL** (three million, six hundred and eighty-five thousand five hundred and sixteen, 54 MDL).

- VAT: 0%



This project is funded by
the European Union



Romania-Republic of Moldova
ENI-CROSS BORDER COOPERATION

ADDENDUM N° 2 din 23. 11. 2022
LA CONTRACTUL WORKS NR. 47 / 24.11.2021

All other terms and conditions of the contract and its annexes remain unchanged. This addendum will form an integral part of the contract and will enter into force on the date of signature by the parties.

Done in English in triplicate: one original for the contracting authority, one original for the European Commission and one original for the contractor.

For the Contractor

Name: Sergiu CIOBANU

Title: Director

Signature:

Date:



For the Contracting Authority

Name: Victor MÎRZA

Title: Deputy head of the Republican
Training Centre of GIES

Signature:

Date:

2021-0000017456



Payment dates of the parties

For the Contractor

Name: "Prestigiu-AZ" SRL

Fiscal code 1005600037219

IBAN MD40AG000000022512217993

Bank Code AGRNMD2X

Bank Name MOLDOVA-AGROINDBANK
SA

For the Contracting Authority

Name: Republican Training Centre of the General
Inspectorate for Emergency Situations of
Ministry of Internal Affairs from Republic
of Moldova

Cod
fiscal 1006601000576

IBAN: MD56TRPBAA311120A00651AF 2490946,43 lei
MD48TRPHAA311120B00651AD 881385,61 lei
MD40TRPBAA311120A00651AC 313184,50 lei

Bank Code TREZMD2X

Bank Name Ministry of Finance - State Treasury

15 ianuarie 2016

Acord prelungire contract infrastructura soft 85



**PROCES-VERBAL
DE RECEPȚIE LA TERMINAREA LUCRĂRILOR**

Nr. 2 din 21.12.2022

privind lucrarea **Reparații capitale a sediului din s. Răzeni, r-l Ialoveni, în cadrul proiectului "Îmbunătățirea timpului de reacție pentru situații de urgență în zona transfrontalieră prin renovarea infrastructurii pentru instruirea populației" (2SOFT/4.2/85)** executată la obiectul **Centrul Republican de Instruire al IGSU din s. Răzeni, r-l Ialoveni** în cadrul contractului nr. 47 din 24 noiembrie 2021 încheiat între **Centrul Republican de Instruire al IGSU și SRL "Prestigiu Az"** pentru lucrările de **Reparație capitală**.

1. Lucrările au fost executate în baza autorizației nr. 9, eliberată de **Primăria s. Răzeni, r-l Ialoveni** la **15 august 2022**, cu valabilitate pînă la **15 august 2023**.

2. Comisia de recepție și-a desfășurat activitatea în intervalul , fiind formată din:

Președintele comisiei:

Victor Mirza

Șef adjunct al CRI al IGSU, locotenent-colonel al s/intern

Membrii comisiei:

Vlad Golban

Șef DL al IGSU, colonel al s/intern

Ion Ciobanu

Șef DACI al IGSU, locotenent-colonel al s/intern

Nadejda Harea

Ofițer superior al SL a CRI al IGSU, maior al s/intern

Tatiana Pogolșa

Șef SF al CRI al IGSU, maior al s/intern

3. Au mai participat la recepție:

Ion Butucea

Responsabil tehnic

Sergiu Ciobanu

Director SRL "Prestigiu Az"

4. Constatările comisiei de recepție:

1) din documentația scrisă și desenată, care trebuia prezentată, au lipsit sau sînt incomplete piesele cuprinse în lista-anexă nr. 1;

2) lucrările cuprinse în lista-anexă nr. 2 nu au fost executate;

3) în lucrările, cuprinse în lista-anexă nr.3, nu s-au respectat prevederile proiectului.

5. Comisia de recepție, în urma constatărilor făcute, propune:

Admiterea recepției la terminarea lucrărilor

6. Comisia de recepție motivează propunerea făcută prin:

Lucrările sunt finalizate.

7. Comisia de recepție recomandă următoarele:

Obiectul de recepționat la terminarea lucrărilor.

7¹. Descrierea obiectului recomandat spre recepție:

Obiectul cu numărul cadastral **2334314.005.06**, adresa poștală **s. Răzeni, r-l Ialoveni**, destinația **săli de studii**, compus din următoarele construcții: suprafața la sol **997,65 m²**, suprafața totală, **1 739,7 m²**, numărul de etaje **S+P+E**, conform certificatului despre rezultatele inspectării bunului imobil, anexat la prezentul proces-verbal.



8. Prezentul proces-verbal, conținând 2 file și 3 anexe numerotate, cu un total de 5 file, a fost încheiat astăzi 21.12.2022 în 5 exemplare.

9. Concluzia Agenției pentru Supraveghere Tehnică:
Comisia de recepție:

Președintele comisiei:

Membrii comisiei:




Victor Mîrza


Vlad Golban


Ion Ciobanu


Nadejda Harea


Tatiana Pogolșa




Ion Butucea

10. Lucrarea *Reparații capitale a sediului din s. Răzeni, r-l Ialoveni* este recepționată.

TRANSMISĂ:

EXECUTANTUL:

SRL „Prestigiu - Az”

Sergiu Ciobanu

"21" "12" 2022



PRIMITĂ:

INVESTITORUL:

Șef adjunct al CRI al IGSU

Victor Mîrza

"21" "12" 2022



LISTA
lista documentației scrise și desenate care lipsește

Obiecții nu sunt.

Diriginte de șantier

Responsabil tehnic

Șef adjunct al CRI



Ion Beșelea

Ion Butucea

Victor Mîrza

LISTA
lista lucrărilor care nu au fost executate

Obiecții nu sunt

Diriginte de șantier

Responsabil tehnic

Șef adjunct al CRI



Ion Beșulea

Ion Butucea

Victor Mîrza

LISTA
lista observațiilor comisiei de recepție și a lucrărilor care nu
au respectat prevederile proiectului

Obiecții nu sunt

Diriginte de șantier

Responsabil tehnic

Șef adjunct al CRI



Ion Beșelea

Ion Butucea

Victor Mîrza

PROCES-VERBAL
DE RECEPȚIE LA TERMINAREA LUCRĂRILOR

Nr. 1 din 21.12.2022

privind lucrarea *Reparații capitale a sediului din s. Răzeni, r-l Ialoveni, în cadrul proiectului "Creșterea protecției populației în situațiile de urgență cauzate de dezastre naturale în zona transfrontalieră" (2SOFT/4.2/71)* executată la obiectul *Centrul Republican de Instruire al IGSU din s. Răzeni, r-l Ialoveni* în cadrul contractului nr. 46 din 24 noiembrie 2021 încheiat între *Centrul Republican de Instruire al IGSU și SRL "Prestigiu Az"* pentru lucrările de *Reparație capitală*.

1. Lucrările au fost executate în baza autorizației nr. 10, eliberată de *Primăria s. Răzeni, r-l Ialoveni* la 15 august 2022, cu valabilitate pînă la 15 august 2023.

2. Comisia de recepție și-a desfășurat activitatea în intervalul , fiind formată din:

Președintele comisiei:

Victor Mîrza

Șef adjunct al CRI al IGSU, locotenent-colonel al s/intern

Membrii comisiei:

Vlad Golban

Șef DL al IGSU, colonel al s/intern

Ion Ciobanu

Șef DACI al IGSU, locotenent-colonel al s/intern

Nadejda Harea

Ofițer superior al SL a CRI al IGSU, maior al s/intern

Tatiana Pogolșa

Șef SF al CRI al IGSU, maior al s/intern

3. Au mai participat la recepție:

Ion Butucea

Responsabil tehnic

Sergiu Ciobanu

Director SRL "Prestigiu Az"

4. Constatările comisiei de recepție:

1) din documentația scrisă și desenată, care trebuia prezentată, au lipsit sau sînt incomplete piesele cuprinse în lista-anexă nr. 1;

2) lucrările cuprinse în lista-anexă nr. 2 nu au fost executate;

3) în lucrările, cuprinse în lista-anexă nr.3, nu s-au respectat prevederile proiectului.

5. Comisia de recepție, în urma constatărilor făcute, propune:

Admiterea recepției la terminarea lucrărilor

6. Comisia de recepție motivează propunerea făcută prin:

Lucrările sunt finalizate.

7. Comisia de recepție recomandă următoarele:

Obiectul de recepționat la terminarea lucrărilor.

7¹. Descrierea obiectului recomandat spre recepție:

Obiectul cu numărul cadastral 2334314.005.06, adresa poștală *s. Răzeni, r-l Ialoveni*, destinația *săli de studii*, compus din următoarele construcții: suprafața la sol 997,65 m², suprafața totală, 1 739,7 m², numărul de etaje S+P+E, conform certificatului despre rezultatele inspectării bunului imobil, anexat la prezentul proces-verbal.

MINISTERUL AFACERILOR INTERNE AL RM	
INSPECTORATUL GENERAL PENTRU SITUAȚII DE URGENȚĂ	
CENTRUL REPUBLICAN DE INSTRUIRE	
Nr. intrare	<u>796 int</u>
File	<u>5</u> din <u>21.12.2022</u>

8. Prezentul proces-verbal, conținând 2 file și 3 anexe numerotate, cu un total de 5 file, a fost încheiat astăzi 21.12. la 2022 în 5 exemplare.

9. Concluzia Agenției pentru Supraveghere Tehnică:
Comisia de recepție:

Președintele comisiei:

Membrii comisiei:



[Signature]

Victor Mîrza

[Signature]

Vlad Golban

[Signature]

Ion Ciobanu

[Signature]

Nadejda Harea

[Signature]

Tatiana Pogolșa

[Signature]

Ion Butucea

10. Lucrarea *Reparații capitale a sediului din s. Răzeni, r-l Ialoveni* este recepționată.

TRANSMISĂ:

EXECUTANTUL:

SRL „Prestigiu - Az”

[Signature]
Sergiu Ciobanu

"21" "12" 2022

L.Ș.



PRIMITĂ:

INVESTITORUL:

Șef adjunct al CRI al IGSU

[Signature]
Victor Mîrza

"21" "12" 2022

L.Ș.



LISTA
lista documentației scrise și desenate care lipsește

Obiecții nu sunt.

Diriginte de șantier

Responsabil tehnic

Șef adjunct al CRI



Ion Beșlea

Ion Butucea

Victor Mîrza

LISTA
lista lucrărilor care nu au fost executate

Obiecții nu sunt

Diriginte de șantier

Responsabil tehnic

Șef adjunct al CRI



Ion Beșulea

Ion Butucea

Victor Mîrza

LISTA
lista observațiilor comisiei de recepție și a lucrărilor care nu
au respectat prevederile proiectului

Obiecții nu sunt

Diriginte de șantier

Responsabil tehnic

Șef adjunct al CRI



Ion Beșelea

Ion Butucea

Victor Mîrza



Empowered lives.
Resilient nations.

CONTRACT FOR WORKS

Date: December 21, 2020

Dear Sir/Madam,

Ref.: ITB 20/02152: MIA/Reconstruction works for the modernization of the Swimming Center within the "Dinamo Central Sport Club" (Stage III)

The United Nations Development Programme (hereinafter referred to as "UNDP"), wishes to engage your company, duly incorporated under the Laws of the Republic of Moldova (hereinafter referred to as the "Contractor") in order to perform the Reconstruction works for the modernization of the Swimming Center within the "Dinamo Central Sport Club" - Stage III (hereinafter referred to as the "Works"), in accordance with the following Contract:

1. Contract Documents

- 1.1 This Contract is subject to the UNDP General Conditions for Civil Works, October 2017, attached hereto as Annex I. The provisions of such Annex shall control the interpretation of this Contract and in no way, shall be deemed to have been derogated by the contents of this letter and any other Annexes, unless otherwise expressly stated under section 4 of this letter, entitled "Special Conditions".
- 1.2 The Contractor and UNDP also agree to be bound by the provisions contained in the following documents, which shall take precedence over one another in case of conflict in the following order:
 - a) this Contract;
 - b) Annex I – The General Conditions of Contract for Civil Works;
 - c) the Schedule of Requirements and Technical Specifications dated of October 23, 2020 and Verified Technical Design Documentation as of August 2019, not attached hereto but known to and in the possession of both parties;
 - d) the Contractor's Price Schedule and Bills of Quantities not attached hereto but known to and in the possession of both parties.
- 1.3 All the above shall form the Contract between the Contractor and UNDP, superseding the contents of any other negotiations and/or agreements, whether oral or in writing, pertaining to the subject of this Contract.

Prestigiu-AZ SRL,

Straseni R-n, Sireti village, Republic of Moldova

2. Obligations of the Contractor

- 2.1 The Contractor shall commence work within **5 (five) calendar days** from the date on which he shall have been given access to the Site and received the notice to commence from the Engineer and shall perform and substantially complete the Works within **120 calendar days, by 20/04/2021**, in accordance with the Contract. The Contractor shall provide all materials, supplies, labor and other services necessary to that end.
- 2.2 This Contract will come into effect on the day of signature by both parties and shall expire on **30/09/2022**.
- 2.3 The Contractor shall submit to the Engineer the Programme of Work referred to in Clause 13 of the General Conditions within **5 (five) calendar days** from the date on which he shall have been given access to the Site.
- 2.4 The Contractor represents and warrants the accuracy of any information or data provided to UNDP for the purpose of entering into this Contract, as well as the quality of the Works foreseen under this Contract in accordance with the highest industrial and professional standards.

3. Price and Payment

- 3.1 In full consideration of the complete and satisfactory performance of the Works under this Contract, UNDP shall pay the Contractor a fixed contract price of **USD 438,417.63 (four hundred thirty-eight thousand, four hundred seventeen US Dollars and 63 cents) VAT 0% rate** contained in Bills of Quantities and Supplier's Quotation.
- 3.2 The price of this Contract is not subject to any adjustment or revision because of price or currency fluctuations or the actual costs incurred by the Contractor in the performance of the Contract.
- 3.3 The contractor shall submit an invoice for **USD 29,000.00 (twenty-nine thousand US Dollars)** upon submission and approval of the detailed Programme of Work and submission of the Performance Security. Invoices for the performed works, used materials and installed equipment shall be submitted by the 20th date of each month; and a final invoice within 15 days from the issuance of the Certificate of Substantial Completion by the Engineer.
- 3.4 UNDP shall effect payment of the invoices in USD, after receipt of the certificate of payment issued by the Engineer, approving the amount contained in the invoice. The Engineer may make corrections to that amount, in which case UNDP may effect payment for the amount so corrected. The Engineer may also withhold invoices if the work is not performed at any time in accordance with the terms of the Contract or if the necessary insurance policies or performance security are not valid and/or in order. The Engineer shall

process the invoices submitted by the Contractor within 10 days of their receipt, when no objections for the performed works exist.

- 3.5 Payments effected by UNDP to the Contractor shall be deemed neither to relieve the Contractor of its obligations under this Contract nor as acceptance by UNDP of the Contractor's performance of the Works.
- 3.6 Payment of the final invoice shall be effected by UNDP after issuance of the Certificate of Final Completion by the Engineer.
- 3.7 The final price of the Contract will be determined on the basis of the actual quantities of work and materials utilized in the complete and satisfactory performance of the Works as certified by the Engineer and the unit prices contained in the Contractor's financial proposal. Such unit prices are fixed and are not subject to any variation whatsoever.
- 3.8 If the Contractor foresees that the final price of the Contract may exceed the total estimated price contained in 3.1 above, he shall so inform the Engineer without delay, in order for UNDP to decide, at its discretion, to increase the estimated price of the Contract as a result of a larger quantity of work/material or to reduce the quantity of work to be performed or materials to be used. UNDP shall not be responsible for payment of any amount in excess of that stipulated in 3.1 above unless this latter amount has been increased by means of a written amendment of this Contract in accordance with its paragraph 8 below.

4. Special conditions

- 4.1 The Performance Security (Bank Guarantee, as per Section 6, FORM H: Form for Performance Security) referred to in Clause 10 of the General Conditions shall be equal to 10% of the contract amount and be submitted as per point 3.3 of this contract.
- 4.2 The Contractor will provide **minimum 3-year warranty on works and materials, 5-year warranty on equipment.**
- 4.3 According to Clause 45 of the General Conditions, the liquidated damages for delay shall be 0.25% of the price of the Contract per day of delay, up to a maximum of 30 days of the final price of the Contract, after which UNDP may terminate the contract.

5. Submission of invoices

- 5.1 One original and one copy of every invoice shall be submitted by mail by the Contractor for each payment under the Contract to the Engineer's address specified in clause 8.2.
- 5.2 Invoices submitted by fax shall not be accepted by UNDP.

6. Time and manner of payment

6.1 Invoices shall be paid within thirty (30) days of the date of their receipt and acceptance by UNDP.

6.2 All payments shall be made by UNDP to the following Bank account of the Contractor:

Bank Name: BC „MOLDOVA-AGROINDBANK” SA, Chisinau Branch #6

Bank Code: C/B AGRNMD2X413

IBAN: MD40AG000000022512217993

Contractor Fiscal Code: 1005600037219

7. Modifications

7.1 Any modification to this Contract shall require an amendment in writing between both parties duly signed by the authorized representatives of the Contractor and UNDP.

8. Notifications

8.1 For the purpose of notifications under the Contract, the addresses of UNDP and the Contractor are as follows:

For the UNDP:

Viorel ALBU, MIA Project Manager

Address: 75, Stefan cel Mare blvd., Chisinau MD, Moldova

Tel.: (+373) 69 182 848

E-mail: viorel.albu@undp.org

For the Contractor:

Sergiu CIOBANU, Director of Prestigiu-AZ SRL

Address 1: Straseni R-n, Sireti village, Moldova

Address 2: 1, Mesterul Manole Str., Chisinau MD2036, Moldova

Tel.: (+373) 022 009 500; (+373) 68 882 020

E-mail: prestigiu@mail.ru

8.2 For the purposes of communications with the Engineer, the contact details of the Engineer shall be as follows:

Oleg Afanasii, Engineer

Tel.: (+373) 69 830 010

E-mail: o_afanasii@yahoo.com

If the above terms and conditions meet with your agreement as typed in this letter and in the Contract Documents, please initial every page of this letter and its attachments and return to this office one original of this Contract, duly signed and dated.



Yours sincerely,

Dima Al-Khatib

21-Dec-2020

Dima AL-KHATIB,
UNDP Resident Representative

For Prestigiu-AZ SRL

Agreed and Accepted:

Signature _____

Name: Sergiu CIOBANU

Title: Director

Date _____



PROCES-VERBAL DE RECEPȚIE LA TERMINAREA LUCRĂRILOR

Nr. 1 din 18.05.2022

privind lucrările de reconstruire executate la obiectul Modernizarea bazinului "Dinamo" din str. Gh. Asachi 23a în cadrul contractelor nr. ITB18/01769 din 23.08.2018 încheiat între "Sport Play Systems" SRL și PNUD Moldova, nr. ITB19/01942 din 17.09.2019 încheiat între "Giesena" SRL și PNUD Moldova, nr. ITB20/02152 din 21.12.2020 încheiat între "Prestigiu AZ" SRL și PNUD Moldova, și acordurile de finanțare încheiate între PNUD Moldova și CSC "Dinamo" pentru lucrările de Modernizarea bazinului "Dinamo" din str. Gh. Asachi 23a.

1. Lucrările au fost executate în baza autorizațiilor nr. 582-c/18 din 19.10.2018, nr. 423-e/19 din 16.08.2019, nr. 43-c/21 din 22.02.2021, eliberate de Primăria un. Chișinău, cu valabilitate până la 22.01.2022.

2. Comisia de recepție și-a desfășurat activitatea în intervalul lunii mai 2022, fiind formată din:

Președinte:

Ilie Ceban – Viceprimar mun. Chișinău

Membrii:

Vladimir Răducan – Șef CCFS al CSC "Dinamo"

Sergiu Buzenco – Șef SAD a CSC "Dinamo", atestat Responsabil Tehnic

Iulian Coșcodan – Inginer SAD a CSC "Dinamo", atestat Diriginte de Șantier

Iurie Gromatchi – Responsabil Tehnic PNUD Moldova

Oleg Afanasii – inginer construcții civile, consultantul proiectului PNUD

Viorel Albu – managerul proiectului PNUD

3. Au mai participat la recepție:

Ion Strelețchi – Diriginte de șantier "Prestigiu AZ" SRL

Mihai Balaș – Director "Sport Play Systems" SRL

Simion Gutan – Director "Giesena" SRL

Vasilii Ambrozeac – Arhitect „Bim-Tech Solution” SRL

Vasile Vîrlan – Proiectant „Apean Proiect” SRL

4. Constatările comisiei de recepție:

1) din documentația scrisă și desenată, care trebuia prezentată, au lipsit sau sînt incomplete piesele cuprinse în lista-anexă nr. 1:

2) lucrările cuprinse în lista-anexă nr. 2 nu au fost executate;

3) în lucrările, cuprinse în lista-anexă nr. 3, nu s-au respectat prevederile proiectului.

5. Comisia de recepție, în urma constatărilor făcute, propune:

Recepția la terminarea lucrărilor de construcție și montaj conform proiectului de execuție

6. Comisia de recepție motivează propunerea făcută prin:

Terminarea integral a volumelor de lucrări prevăzute în proiect. Obiectivul este pregătit și adaptat pentru exploatare conform destinației

7. Comisia de recepție recomandă următoarele:

Se receptionează lucrările de reconstruire executate la obiectul Modernizarea bazinului "Dinamo" din str. Gh. Asachi 23a

7¹. Descrierea obiectului recomandat spre recepție:

Obiectul cu numărul cadastral 0100213.011.02, adresa poștală mun. Chișinău, str. Gheorghe Asachi 23a, destinația Construcție sportivă, compus din următoarele construcții: Clădirea bazinului litera B, suprafața la sol 1030.2 m², suprafața totală, 969.2 m², numărul de etaje 2, conform certificatului despre rezultatele inspecției bunului imobil, anexat la prezentul proces-verbal.

8. Prezentul proces-verbal, conținând 2 file și 3 anexe numerotate, cu un total de 5 file, a fost încheiat astăzi 18.05.2022 la str. Gh. Asachi 23a în 8 exemplare

Comisia de recepție:

Președinte: Ilie Ceban

Membri: Vladimir Răducan

Sergiu Buzenco

Iulian Coșcodan

Iurie Gromatchi

Oleg Afanasii

Viorel Albu

9. Concluzia Agenției pentru Supraveghere Tehnică:

Conform actului de inspecție nr. 428/22 din 17.05.2022, se acceptă recepția la terminarea lucrărilor și volumul lucrărilor plus la recepția finală

10. Lucrarea Modernizarea bazinului "Dinamo" din str. Gh. Asachi 23a este:

TRANSMISĂ:

EXECUTANTUL:

" " 2022

L.Ș.

(semnătură)

PRIMITĂ:

RECEPȚIORUL:

" " 2022

L.Ș.

(semnătură)

CONFIDENTIAL

CONTRACT NO. EUCOM/#15JPSS20D00000035

by and between the

GOLDEN WEST HUMANITARIAN FOUNDATION

and

PRESTIGIU-AZ

for

**ENGINEERING SERVICES AT THE MOLDOVA AMMUNITION &
EXPLOSIVES STORAGE AREAS, FLORESTI AND CAHUL**

CONFIDENTIAL

Page 1 of 19

TABLE OF CONTENTS

ARTICLE 1. CONTRACT DOCUMENTS AND SCOPE OF WORK.....	3
ARTICLE 2. DEFINITIONS.....	3
ARTICLE 3. SIGNATURE REQUIRED.....	4
ARTICLE 4. CONTRACT ADMINISTRATION.....	4
ARTICLE 5. CONTRACTOR'S RESPONSIBILITY.....	6
ARTICLE 7. CONTRACT PRICE.....	6
ARTICLE 8. PROGRESS PAYMENTS.....	6
ARTICLE 9. SUBSTANTIAL COMPLETION.....	7
ARTICLE 10. CHANGES AND MODIFICATIONS.....	7
ARTICLE 11. TIME EXTENSIONS AND LIQUIDATED DAMAGES.....	8
ARTICLE 13. FINAL INSPECTION.....	8
ARTICLE 14. FINAL PAYMENT.....	9
ARTICLE 15. WARRANTY.....	9
ARTICLE 17. INDEMNIFICATION.....	11
ARTICLE 18. SUSPENSION OF WORK.....	11
ARTICLE 19. TERMINATION FOR CONVENIENCE.....	11
ARTICLE 20. TERMINATION FOR DEFAULT.....	12
ARTICLE 21. DISPUTES.....	12
ARTICLE 22. CONSEQUENTIAL DAMAGES.....	13
ARTICLE 23. SAFETY.....	13
ARTICLE 24. OWNERSHIP RIGHTS AND OWNER PROPERTY.....	13
ARTICLE 25. AUDIT.....	14
ARTICLE 26. CONFIDENTIALITY.....	14
ARTICLE 27. OWNER NAME/LOGO.....	15
ARTICLE 28. CLOSE RELATIVES.....	15
ARTICLE 29. PROCUREMENT INTEGRITY.....	15
ARTICLE 30. BACKGROUND INVESTIGATION.....	16
ARTICLE 31. ASSIGNMENT.....	16
ARTICLE 32. ENVIRONMENTAL.....	16
ARTICLE 33. DIVERSITY.....	16
ARTICLE 34. CHILD LABOR.....	17
ARTICLE 35. FAIR LABOR STANDARDS.....	17
ARTICLE 36. PUBLIC HEALTH PLANS AND CONTINGENCY.....	17
ARTICLE 37. FORCE MAJEURE.....	17
ARTICLE 38. SEVERABILITY.....	17
ARTICLE 39. LANGUAGE.....	17
ARTICLE 40. CONFLICTS OF LAW.....	18
ARTICLE 41. PRESERVATION OF IMMUNITIES.....	18
ARTICLE 43. NOTICES.....	18
ARTICLE 44. ENTIRE CONTRACT.....	Error! Bookmark not defined.
Signatures.....	Error! Bookmark not defined.

CONTRACT NO. EUCOM/P010247335

This Contract is made this 15th day of October in the year 2021 by and between the Golden West Humanitarian Foundation (hereinafter referred to as the "Owner"), having its principal office at 6355 Topanga Canyon Blvd, Suite 517, Woodland Hills, CA 91367, United States of America, and Prestigiu-AZ (hereinafter referred to as the "Contractor"), a corporation incorporated under the laws of the state of Moldova having a principal place of business at Chisinau, Moldova.

WHEREAS the Owner is desirous that certain works should be executed by Contractor, viz Reconstruction of The Moldova Ammunition and Explosives Storage Areas, Floresti and Cahul, Moldova and has accepted an offer by the Contractor for the execution and completion of such services.

NOW IT IS HEREBY AGREED:

ARTICLE 1. CONTRACT DOCUMENTS AND SCOPE OF WORK

1.1 The Contract Documents shall consist of:

- (a) This Contract;
- (b) SOW & Price Schedule as detailed in Annex A
- (c) Time and Materials Breakdown in Annex B

1.2 Contractor shall perform all the construction and services required by, reasonably implied by, and reasonably inferable from the Contract Documents, including but not limited to all labor, materials, equipment, services, construction management and coordination of project requirements provided or to be provided by the Contractor to fulfill Contractor's obligations under the Contract Documents (collectively referred to herein as the "Work").

ARTICLE 2. DEFINITIONS

2.1 The following terms, whenever used in this Contract, shall have the following meaning:

- (a) "Chief Finance Officer" means the Chief of Finance, Golden West Humanitarian Foundation.
- (b) "Contract" means this Contract between the Owner and the Contractor.
- (c) "Contract Price" means the sum to be paid Contractor for the performance of the Work, as such sum may be adjusted pursuant to the terms of the Contract Documents.
- (d) "Contractor" means the company, consulting firm, or individual who has contracted with the Owner to perform the Work.
- (e) "Contractor Representative" or "CR" shall mean the official of the Contractor referred to in Article 4 (Contract Administration) of this Contract.
- (f) "Force Majeure Event" means an event which is beyond the reasonable control of a Party, and which makes a Party's performance of its obligations hereunder impossible or so impractical as reasonably to be considered impossible in the circumstances, and includes, but is not limited to, war, riots, civil disorder, earthquake, fire, explosion, storm, flood or other exceptionally adverse weather conditions, strikes, lockouts or other industrial action (except where such strikes, lockouts or other industrial actions are within the power of the Party invoking Force Majeure to prevent), confiscation or any other action by government agencies. Force Majeure Events shall not be deemed to include: (i) any event which is caused by the negligence or intentional action of a Party or such Party's consultants, agents or employees; (ii) any event which a diligent Party could reasonably have been expected to both: (A) take into account at the time this contract was entered into; and (B) avoid or overcome in the carrying out of its obligations hereunder; or (iii) the insufficiency of funds, inability to make any payment required under this Contract, or any economic conditions, including but not limited to inflation, price escalations, or labor availability.
- (g) "Owner" means the Golden West Humanitarian Foundation, headquartered in 6355 Topanga Canyon Blvd, Suite 517, Woodland Hills, CA 91367, United States of America.
- (h) "Owner's Project Manager" or "Owner's PM" shall mean the official of the Owner referred to in Article 4 (Contract Administration) of this Contract.
- (i) "Subcontract" means any agreement by Contractor with any contractor, vendor, supplier, consultant, or other entity or person to furnish or perform a portion of the Work, as well as any agreements between a

CONFIDENTIAL

Page 3 of 19

Subcontractor and its lower tier contractors, vendors, suppliers, consultants, or other entities or persons.

- (j) "Subcontractor" means any person or entity that has entered into a Subcontract to furnish or perform any part of the Work.
- (k) "Substantial Completion" or "Substantially Complete" shall have the meanings set forth in Article 9 (Substantial Completion) of this Contract.
- (l) "Work" shall have the meaning set forth in Article 1 (Contract Documents and Scope of Work) above.

ARTICLE 3. SIGNATURE REQUIRED

3.01 This Contract shall not become binding unless and until signed by the Purchaser's Authorized Representative and the Contractor's Authorized Representative.

ARTICLE 4. CONTRACT ADMINISTRATION

4.1 Owner designates Mr. Simon Morton as the Owner's Project Manager (Owner's PM) for this Contract who shall monitor administration and completion of the Contract according to its terms and conditions as described below:

- (a) The Owner's PM will be the Owner's authorized representative during construction and shall be responsible for the coordination of activities between the Owner and the Contractor under this Contract.
- (b) The Owner's PM will visit the site at such intervals as are appropriate to the stage of construction to become familiar generally with the progress and quality of the completed Work so as to enable him/her to determine in general if the Contractor is performing the Work in such a manner that, when completed, will be in accordance with the Contract Documents.
- (c) The Owner's PM will receive all communications of whatever nature which the Contractor is obligated to submit to the Owner under this Contract, including but not limited to changes to the Contract Documents involving the quality level, Statement of Work, price, rates, delivery and/or completion dates/schedules, Subcontractor, or key personnel changes.
- (d) The Owner's PM also is responsible for receiving and approving the Contractor's invoices for payment and accepting the Work and/or deliverables on behalf of the Owner.
- (e) The Owner's PM's responsibilities include but are not limited to receiving and approving the Contractor's invoices for payment, and accepting the Work and/or deliverables on behalf of the Owner. The Owner's PM may request a change; however, the Owner's PM does not have the authority to issue a change to the Contract Price, Scheduled Substantial Completion Date, or rates. Such changes must be made in accordance with Article 10 (Changes and Modifications).

4.2 Contractor designates Elena Bumbac-Ciobanu as the Contractor's Representative (CR) who shall be responsible for the coordination of all Contract activities between the Owner and the Contractor under this Contract. In this capacity, his/her responsibilities include but are not limited to daily supervision and oversight of the Work and all communications between the Contractor and the Owner. The CR has the authority to agree to a change to the Work, Contract Price, Scheduled Substantial Completion Date, and rates.

ARTICLE 5. CONTRACTOR'S RESPONSIBILITY

5.1 Contractor shall supervise and direct the Work, using Contractor's best skill and attention. Contractor shall be solely responsible for and have control over construction means, methods, techniques, sequences and procedures and for coordinating all portions of the Work.

5.2 Contractor shall be responsible to the Owner for acts and omissions of Contractor, Subcontractors, anyone employed directly or indirectly by any of them or anyone for whose acts any of them may be liable.

5.3 Contractor shall provide and pay for labor, materials, equipment, tools, construction equipment and machinery, transportation, and other facilities and services necessary for proper execution and completion of the Work.

5.4 Where applicable, Contractor shall preserve and protect all vegetation (trees, shrubs, plantings), removing only such vegetation as authorized and/or directed by the Owner (as specified in the Contract Documents). Contractor shall take precautions, as needed, to avoid damaging existing utilities, facilities and improvements.

5.5 Contractor shall provide continuous on-site supervision during the entire construction period.

ARTICLE 7. CONTRACT PRICE

7.1 The Owner hereby covenants to pay the Contractor in consideration of the execution and completion of the Work and remedying of defects therein the Contract Price of USD 515,811.16 (Five Hundred and Fifteen Thousand, Eight Hundred and Eleven United States Dollars and Sixteen Cents) or such other sums as may become payable under the provisions of the Contract at the times and in the manner prescribed by the Contract.

ARTICLE 8. PROGRESS PAYMENTS

8.1 Contractor shall be paid 10% of the Contract Price as mobilization payment upon signing of the Contract and submission to the Owner of: (a) acceptable insurance certificates, as required by Article 16 (Insurance). The mobilization payment shall amount to USD 51,581.12 (Fifty One Thousand Five Hundred and Eighty One United States Dollars and Twelve Cents).

8.2 Based upon invoices submitted by Contractor on the last day of the month, the Owner shall make progress payments on account of the Contract Price to Contractor as provided in the Contract Documents for the milestones ending as follows:

(a) Not later than thirty (30) days following the completion of the security doors, CCTV and perimeter lighting, a progress payment of USD 257,905.58 (Two Hundred and Fifty Seven Thousand, Nine Hundred and Five United States Dollars and Fifty Eight Cents), shall be paid.

(b) Upon Substantial Completion of the entire Work, a sum sufficient to increase the total payments to one hundred (100) percent of the Contract Price, less such amounts as the Owner's PM shall determine for all incomplete Work and unsettled claims as provided in the Contract Documents, shall be paid.

8.3 Application for payment should be presented in a format approved by the Owner's PM in support of the milestones achieved. Such application may not include requests for payment of amount Contractor does not intend to pay to a Subcontractor because of a dispute or other reason.

8.4 Owner shall have the right to deduct from any application for payment monies accruing for liquidated damages, as well as any other monetary claim that the Owner has against Contractor.

Contractor shall submit invoices to the Chief Finance Officer (CFO), Golden West Humanitarian Foundation. Email: mike.troiano@goldenwesthf.org with a duplicate to the Owner's PM. Email: simon.morton@goldenwesthf.org

8.5 Invoices, in duplicate, shall contain the following information:

- (a) Contract No. FUCOM/15/IPSS20D00000035
- (b) Work activity presented in accordance with the approved format.
- (c) Payment advice, including wire transfer information

8.6 Each invoice shall be accompanied by such data as the Owner may require to substantiate Contractor's right to payment, such as copies of invoices and requisitions from Subcontractors.

8.7 Contractor warrants that title to all Contract Deliverables covered by an invoice will pass to the Owner on

the earlier of incorporation into the Project or the time of payment. Contractor further warrants that it shall bear the risk of loss or damage of the Work at all times prior to Substantial Completion. Contractor shall represent and warrant in all invoices that all completed Contract Deliverables shall be free and clear of all liens, claims, security interests or encumbrances in favor of Contractor, subcontractors, material suppliers, or other persons or entities making a claim by reason of having provided labor, materials and equipment relating to the Work.

8.8 The Owner is immune from the payment of import duties, sales, use and excise taxes and the Moldova Ministry of Defence shall provide the Contractor with evidence of such tax exemption certification upon request. Contractor authorizes the Owner to deduct from any invoice presented in connection with this Contract any allocation for duties or taxes, without prior notice to Contractor and without cost to the Owner. Payment of such corrected invoiced amount shall constitute full payment by the Owner.

8.9 Points of contact for Tax exemption shall be: Lt. Col. Oleg Pulbere

oleg.pulbere@army.md

8.10 Contractor and all Subcontractor(s) shall use reasonable efforts to ensure that funds paid to Contractor and Subcontractor(s) by the Purchaser are not used to finance, support or conduct terrorism.

ARTICLE 9. SUBSTANTIAL COMPLETION

9.1 Contractor shall commence performance of the Work under this Contract by the date of this signed contract ("Contract Commencement Date") and Substantially Complete the Work no later than 31 May 2022 ("Scheduled Substantial Completion Date"), as such date may be extended pursuant to the terms of the Contract Documents. Substantial Completion is the stage in the progress of the Work when there is sufficient completion to allow beneficial use by the Owner. The Owner's occupancy or use of any portion of the Work or Work site shall not constitute the Owner's acceptance of any Work which is not in accordance with the requirements of the Contract Documents, nor relieve Contractor from: (a) its obligation to complete the Work; (b) responsibility for loss or damage due to or arising out of defects in, or malfunctioning of the Work; nor (c) from any other unfulfilled obligations or responsibilities under the Contract Documents.

9.2 Within ten (10) calendar days after the Contract Commencement Date, Contractor shall provide a detailed schedule of Work to the Owner's PM for review and acceptance, in writing.

ARTICLE 10. CHANGES AND MODIFICATIONS

10.1 The Owner may, at any time and without notice to the sureties (if any), by written order designated or indicated to be a change order, make changes in the Work within the general scope of the Contract, including changes in:

- (a) the Specifications, including plans, drawings and designs;
- (b) the method or manner of performance of the Work;
- (c) the Owner furnished facilities, equipment, materials, services or site;
- (d) directing acceleration in the performance of the Work;
- (e) the method of shipping or packing; or
- (f) the date or place of delivery, performance or completion.

10.2 If Contractor receives any other written or oral order from the Owner's staff, representatives, Project Office or Owner's Project Manager (which includes instruction, interpretation, or determination) that Contractor believes causes a change or that otherwise may impact the Contract Price or Scheduled Substantial Completion Date, Contractor must give the Owner written notice within seven (7) business days of such written or oral order stating

- (a) the date, circumstance and source of the change; and
- (b) that the Contractor regards the order as a change to the Contract. The Chief, Corporate Procurement Unit, shall respond in writing to Contractor's notice in a timely manner. It is expressly understood that, except as provided in this Section, no order, statement or conduct of the Owner staff or its representatives shall be a change to this Contract or entitle Contractor to an equitable adjustment in the Contract Price or Scheduled Substantial Completion Date. The failure to comply with the seven (7) day notice above shall be a waiver of Contractor's right to claim an equitable adjustment.

10.3 If any change under this Article causes an increase or decrease in Contractor's cost of, or the time required

for the performance of any part of the Work under this Contract, whether or not changed by any such order, the Chief Corporate Procurement Unit shall make an equitable adjustment in the Contract Price and/or Scheduled Substantial Completion Date and modify the Contract, in writing. However, except for an adjustment based on defective specifications, no adjustment in the Contract Price shall be made for any costs incurred more than seven (7) days before Contractor gives written notice as required in Section 10.02 above. In the case of defective specifications for which the Owner is responsible, the equitable adjustment shall include any increased cost reasonably incurred by Contractor in an attempt to comply with the defective specifications.

10.4 Within thirty (30) days of the earlier of: (a) receipt of the Owner's written response to the notice under Section 10.02 above; or (b) receipt of the Procurement Representative's determination based upon Contractor's notification under Section 10.02 above, Contractor must submit a written statement describing a detailed description of the changes and the amount of any claimed impact to adjustment of the Contract Price and/or Scheduled Substantial Completion Date. Contractor may include this statement in its notice under Section 10.02 above. However, no adjustment for any change under Section 10.02 above shall be made for any costs incurred more than seven (7) days before Contractor gives written notice as required. Failure to submit such a statement within the thirty (30) day limit specified herein shall be deemed a waiver of the Contractor's right to an equitable adjustment. No proposal by Contractor for equitable adjustment shall be allowed if asserted after final payment under this Contract.

10.5 The failure of Owner and Contractor to agree to any adjustment hereunder, including any claims as to the entitlement of an adjustment, or any disputed amount of the increase in the Contract Price or Scheduled Substantial Completion Date, shall be a dispute to be resolved in accordance with Article 21 (Disputes). Unless directed otherwise by Owner, Contractor shall have the duty to diligently proceed with the Work in accordance with Owner's instructions pending the resolution of the dispute, and nothing in these Contract Documents shall excuse Contractor from proceeding diligently with the Contract.

ARTICLE 11. TIME EXTENSIONS AND LIQUIDATED DAMAGES

11.1 If Contractor is delayed in the performance of the Work due to acts, omissions, conditions, events, or circumstances beyond its control and due to no fault of its own or those for whom Contractor is responsible, the Scheduled Substantial Completion Date shall be reasonably extended provided, however, that Contractor can demonstrate that: (a) such events have or will delay the critical path and the Scheduled Substantial Completion Date; (b) it has complied with the notice and submission requirements set forth in Section 11.02 below; and (c) Contractor, in view of all the circumstances, has exercised reasonable efforts to avoid and mitigate the delay. By way of example, events that will entitle Contractor to such an extension include acts or omissions of Owner or anyone under Owner's control, changes in the Work, and Force Majeure Events.

11.2 Contractor shall, within seven (7) calendar days after encountering the above events which cause delay to the Work, submit to the Owner in writing a notification describing such events in reasonable detail, as well as the nature and cause of the event and its expected duration and impact on the performance of the Contract. Contractor shall, within fourteen (14) calendar days of the preceding notification, provide Owner with a time impact analysis to establish the specific basis for its request for time extension to the Scheduled Substantial Completion Date, as well as evidence supporting any claimed increase in the Contract Price arising from the event. Failure by Contractor to comply with these requirements shall constitute a waiver by Contractor of any claim.

11.3 Contractor expressly waives its right to recover any damages for delay to the Scheduled Substantial Completion Date caused by any Force Majeure Event, with the understanding that its sole remedy shall be an extension of the Scheduled Substantial Completion Date.

11.4 If Contractor fails to achieve Substantial Completion on or before the Scheduled Substantial Completion Date, the actual damage to the Owner will be difficult or impossible to determine. Therefore, in lieu of actual damages, Contractor shall pay to the Owner fixed liquidated damages, for each calendar day of delay beyond the Scheduled Substantial Completion Date, the sum of USD 500.00 per day so delayed subject to maximum limit of USD 25,000.00 or 50 days beyond the date for Substantial Completion. Owner shall have the right to set-off such liquidated damages from any payments due, or that may become due, to Contractor hereunder.

ARTICLE 13. FINAL INSPECTION

13.1 When all of the Work is complete, Contractor shall notify the Owner in writing so that the Owner may conduct a final inspection and, if required, prepare a punch list stating all deficient items which are to be corrected promptly by the Contractor.

13.2 The Owner will conduct its final inspection within a reasonable time after notification by Contractor. A punch list will be prepared as a result of such final inspection, the Owner shall provide to Contractor in a timely manner two (2) copies of the punch list.

13.3 Contractor, at its sole cost and expense, will correct all punch list items, return one copy of the punch list with corrections initialed, and contact the Owner when ready for re-inspection. The Owner shall notify Contractor of the re-inspection date. The Owner will not consider the Work eligible for acceptance and final payment until all punch list items have been corrected and approved by the Owner.

ARTICLE 14. FINAL PAYMENT

14.01 Final payment shall be paid by the Owner to Contractor when the Work has been fully completed and finally inspected, the Contract fully performed, a final invoice has been approved by the Owner's PM, and Contractor has submitted to the Owner each of the following: (a) an affidavit that all payrolls, bills for materials and equipment, and other indebtedness connected with the Work for which the Owner or its property might in any way be responsible or encumbered, have been paid or otherwise satisfied; (b) consent of surety, if any, to final payment; (c) all Drawings, approved Shop Drawings, Product Data and Samples required by this Contract to be delivered by Contractor to the Owner; and (d) if required by the Owner, other data establishing payment or satisfaction of all such obligations, such as receipts, releases and waivers of liens, claims, security interests or encumbrances arising out of the Contract, to the extent and in such form as may be required by the Owner. If any Subcontractor refuses to furnish a release or waiver required by the Owner, Contractor may furnish a bond satisfactory to the Owner to indemnify it against any such lien. If any such lien remains unsatisfied after all payments are made, Contractor shall refund to the Owner all money that the latter may be compelled to pay in discharging such lien, including all costs and attorney's fees.

ARTICLE 15. WARRANTY

15.1 Contractor warrants that the Work:

- (a) is in conformance with the requirements of the Contract Documents;
- (b) is of good quality and new, unless otherwise required or permitted by the Contract Documents;
- (c) is free of any defect in equipment, material, or design furnished, or workmanship, whether performed by Contractor or any Subcontractor; and
- (d) is in accordance with all construction principles, practices and methods generally accepted as standards of the industry for projects similar in nature, size and complexity to this Project.

15.2 If required by the Owner, Contractor shall furnish satisfactory evidence as to the kind and quality of materials and equipment provided in performance of the Work.

15.3 Work not conforming to the warranty set forth in Section 15.01 above, including substitutions not properly approved and authorized by the Owner, may be considered defective by the Owner. In such case, the Owner has the right to reject the materials or equipment or to terminate the Contract for default and without prejudice to any other rights the Owner may have arising from such breach. Alternatively, the Owner may allow Contractor to repair, replace or rework the non-conforming Work at the Owner's option, or to retain the Work in accordance Section 15.13 below. In such event, the Owner's continued use shall not be deemed a waiver of Contractor's breach of warranty.

15.4 If, during the period of one (1) year from the date of Substantial Completion of the Work, or, if the Owner takes possession of any part of the Work prior to Substantial Completion, for the period of one (1) year from the date the Owner takes possession, any Work is found to be in violation of the above-referenced warranty or otherwise defective, Contractor shall remedy, at Contractor's expense, any such violation or defect. In addition, Contractor shall remedy at Contractor's expense any damage to the Owner owned or controlled real or personal property when that damage is the result of:

- (a) Contractor's failure to conform to the requirements of the Contract Documents; or
- (b) Any defect of equipment, material, workmanship or design furnished.

15.5 Contractor shall restore any Work damaged in fulfilling the terms and conditions of this Article. For any Work so remedied or corrected by Contractor, Contractor agrees that its obligation to remedy and correct shall be extended for one (1) year from the date of repair or replacement.

15.6 The Owner shall notify Contractor, in writing, within a reasonable time after the discovery of any failure,

defect or damage.

15.7 If Contractor fails to remedy any failure, defect or damage within a reasonable time after receipt of notice, the Owner shall have the right to replace, repair, or otherwise remedy the failure, defect or damage at Contractor's expense.

15.8 With respect to all warranties, express or implied, from Subcontractors for Work performed and furnished under this Contract, Contractor shall:

- (a) Obtain all warranties that would be given in normal commercial practice;
- (b) Require all warranties be executed, in writing, for the benefit of the Owner, if so directed in this Contract or by the Owner; and
- (c) Enforce all warranties for the benefit of the Owner, if so directed by the Owner.

15.9 The Owner may directly enforce any Subcontractor's warranty, including bringing suit against the Subcontractor.

15.10 Unless a defect is caused by the negligence of Contractor or a Subcontractor, Contractor shall not be liable for the repair of any defects of material or design furnished by the Owner or for the repair of any damage that result from any defect in Owner-furnished material or design.

15.11 The warranties and rights under this Article shall not limit the Owner's rights under Article 13 (Final Inspection) with respect to latent defects, gross mistakes, or fraud.

15.12 Nothing contained in this Article shall be construed to establish a period of limitation with respect to other obligations which Contractor might have under the Contract Documents. Establishment of the time period of one year as described in this Article relates only to the specific obligation of Contractor to correct the Work, and has no relationship to the time within which the obligation to comply with the Contract Documents may be sought to be enforced, nor to the time within which proceedings may be commenced to establish Contractor's liability with respect to Contractor's obligations other than specifically to correct the Work.

15.13 If the Owner prefers to accept Work which is not in accordance with the requirements of the Contract Documents, the Owner may do so instead of requiring its removal and correction, in which case the Contract Price will be reduced as appropriate and equitable. Such adjustment shall be affected whether or not final payment has been made.

ARTICLE 16. INSURANCE

During the term of this Contract, Contractor agrees to secure and maintain in effect, at its own expense, the following minimum insurances.

- 1) Provide **Workers Compensation Coverage and Employer's Liability Coverage** per Moldovan Law.
- 2) Provide **Commercial General Liability Coverage** (aka Public Liability Coverage) for third party bodily injury and property damage, including products and completed operations, contractual liability, and independent contractors' liability with limits not less than \$1,000,000 per occurrence and \$2,000,000 in the aggregate.

This General Liability Policy should be endorsed to list the following companies as Additional Insured:
-Golden West Humanitarian Foundation, 6355 Topanga Canyon Bl, #517, Woodland Hills, CA 91367 USA
-PAE Government Services Inc, 1320 N. Courthouse Road, Suite 700, Arlington, VA 22201 USA

- 3) Provide **Commercial Automobile Liability Coverage** for use of all owned, non-owned, and hired vehicles with limits of not less than \$1,000,000 per accident combined single limit for bodily injury and property damage liability.

This Commercial Automobile Policy should be endorsed to list the following companies as Additional Insured:
-Golden West Humanitarian Foundation, 6355 Topanga Canyon Bl, #517, Woodland Hills, CA 91367 USA
-PAE Government Services Inc, 1320 N. Courthouse Road, Suite 700, Arlington, VA 22201 USA

Contractor shall provide the Owner with certificates of insurance for these coverages within seven (7) calendar days of execution of this Contract. Said certificates shall provide for a thirty (30) day cancellation notice from the insurer(s) on

all coverages with a copy of such cancellation notice to be sent directly to the Owner from the insurer(s). Contractor shall also promptly provide the Owner with new certificates of insurance upon renewal of or material changes in each insurance policy. Contractor shall cause its liability Insurance Provider(s) to name the Owner (Golden West Humanitarian Foundation) as an additional insured, as its interest may appear with respect to the Contract. Provision of Certificates of Insurance is a condition precedent to payment under this Contract.

Contractor shall obligate and be responsible for all of its Subcontractors providing similar coverages and shall obtain from them certificates of insurance which shall be placed on file and made available for Owner examination. In any event, Contractor shall be liable to the Owner for any damages due to performance of any Subcontractor.

ARTICLE 17. INDEMNIFICATION

17.1 To the fullest extent permitted by law, Contractor agrees to indemnify and hold harmless the Owner, its officers, directors, employees and agents from and against all claims, suits, damages and losses, including reasonable attorneys' fees and expenses, that are due to:

- (a) bodily injury, sickness or death, or property damage or destruction (other than the Work itself), to the extent resulting from the negligent or wrongful acts or omissions of, or failure to comply with the Contract Documents by, Contractor, Subcontractors, anyone employed directly or indirectly by any of them or anyone for whose acts any of them may be liable;
- (b) violation of any intellectual property rights of third parties, including without limitation rights relating to patents, trademarks, copyrights, or trade secrets, by Contractor, Subcontractors, anyone employed directly or indirectly by any of them, or anyone for whose acts any of them may be liable;
- (c) compensation for claims covered by Contractor's Workers' Compensation insurance; or
- (d) violations of the obligations set forth in Article 34 (Child Labor) and/or Article 35 (Fair Labor Standards).

17.2 If an employee of Contractor, Subcontractors, anyone employed directly or indirectly by any of them or anyone for whose acts any of them may be liable has a claim against Owner, its officers, directors, employees, or agents, Contractor's indemnity obligations shall not be limited by any limitation on the amount of damages, compensation or benefits payable by or for Contractor, Subcontractors, or other entity under any employee benefit acts, including workers' compensation or disability acts.

17.3 The obligation set out in this Article shall survive the expiration or termination of this Contract.

ARTICLE 18. SUSPENSION OF WORK

18.1 The Owner may order Contractor, by written notice, to suspend, delay or interrupt all or any part of the Work for the period of time that the Owner determines appropriate for the convenience of the Owner.

18.2 If this suspension, delay or interruption is unreasonable in duration, the Owner shall modify the Contract accordingly to adjust for any change to the Contract Price or Scheduled Substantial Completion Date, caused by the Owner's action or inaction in unreasonably suspending, delaying or interrupting the Work, provided, however, that under no circumstances will Contractor be entitled to claim any profit for a suspension. No adjustment will be made for any suspension, delay or interruption to the extent that performance would have been so suspended, delayed or interrupted by any other cause, including the fault or negligence of Contractor, or suspensions arising from Contractor's failure to abide by its safety obligations hereunder.

18.3 A request for adjustment under this Article shall not be allowed: (a) for any costs incurred more than twenty (20) days before Contractor notifies the Owner in writing of the Owner's act or failure to act that allegedly caused the suspension, delay or interruption involved; and (b) unless the request, in an amount stated, is asserted in writing within seven (7) days after the end of the suspension, delay or interruption.

ARTICLE 19. TERMINATION FOR CONVENIENCE

19.1 The Owner may terminate the Contract in whole or in part at any time if Owner determines, in its sole and absolute discretion, that a termination is in its best interests. Owner shall effect the termination by sending written notice of such termination to Contractor, which notice shall state that termination is for the Owner's convenience, the extent to which performance of services under the Contract is terminated, and the termination date. Unless otherwise instructed by the Owner, Contractor shall stop work immediately on receipt of notice and follow the instructions and directions of Owner.

19.2 In the event of a termination for convenience, Contractor shall be entitled to be paid for Work properly performed by Contractor prior to the effective date of termination, provided, however, that such payment shall not

exceed the total Contract Price after adjustment to account for the price associated with Work not performed. Contractor will also be paid for demobilization costs, termination penalties, and other reasonable wind-down expenses, provided, however, that all such costs, penalties and expenses shall have been unavoidable, actually incurred by Contractor, and directly related to the termination. Contractor shall not be allowed, and expressly waives, payment for profit on Work which was not performed as of the termination date. Under no circumstances shall Contractor be entitled to anticipatory or unearned profits, unabsorbed overhead, opportunity costs or consequential or other damages as a result of a termination for convenience.

ARTICLE 20. TERMINATION FOR DEFAULT

20.1 If Contractor materially fails to prosecute the Work in accordance with the Project schedule or in the manner required by the Contract Documents, or if the Work does not conform, in all respects, to the requirements of the Contract Documents, or Contractor becomes insolvent or unable to meet its payment obligations when due, or breaches any other material obligation of the Contract Documents, the Owner will give Contractor written notice describing the reasons for default and a reasonable opportunity to cure.

20.2 If the Contractor does not cure the default within the period specified, the Owner may, without prejudice to any other rights available to it by law, terminate the Contract for default by written notice, specifying the reason for the default, the portion(s) of the Contract defaulted and the effective date of default.

20.3 Notwithstanding anything herein to the contrary, Owner shall have the right, in its sole discretion, to terminate the Contract for default if Contractor is in breach of any provision of Article 29 (Procurement Integrity), and Owner shall have the right to do so without giving Contractor an opportunity to cure. If Contractor is identified on any terrorist sanctions list recognized by the Owner, including but not limited to the United Nations 1267 sanctions list, the United States Executive Order 13224 sanctions list and the United Kingdom terrorist sanctions list, this Contract shall be subject to immediate termination for default upon written or oral notice to the Contractor. In such case all funds paid to the Contractor shall be returned to the Owner.

20.4 In addition to any other remedy available to the Owner, if, as a result of Contractor's default, the Owner re-procures all or any part of the Work, Contractor shall be liable for all excess costs of re-procurement, including but not limited to reasonable attorneys' fees.

20.5 If Owner fails to pay undisputed amounts owed to Contractor within forty-five (45) days of the date such payment is due under this Contract, and then fails to make such payment within five (5) days following Contractor's delivery to Owner of a written notice of such nonpayment, Contractor shall have the following remedies, which remedies are exclusive:

- (a) Contractor shall be entitled to suspend the Work after delivery of a written notice to Owner. If Contractor claims that the suspension has affected the cost or time of performance, it shall follow the processes set forth in Article 18 (Suspension of Work).
- (b) Contractor shall be entitled to terminate this Contract for default if a suspension for nonpayment continues for more than one hundred eighty (180) consecutive days. The termination shall become effective if, after such 180-day period, Owner fails to cure the nonpayment within twenty (20) days of its receipt of a written notice from Contractor of its intent to terminate. Upon such termination, Contractor shall be entitled to the payment set forth in Article 18 (Suspension of Work). Under no circumstances shall Contractor be entitled to anticipatory or unearned profits, unabsorbed overhead, opportunity costs or consequential or other damages as a result of a termination for default.

ARTICLE 21. DISPUTES

21.1 Any dispute or difference arising out of, or in connection with, this Contract or the breach thereof which cannot be amicably settled between the Parties (including through alternative dispute resolution procedures as may be agreed to by the Parties) shall be arbitrated in accordance with the UNCITRAL Arbitration Rules then in effect. The arbitration shall take place in the City of Los Angeles. Any resulting arbitral decision shall be final and binding on both parties. Judgment upon any arbitration award may be entered in any court having jurisdiction thereof. Such judgment shall be in lieu of any other remedy.

21.2 In resolving a dispute hereunder, the parties agree that the Contract will be interpreted in accordance with the substantive laws of the City of Los Angeles.

21.3 Pending final resolution of any claim, dispute or action arising under or related to this Contract, Contractor

shall, if requested by the Purchaser, proceed diligently with the performance of this Contract.

ARTICLE 22. CONSEQUENTIAL DAMAGES

22.1 Notwithstanding any other provision of the Contract, in no event shall either Contractor or Owner be liable to the other party for indirect, incidental, special, punitive or consequential damages of any nature, including, but not limited to, loss of use, loss of revenue, or loss of income, whether arising in contract, tort (including negligence) or other legal theory, even if the possibility of such damages is known at the time of the execution of this Contract.

22.2 The exclusion of consequential damages set forth in Section 22.01 above shall not exclude or affect: (a) Contractor's obligation to pay liquidated damages in accordance with Article 11 (Time Extensions and Liquidated Damages); (b) Contractor's liability for fraud or intentional misconduct; or (c) Contractor's liability for its indemnity obligations in accordance with Article 17 (Indemnification).

ARTICLE 23. SAFETY

23.1 Contractor shall be responsible for initiating, maintaining and supervising all safety precautions and programs in connection with the performance of this Contract to prevent damage, injury and loss to employees, other persons and the Work. Contractor shall designate someone within its organization to oversee all safety aspects of the Work.

23.2 Contractor agrees to:

- (a) furnish machinery, tools, supplies and equipment that meet with all applicable safety standards;
- (b) require all Contractor personnel and Subcontractors to comply with all applicable safety rules, including those specified by Contractor and the Moldova Ministry of Defence;
- (c) secure all flammables at the close of each workday in nonflammable containers in designated storage areas provided by the Moldova Ministry of Defence; and
- (d) ensure that its work areas assigned by the Moldova Ministry of Defence to the Contractor are cleaned daily and remain free of hazards.

23.3 Contractor shall comply with applicable local laws, ordinances, rules, regulations and lawful orders of public authorities bearing on safety or the protection from damage, injury or loss of persons and property.

23.4 In the event Owner determines that Contractor is in violation of its safety obligations hereunder, Owner shall have the right to direct Contractor to immediately stop the Work and correct the violation, and Contractor shall comply with such directive at Contractor's sole cost and expense.

23.5 When the Work requires or involves the use/storage of explosives, other hazardous materials or unusual methods for execution of the Work, Contractor shall exercise utmost care and carry on such activities under supervision of properly qualified personnel.

23.6 If Contractor encounters material on site which it believes to be asbestos, polychlorinated biphenyl (PCB) or any other hazardous material, which has not been rendered harmless, Contractor shall stop Work immediately in the area affected and report the condition to the Owner, in writing. Thereafter:

- (a) if the material is hazardous and has not been rendered harmless, Contractor may not resume Work in the affected area, except by written agreement of the Owner and Contractor; or
- (b) if the hazardous material(s) has been rendered harmless, or is determined by the Owner not to exist in the designated Work area, Contractor may resume Work in the affected area by written agreement of the Owner and Contractor.

ARTICLE 24. OWNERSHIP RIGHTS AND OWNER PROPERTY

24.1 All Owner property, including but not limited to equipment, facilities, fixtures, drawings, patterns, molds, plans, research, writings, data in any format (including electronic), or other information furnished to Contractor by the Owner/Ministry of Defence, Moldova for use in the performance of this Contract, shall at all times be the property of the Owner/Ministry of Defence, Moldova. Upon completion, termination or expiration of this Contract, or at such other times as the Owner may direct, Contractor will return to the Owner all such property, at Contractor's expense.

24.2 All drawings and designs are the property of the Moldova Ministry of Defence at the time they are

submitted to the Owner & contractor for use.

24.3 On signing of this contract, the design will be available to **Prestigiu-AZ** according to the Moldova Ministry of Defence SOP for the classified information. As soon as we have the contract number, the Moldova Ministry of Defence will issue the Minister Order, where it will be defined:

- i. Who, when and how will turn over the classified design drawings to the Contractor.
- ii. Who (and how) will pay the taxes (20%). This will be the responsibility of the Moldova Ministry of Defence.
- iii. Who will give the permits for the entry of the employees to the site.
- iv. The point of contact for the progress of the project within the Moldova Ministry of Defence.

ARTICLE 25. AUDIT

25.1 As used in this Article, "Records" shall include, without limitation, books, documents, accounting records, payroll payment records, accounting policies, practices, and procedures, subcontractor files, original estimates and estimate worksheets, records relating to services or quantities delivered, hours of work performed, compliance with contract requirements, proposals, pricing of the contract, subcontract, or modifications, or any other cost, price adjustment, or extra charge claimed under the Contract, change order files, and any other records or performance reports which may have a bearing on matters associated with the Work, regardless of type and regardless of whether such items are in written form, in the form of computer data, or in any other form.

25.2 Contractor agrees to maintain, in accordance with sound and generally accepted accounting procedures and practices, Records of all direct and indirect costs and disbursements of any nature involving transactions related to this Contract or a Subcontract.

25.3 Contractor shall make its Records available at its office for examination, audit, or reproduction by Owner or Owner's designated representative, at all reasonable times until the expiration of five (5) years after the date of final payment, or for such shorter or longer period, if any, as is required by other Articles of this Contract. Owner shall have the right to examine and audit all Records and other evidence sufficient to reflect properly all costs claimed to have been incurred or anticipated to be incurred directly or indirectly in the performance of this Contract.

25.4 If Contractor or any Subcontractor has submitted cost or pricing data in connection with this Contract, Owner or its designated representative shall have the right to examine and audit all of Contractor's and Subcontractor's Records prepared or used by Contractor and/or Subcontractor, including related computations and projections, in order to evaluate the accuracy, completeness and currency of such data.

25.5 In the event an audit determines that Owner has overpaid Contractor, Owner, in addition to any other rights it may have as a matter of law, shall have the right to: (a) deduct the amount of such overpayment from any payments due, or that may become due, to Contractor under this Contract; and/or (b) demand that Contractor reimburse Owner the amount of any such overpayment. The aforementioned rights shall also apply to any obligations Contractor owed but did not provide to its employees or Subcontractors under this Contract.

25.6 The obligations of Contractor under this Article shall be incorporated into all Subcontracts of any tier, and Owner shall have the rights to examine, audit and reproduce Records of all Subcontractors to the same extent and manner as if such Subcontractor was in privity of contract with Owner.

25.7 The failure of Contractor to comply with the requirements of this Article shall be a material breach of Contract.

ARTICLE 26. CONFIDENTIALITY

26.1 Contractor shall keep all work and services carried out hereunder for Owner entirely confidential, and not use, publish, or make known to any persons other than its personnel and Subcontractors any information, whether developed by Contractor or provided by Owner, without Owner's prior written authorization. Contractor may not publish any articles or make any presentations relating to the Contract or Work, nor shall it refer to data, information or materials generated as part of the Contract or Work, without the prior written consent of Owner. For the avoidance of doubt, Owner shall have the right, in its sole discretion, to withhold the authorizations and/or consents referred to in the preceding sentences.

26.2 The foregoing obligations shall not apply to any information that was in Contractor's possession prior to commencement of work under this Contract, or which is or shall become available to the general public in a printed

publication through no fault of the Contractor, and provided further that this obligation shall in no way limit Contractor's internal use of such work. Any public representation regarding the Owner shall be made by Owner and any requests for information concerning the Contract or Work made to Contractor by the news media, or others, shall be referred to the Owner. Information Contractor considers as proprietary or confidential, and which Contractor has marked as proprietary or confidential, will be treated by Owner in the same manner as Owner treats its own proprietary or confidential information.

26.3 Notwithstanding the provisions of this Article 26, for any contract the Owner reserves the right to publicly disclose contract award information—specifically, in relation to the Contractor, the name of the Contractor receiving the contract and its country, a brief description of the contract goods or services, and the contract award amount. Contractor's proposal and contractual documents will remain confidential and therefore not subject to disclosure.

ARTICLE 27. OWNER NAME/LOGO

27.1 Contractor may not use the Owner's name and/or logo in any manner other than as identified in Section 27.2 below without first obtaining written permission from the Owner's Chief, Corporate Procurement Unit.

27.3 Contractor may, without prior approval of the Owner, use the Owner's name among its references in its customer lists or resumes. Any other use of the Owner's name, including use of the Owner's logo or discussion of the Work performed by the Contractor for the Owner, is not authorized.

ARTICLE 28. CLOSE RELATIVES

28.1 Not applicable as part of this contract.

ARTICLE 29. PROCUREMENT INTEGRITY

29.1 Contractor agrees to adhere to the highest standards of ethical competence and integrity in the performance of this Contract, having due regard for the nature and purposes of the Owner as an international organization, and to ensure that employees assigned to perform any services under this Contract will conduct themselves in a manner consistent therewith.

29.2 Contractor represents and warrants that it follows, and shall continue to comply with, all applicable laws, ordinances, rules, regulations, and lawful orders of public authorities of any jurisdiction in which work shall be performed under this Contract.

29.3 Contractor acknowledges that it is aware of and will comply with the Owner's policies including but not limited to those regarding conflicts of interest, fraud and corruption, gifts, conduct of contractor personnel, contractor responsibility, and anti-money laundering policies. Contractor warrants that Contractor and Contractor's employees, Subcontractors and Subcontractors' employees are in compliance with Vendor Integrity Policies; and have not engaged in conduct that would lead to suspension, debarment or a finding of ineligibility.

29.4 Contractor and all Subcontractors shall use reasonable efforts to ensure that funds paid to Contractor and all Subcontractors by the Owner are not used to finance, support or conduct terrorism.

29.5 Contractor and Contractor's employees, Subcontractors and Subcontractor's employees shall, during the term of the Contract, strictly avoid any activities that may create real or apparent conflicts of interest with their duties to the Owner under this Contract.

29.6 Contractor warrants that no official of the Ministry of Defence of Moldova or its member governments has received or will be offered by Contractor any direct or indirect gifts, favors or benefit arising from this Contract or the award thereof.

29.7 The remuneration of the Contractor shall constitute the sole remuneration in connection with this Contract. The Contractor shall not accept for its own benefit any trade commission, discount or similar payment in connection with activities pursuant to this Contract, or in the discharge of its obligations hereunder, and the Contractor shall use its best efforts to ensure that any Subcontractors, and the employees, agents and representatives of Contractor and any Subcontractors shall not receive any such additional remuneration. Contractor shall disclose in writing, by providing Notice to Owner pursuant to Article 43 (Notices), all fees, commissions, rebates, and discounts paid or received in connection with this Contract.

29.8 Contractor agrees that, within 30 days of having reasonable grounds to believe that Contractor, Contractor's employees, Subcontractors or Subcontractors' employees have: (a) violated any applicable laws, ordinances, rules, regulations, and lawful orders of public authorities in performing this Contract; (b) violated Owner's Vendor

Integrity Policies: (c) engaged in conduct that would lead to suspension, debarment or a finding of ineligibility; (d) used funds paid by the US Government to Contractor or any Subcontractors to finance, support or conduct terrorism; or (e) an actual, potential or apparent conflict of interest, Contractor will disclose in writing, by providing Notice to Owner pursuant to Article 43 (Notices), such violations, conduct, prohibited use of funds, or conflicts of interest.

29.9 Contractor agrees that it will not discharge, demote, suspend, threaten, harass, retaliate against, or otherwise discriminate against any Contractor employee in the terms and conditions of such employee's employment as a reprisal for such employee's disclosing to Owner or other proper authority information relating to a violation of Owner's Vendor Integrity Policies or any substantial violation of law relating to the award or performance of this Contract.

29.10 Contractor agrees that Owner has a right to audit Contractor's and Subcontractor's compliance with this Article pursuant to Article 28 ("Audit") of this Contract.

29.11 Contractor agrees that a breach of this Article is a material breach of an essential term of this Contract.

ARTICLE 30. BACKGROUND INVESTIGATION

30.1 Prior to employing individuals or Subcontractors to perform services under this Contract on Ministry of Defence Moldova premises, Contractor agrees, at its own expense, to perform or cause to be performed the following background investigation, and to maintain, or cause to be maintained, the results of the investigation in its employee's and its Subcontractor's employee's file:

- (a) Criminal records search over the last seven (7) years, with such search being conducted in all jurisdictions where the individual worked and jurisdictions where the individual indicated maintaining residence; and
- (b) Employment history verification, including dates of employment performance, salary, job title, and eligibility for re-hire, etc., and work permit to ensure they are valid and issued in the corresponding name. Contractor shall represent and warrant that its employees and its Subcontractors' employees assigned to work on the Owner premises: (a) have not been convicted of a Crime during the last seven (7) years; and (b) have a valid work permit based on local law. For purposes of this Article, the term "Crime" shall mean a crime that, if committed in the country would be classified as a felony under local law. It will be necessary to re-accomplish investigations prior to requesting renewal of Owner-issued ID cards.

ARTICLE 31. ASSIGNMENT

31.1 Neither this Contract nor any duty or right under it shall be delegated, subcontracted or assigned by Contractor without the prior written consent of the Owner, except that claims for monies due or to become due under this Contract may, in accordance with Section 31.02 below, be assigned to a bank, trust company, or other financial institution, including any federal lending agency, by Contractor without such consent.

31.2 In the event that Contractor does assign any monies due or to become due to it hereunder, Contractor shall provide the Owner with two copies of each and every such assignment. Contractor also hereby agrees, notwithstanding the terms of any such assignment, that the Owner may subject any payments to an assignee to set-off or recoupment for any present or future claim or claims which the Owner may have against the Contractor. The Owner reserves the right to make direct settlements or adjustments in price or both, with Contractor under the terms of this Contract and without notice to any assignee. Contractor shall indemnify and hold harmless the Owner against any liability that may arise as a result of such assignment.

ARTICLE 32. ENVIRONMENTAL

32.1 In order to contribute to waste reduction and to increase the development and awareness of environmentally sound purchasing, wherever possible, Contractor will perform the Work by using durable products, reusable products and products (including those used in services) that contain the maximum level of post-consumer waste, post-industrial and/or recyclable content, without significantly affecting the intended use of the goods or services. It is recognized that a cost analysis may be required in order to ensure that such products are made available at competitive prices.

ARTICLE 33. DIVERSITY

33.1 The Contractor will provide opportunities for access and growth of entities owned and controlled by

minorities, women, and disabled persons with an emphasis on measurable results and continuous improvement.

ARTICLE 34. CHILD LABOR

34.1 Forced or indentured child labor means all work or service: (a) exacted from any person under the age of eighteen (18) under the menace of any penalty for its non-performance and for which the worker does not offer himself voluntarily; or (b) performed by any person under the age of eighteen (18) pursuant to a contract the enforcement of which can be accomplished by process or penalties. Contractor certifies that no forced or indentured child labor was used to mine, produce, or manufacture, in whole or in part, any end product or component, or perform any service furnished under this Contract.

ARTICLE 35. FAIR LABOR STANDARDS

35.1 Contractor shall pay all employees whose work relates to this Contract not less than the minimum wage prescribed by applicable law or regulation, without rebate, either directly or indirectly, and without making any deductions, either directly or indirectly, from the full wages earned, other than permissible deductions as set forth in applicable laws or regulations. Contractor shall not require, suffer, or permit any employee whose work relates to this Contract to work more than the maximum hours in any workweek permitted by applicable law or regulation unless such employees are paid at least the overtime rate specified by applicable law or regulation.

ARTICLE 36. PUBLIC HEALTH PLANS AND CONTINGENCY

36.01 In the event of a Pandemic Influenza outbreak, SARS outbreak, other biomedical emergency, or other catastrophe ("Public Health Event or Other Catastrophe"), Contractor agrees to take all reasonable measures to continue performance of the Contract with a minimum of delay, interruption or other disruption, if Owner designates this Contract as mission critical and essential to the ongoing operations of Owner. If Owner so designates this Contract, within thirty (30) days after award, Contractor will submit to Owner, for its review and approval, a contingency plan detailing how Contractor will continue performance of this Contract with a minimum of delay, interruption or other disruption in the event of a Public Health Event or Other Catastrophe. In the event of a Public Health Event or Other Catastrophe, Owner and Contractor shall immediately discuss and agree upon the measures to be taken, with the expectation that the contingency plan will be the baseline for discussions. Contractor shall be entitled to relief under Article 11 (Time Extensions and Liquidated Damages) and Article 10 (Changes and Modifications) in the event of a Public Health Event or Other Catastrophe.

ARTICLE 37. FORCE MAJEURE

37.1 The failure of a Party to fulfill any of its obligations hereunder shall not be considered to be a breach of, or default under, this Contract insofar as such inability arises from a Force Majeure Event, provided that the Party affected by such an event has taken all reasonable precautions, due care and reasonable alternative measures, all with the objective of carrying out the terms and conditions of this Contract.

37.2 A Party affected by a Force Majeure Event shall take all reasonable measures to remove such Party's inability to fulfill its obligations hereunder with a minimum of delay.

37.3 A Party affected by a Force Majeure Event shall notify the other Party of such event as soon as possible, and in any event not later than seven (7) days following the occurrence of such event, providing evidence of the nature and cause of such event and its expected duration and impact on the performance of this Contract, and shall similarly give notice of the restoration of normal conditions as soon as possible.

37.4 The Parties shall take all reasonable measures to minimize the consequence of any Force Majeure Event.

37.5 Any period within which a Party is required by this Contract to complete any action or task shall be extended for a period equal to the time during which such Party was unable to perform such action as a result of Force Majeure Event, provided that such Party has provided notice as required by this Article.

ARTICLE 38. SEVERABILITY

38.01 If any term or provision of this Contract shall to any extent be invalid and unenforceable, the remainder of the Contract shall be valid and shall be enforced to the extent permitted by law.

ARTICLE 39. LANGUAGE

39.01 This Contract has been executed in the English language, which shall be the binding and controlling language for all matters relating to the meaning or interpretation of this Contract.

ARTICLE 40. CONFLICTS OF LAW

40.01 Any provision of this Contract prohibited by the laws of any jurisdiction where Work is carried out or performed shall be ineffective within said jurisdiction, without invalidating the remaining provisions of this Contract.

ARTICLE 41. PRESERVATION OF IMMUNITIES

41.01 Nothing herein shall constitute or be considered to be a limitation upon or a waiver of the privileges and immunities of any member of the Golden West Humanitarian Foundation, which privileges and immunities are specifically reserved.

ARTICLE 43. NOTICES

43.01 Any notice, including without limitation any notification, claim, or request for consent or authorization, required or permitted to be given under this Contract, shall be in writing addressed to the person identified below and shall be deemed to have been given if (a) sent by registered or certified mail; or (b) transmitted by any other means if and when receipt is acknowledged by the person identified below. No authorization or consent required under this Contract shall be effective unless and until given in writing by the person identified below:

43.2 For the Owner:

The Golden West Humanitarian Foundation

Address:

6355 Topanga Canyon Blvd.

Suite 517,

Woodland Hills,

CA 91367,

United States of America

43.3 For the Contractor:

Prestigiu_AZ

3, Padurilor str, Pohatni

Chisinau, Moldova-MD2092

CONFIDENTIAL

ARTICLE 44. ENTIRE CONTRACT

44.01 This Contract, including the Contract Documents attached hereto and referenced herein, constitutes the entire, integrated understanding and agreement between the parties and supersedes any oral or prior written agreements with respect to the subject matter of this Contract.


IN WITNESS WHEREOF the parties have caused this Contract No. **EUCOM/#15JPSS20D00000035** to be executed.

Signatures

GOLDEN WEST HUMANITARIAN FOUNDATION



PRESTIGIU-AZ



CONFIDENTIAL

Page 19 of 19

CONTRACT NO. EUCOM/EUCOM/#15JPSS20D00000035 MODIFICATION "A"

This modification, made on 21 February 2022, by and between the **GOLDEN WEST HUMANITARIAN FOUNDATION**, on behalf of the United States European Command (EUCOM) HMA Program (hereafter referred to as the Owner), and **PRESTIGIU-AZ** (hereafter referred to as the contractor).

WHEREAS, the parties entered into a Contract dated 15th October 2021 whereby Contractor provides Engineering Services at the Moldova Ammunition & Explosives Storage Area, Floresti and Cahul, Moldova

WHEREAS, the parties now desire to modify this contract;

PURPOSE: To authorize additional work and increase the contract price.

1. PURSUANT TO ARTICLE 10 CHANGES AND MODIFICATIONS, the

Owner hereby authorizes the change as detailed in the attachment to this document:

- a. Works detailed in the attached document, of a value of **USD 7,046.29** (Seven Thousand and Forty Six United States Dollars and Twenty Nine Cent), in addition to the works requiring completion detailed in the Annex A, Scope of Work, of a value of **USD 515,811.16** (Five Hundred and Fifteen Thousand, Eight Hundred and Eleven United States Dollars and Sixteen Cents), of the contract and,

- b. Volume of works actually carried out so far

2. PURSUANT TO ARTICLE 7 CONTRACT PRICE, the Owner hereby revises

the total contract price excluding VAT, as follows:

*7.1 The Owner hereby covenants to pay the Contractor in consideration of the execution and completion of the Work and additional work therein the Contract Price of **USD 522,857.45** (Five Hundred and Twenty Two Thousand, Eight Hundred and Fifty Seven United States Dollars and Forty Five Cents) or such other sums as may become payable under the provisions of the Contract at the times and in the manner prescribed by the Contract.*

This modification shall be effective as of 21 February 2022. All other provisions of the Contract shall remain in full force and effect.

IN WITNESS WHEREOF, the parties hereto have caused this Modification to be signed by their duly authorized officer(s).

Director
Prestigiu - AZ 4 RL
Cobanu Iorgu

INVESTITOR

Golden West Humanitarian Foundation

GESTIONAR

Baza păstrare tehnică, armament și patrimoniu militar

ANTREPRENOR

SRL „Prestigiu-Az”

**PROCES-VERBAL
DE RECEPȚIE LA TERMINAREA LUCRĂRILOR**

Nr. 11 din „11” 11 2022

Lucrări de construcție și reparație
la depozitele de muniții
din cadrul Bazei păstrare tehnică, armament și patrimoniu militar

Privind lucrarea „Construcția și reparația la depozitul de muniții” executată la obiectul Bazei păstrare tehnică, armament și patrimoniu militar în cadrul contractului EUCOM#15JPSS20D00000035 din „15” „10” 2021 încheiat între Golden West Humanitarian Foundation și SRL „Prestigiu-Az”.

1. Comisia de recepție la terminarea lucrărilor și-a desfășurat activitatea pe data de „01” „09” 2022, instituită prin ordinul Șefului Bazei păstrare tehnică, armament și patrimoniu militar nr. 82 din 26 august 2022, fiind formată din:

Președintele comisiei:

maior Eduard RÎȘNEAC, șef secție operații logistice-locțiitor șef stat major.

Membrii comisiei:

funcționara Tatiana CIOBANU, specialist (exploatare imobil) serviciu exploatare spațiu locativ;

funcționarul Vladimir DOBROVOLSCHI, contabil-șef.

2. Au mai participat la recepție în calitate de invitați:

Reprezentantul J4 Direcție logistică, Marele Stat Major al Armatei Naționale

locotenent-colonel Alexandru ARION, ofițer principal secție armament și blindate.

Reprezentantul Agenției Asigurare Resurse și Administrare Patrimoniu a Ministerului Apărării

funcționar Victor MORGOCI, inspector superior secție infrastructură și supraveghere tehnică (de specialitate inginer construcții) Direcție administrare bunuri imobile.

Reprezentanții Antreprenorului:

Serghei CIOBANU, directorul SC „Prestigiu-Az” SRL;

Ion STRILETCHII, diriginte de șantier atestat.

3. Constatările comisiei de recepție:

În urma examinării și analizei lucrărilor efectuate au rezultat următoarele:

1) Antreprenorul general SRL „Prestigiu-Az” SRL, a prezentat, în baza contractului EUCOM#15JPSS20D00000035 din „15” „10” 2021 pentru recepție lucrările de construcții și reparație la depozitele de muniții a Bazei păstrare tehnică, armament și patrimoniu militar.

2) Constatările comisiei de recepție mai sînt expuse în următoarele anexe la prezentul proces verbal:

-Lista-anexă nr.1: Din documentația scrisă și desenată, care trebuia prezentată, au lipsit sau sînt incomplete;

-Lista-anexă nr. 2: Lucrări neexecutate;

-Lista-anexă nr.3: Lucrările, la executarea cărora nu s-au respectat prevederile proiectului.

3) Obiecțiile și neconformitățile Beneficiarului, au fost remediate în timpul executării lucrărilor de către Antreprenor.

Totodată, în cazul în care o anumită lucrare neesențială care necesită remedieri sau corectări nu este inclusă în prezentul proces verbal, Antreprenorul nu va fi scutit de responsabilitatea de executare corespunzătoare a acestora în conformitate cu prevederile contractului nominalizat.

4) În conformitate cu prevederile contractului EUCOM/P010247335 din „15” „10” 2021, se stabilește termenul de garanție de bună execuție de la recepția la terminarea lucrărilor la obiectivul nominalizat -1 (unu) ani.

4. Comisia de recepție, în baza constatărilor făcute, propune următoarele:
- de a recepționa terminarea lucrărilor la obiectivul „Lucrări de construcții și reparație la depozitele de muniții” din cadrul Bazei păstrare tehnică, armament și patrimoniu militar, fără obiectii.

5. Comisia de recepție motivează propunerea făcută prin constatarea la fața locului a executării lucrărilor de construcție contractate.

6. Comisia de recepție studiind documentele și constatarea la fața locului, recomandă următoarele:



- de supus recepției la terminarea lucrărilor, cu propunerea acestuia spre recepție finală, conform prevederilor legislației în vigoare.

7. Prezentul proces-verbal, conținând 3 (trei) file și 3 (trei) anexe, cu un total de 6 (șase) file, a fost încheiat astăzi, „01” „09” 2022 în 4 exemplare.

Comisia de recepție:
Președintele comisiei:
maior Eduard RÎȘNEAC



Membrii comisiei:
funcționara Tatiana CIOBANU
funcționarul Vladimir DOBROVOLSCHI



Au mai participat la recepție:
Reprezentantul J4 Direcție logistică, Marele Stat Major al Armatei Naționale
locotenent-colonel Alexandru ARION



Reprezentantul Agenției Asigurare Resurse și Administrare Patrimoniu a Ministerului Apărării
funcționarul Victor MORGOCI




Reprezentanții Antreprenorului:
Serghei CIOBANU
Ion STRILETCHII





8. Lucrarea „Construcția și reparația la depozitele de muniții Florești”, este:

TRANSMISĂ:
ANTREPRENORUL:


(semnătura)

PRIMITĂ:
BENEFICIARUL
(GESTIONAR)


(semnătura)


Documentația scrisă și desenată, care trebuia prezentată, au lipsit sau sînt incomplete

Comisia de recepție la terminarea lucrărilor constată că din documentația scrisă și desenată, care trebuia prezentată, **NU este cazul.**

Comisia de recepție:
Președintele comisiei:
maior Eduard RÎȘNEAC



Membrii comisiei:
funcționara Tatiana CIOBANU
funcționarul Vladimir DOBROVOLSCHI



Au mai participat la recepție:
Reprezentantul J4 Direcție logistică, Marele Stat Major al Armatei Naționale
locotenent-colonel Alexandru ARION



Reprezentantul Agenției Asigurare Resurse și Administrare Patrimoniu a Ministerului Apărării
funcționarul Victor MORGOCI



Reprezentanții Antreprenorului:
Serghei CIOBANU
Ion STRILETCHII




Lucrări neexecutate

Comisia de recepție la terminarea lucrărilor constată că **NU** sunt lucrări neexecutate.

Comisia de recepție:
Președintele comisiei:
maior Eduard RÎȘNEAC



Membrii comisiei:
funcționara Tatiana CIOBANU
funcționarul Vladimir DOBROVOLSCHI



Au mai participat la recepție:


Reprezentantul J4 Direcție logistică, Marele Stat Major al Armatei Naționale
locotenent-colonel Alexandru ARION



Reprezentantul Agenției Asigurare Resurse și Administrare Patrimoniu a Ministerului Apărării
funcționarul Victor MORGOCI



Reprezentanții Antreprenorului:
Serghei CIOBANU
Ion STRILETCHII



Lucrări, la care nu s-au respectat prevederile proiectului

Comisia de recepție la terminarea lucrărilor constată că **NU** sunt lucrări la care nu s-au respectat prevederile proiectului.

Comisia de recepție:

Președintele comisiei:

maior Eduard RÎȘNEAC

Membrii comisiei:

funcționara Tatiana CIOBANU

funcționarul Vladimir DOBROVOLSCHI

Au mai participat la recepție:

Reprezentantul J4 Direcție logistică, Marele Stat Major al Armatei Naționale

locotenent-colonel Alexandru ARION

Reprezentantul Agenției Asigurare Resurse și Administrare Patrimoniu a Ministerului Apărării

funcționarul Victor MORGOCI

Reprezentanții Antreprenorului:

Serghei CIOBANU

Ion STRILETCHII

INVESTITOR

Golden West Humanitarian Foundation

GESTIONAR

Baza păstrare tehnică, armament și patrimoniu militar

ANTREPRENOR

SRL „Prestigiu-Az”

**PROCES-VERBAL
DE RECEPȚIE FINALĂ**

Nr. 12 din „01” 05 2022

Lucrări de construcție și reparație
la depozitele de muniții
din cadrul Bazei păstrare tehnică, armament și patrimoniu militar

Obiectul „**Lucrări de construcții și reparații la depozitele de muniții**” este executat în cadrul Bazei păstrare tehnică, armament și patrimoniu militar conform contractului EUCOM/P010247335 din „15” „10” 2022 încheiat între Golden West Humanitarian Foundation și SRL „Prestigiu-Az”.

1. Comisia de recepție finală și-a desfășurat activitatea în intervalul 01 09 2022, instituită prin ordinul Șefului Bazei păstrare tehnică, armament și patrimoniu militar nr. 82 din 26 august 2022, fiind formată din:

Președintele comisiei:

maior Eduard RIȘNEAC, șef secție operații logistice-încălzitor șef stat major.

Membrii comisiei:

funcționara Tatiana CIOBANU, specialist (exploatare imobil) serviciu exploatare spațiu locativ;

funcționarul Vladimir DOBROVOLSCHI, contabil-șef.

2. Au mai participat la recepție în calitate de invitați:

Reprezentantul J4 Direcție logistică, Marele Stat Major al Armatei Naționale

locotenent-colonel Alexandru ARION, ofițer principal secție armament și blindate.

Reprezentantul Agenției Asigurare Resurse și Administrare Patrimoniu a Ministerului Apărării

funcționar Victor MORGOCI, inspector superior secție infrastructură și supraveghere tehnică (de specialitate inginer construcții) Direcție administrare bunuri imobile.

Reprezentanții Antreprenorului:

Serghei CIOBANU, directorul SC „Prestigiu-Az” SRL;

Ion STRILETCHI, diriginte de șantier atestat.

3. Comisia de recepție finală, în urma examinării și analizei lucrărilor efectuate a constatat următoarele:

1) Lucrările pe specialități au fost executate și recepționate conform procesului verbal de recepție la terminarea lucrărilor nr. 10 din „01” 10 2022;

2) Conform demersului SC „Prestigiu-Az” SRL nr. 18 din 26.07.2022 lucrările de construcții și reparații au fost terminate la data de „26” 10 10 2022;

3) Observații a comisiei de recepție finală: **fară obiecții**;

4) În baza datelor prezentate de către Antreprenor, **valoarea totală a obiectului (inclusiv utilajul)**, la data de „01” 10 2022 constituie **50 013,77 USD**, echivalentul **909 713,33 lei/MD**, care vor fi repartizate și luate la evidență contabilă, de către reprezentanții serviciului financiar a Bazei păstrare tehnică, armament și patrimoniu militar, după cum urmează:

- **valoarea lucrărilor de construcție**, conform bilanțului de transmitere la data de „01” 10 2022 constituie **838 629,71 lei/MD**, care vor fi luate la evidență contabilă, conform anexei nr.1.

- **valoarea bunurilor materiale** montate la obiect, conform bilanțului de transmitere la data de „01” 10 2022 constituie **71 083,62 lei/MD**, care vor fi luate la evidență contabilă, conform anexei nr.2.

4. În baza constatărilor făcute, comisia de recepție finală propune:
- **spre recepție finală** a obiectivului „Lucrări de construcții și reparații la depozitele de muniții” din cadrul Bazei păstrare tehnică, armament și patrimoniu militar.

5. Comisia de recepție finală motivează propunerea făcută prin constatarea la fața locului a finalizării lucrărilor de construcții.

6. Comisia de recepție finală recomandă următoarele:

- **admiterea recepției finale** a obiectivului „Lucrări de construcții și reparații la depozitele de muniții” din cadrul Bazei păstrare tehnică, armament și patrimoniu militar.

6¹. Descrierea obiectului recomandat spre recepție:

a) **obiective de infrastructură tehnico-edilitară:**

- Sistemul de iluminare exterior (perimetral), cu lungimea 2500,0 m/l;
- Sistem de securitate, supraveghere video cu circuit închis a depozitelor.

7. Prezentul proces-verbal, conținând **3 (trei)** file și 2 (două) anexe, cu un total de **5 (cinci)** file, a fost încheiat astăzi „01” 10 2022 în 4 exemplare.

Comisia de recepție finală:

Președintele comisiei:

maior Eduard RÎȘNEAC

Membrii comisiei:

funcționara Tatiana CIOBANU

funcționarul Vladimir DOBROVOLSKI

Au mai participat la recepție:

Reprezentantul J4 Direcție logistică, Marele Stat Major al Armatei

Naționale

locotenent-colonel Alexandru ARION

Reprezentantul Agenției Asigurare Resurse și Administrare Patrimoniu a Ministerului Apărării

funcționarul Victor MORGOCI


Reprezentanții Antreprenorului:

Serghei CIOBANU


Ion STRILETCHII

8. Lucrarea „**Construcția și reparația la depozitele de muniții**” din cadrul Bazei păstrare tehnică, armament și patrimoniu militar, este:

TRANSMISĂ:
ANTREPRENORUL:


(semnătura)

PRIMITĂ:
BENEFICIARUL
(GESTIONAR)


(semnătura)

Valoarea lucrărilor
de construcții și reparații la depozitele de muniții
din cadrul Bazei păstrare tehnică, armament și patrimoniu militar

Nr crt	Denumirea	U/M	Cant	Preț (lei)	Suma (lei)
1.	Sistemul de iluminare exterior (perimetral)	set	1	374 138,47	374 138,47
2.	Sistem de securitate, supraveghere video	set	1	464 491,24	464 491,24
	ÎN TOTAL				838 629,71

Notă: Obiectivul „Construcția și reparația la depozitele de muniții” din cadrul Bazei păstrare tehnică, armament și patrimoniu militar a fost executat prin programe de asistență externă, finanțat de către Golden West Humanitarian Foundation.

Acest contract de construcție este supus Hotărârii Guvernului RM nr.246 din 08.04.2010 privind aplicarea cotei zero a TVA-ului.

Comisia de recepție finală:

Președintele comisiei:


maior Eduard RÎȘNEAC



Membrii comisiei:

funcționara Tatiana CIOBANU

funcționarul Vladimir DOBROVOLSCHI



Au mai participat la recepție:

Reprezentantul J4 Direcție logistică, Marele Stat Major al Armatei Naționale

locotenent-colonel Alexandru ARION



Reprezentantul Agenției Asigurare Resurse și Administrare Patrimoniu a Ministerului Apărării


funcționarul Victor MORGOCI



Reprezentanții Antreprenorului:

Serghei CIOBANU

Ion STRILETCHII



Valoarea bunurilor materiale
montate la obiectivul „Lucrări de construcții și reparații la depozitele de muniții” din
cadrul Bazei păstrare tehnică, armament și patrimoniu militar

Nr crt	Denumirea	U/M	Cant	Preț (lei)	Suma (lei)
I. Sistemul supraveghere video					
1.	Network video recorder Tiandy TC-R3220 (2ch, 2HDD) Spec:1/B/K	buc	1	5183,94	5183,94
2.	Camera IP Tiandy TC-C34US (4MP, extrema, 2,8mm, Mic) Spec:15/y/2,8mm	buc	17	2234,07	37 979,19
3.	Televizor 43" Blaupunkt 43UN265T, Black (3840x2160)UND, SMART TV, 60HZ, DVB-T/T2/C/S2	buc	1	7002.86	7002.86
4.	HDD6Tb Seagate Surveillance	buc	2	4547.315	9094.63
5.	Switch POE BS3010M (8POE+2uplink 1GB 1SFP)managed	buc	5	2364.60	11823.00
ÎN TOTAL					71 083,62

Notă: Obiectivul „Construcția și reparația la depozitele de muniții” din cadrul Bazei păstrare tehnică, armament și patrimoniu militar a fost executat prin programe de asistență externă, finanțat de către Golden West Humanitarian Foundation.

Acest contract de construcție este supus Hotărârii Guvernului RM nr.246 din 08.04.2010 privind aplicarea cotei zero a TVA-ului.

Comisia de recepție finală:

Președintele comisiei:

maior Eduard RÎȘNEAC

Membrii comisiei:

funcționara Tatiana CIOBANU

funcționarul Vladimir DOBROVOLSCII

Au mai participat la recepție:

Reprezentantul J4 Direcție logistică, Marele Stat Major al Armatei Naționale
locotenent-colonel Alexandru ARION

Reprezentantul Agenției Asigurare Resurse și Administrare Patrimoniu a
Ministerului Apărării

funcționarul Victor MORGOCI

Reprezentanții Antreprenorului:

Serghei CIOBANU

Ion STRILETCHII

INVESTITOR

Golden West Humanitarian Foundation

GESTIONAR

Brigada 3 infanterie motorizată

ANTREPRENOR

SRL „Prestigiu-Az”

**PROCES-VERBAL
DE RECEPȚIE LA TERMINAREA LUCRĂRILOR**

Nr. 1384 din „02” 09 2022

**Lucrări de construcție și reparație
la depozitele de muniții
din cadrul Brigăzii 3 infanterie motorizată**

Cahul

Privind lucrarea „Construcția și reparația la depozitele de muniții” executată la obiectul Brigăzii 3 infanterie motorizată în cadrul contractului EUCOM/#15JPSS20D00000035 din „15” 10 2021 încheiat între Golden West Humanitarian Foundation și SRL „Prestigiu-Az”.

1. Comisia de recepție la terminarea lucrărilor și-a desfășurat activitatea în intervalul „02” 09 2022, instituită prin ordinul Comandantului Brigăzii 3 infanterie motorizată nr. 34 din 03.08. 2022, fiind formată din:

Președintele comisiei:

locotenent-colonel Anatolie STRATU, locuitor comandant de brigadă (șef S4 secție logistică) stat major.

Membrii comisiei:

maior Valeri DUȘA, șef serviciu cazare S4 secție logistică stat major;

capitan Iliă GARABAIU, șef serviciu armament și muniții S4 secție logistică stat major;

sergent clasa II Iurie CIOBANU, șef depozit (muniții) grupă depozite pluton asigurare companie logistică.

2. Au mai participat în recepție în calitate de invitați:

Reprezentantul J4 Direcție logistică, Marele Stat Major al Armatei Naționale

locotenent-colonel Alexandru ARION, ofițer principal secție armament și blindate.

Reprezentantul Agenției Asigurare Resurse și Administrare Patrimoniu a Ministerului Apărării

funcționar Victor MORGOCI, inspector superior secție infrastructură și supraveghere tehnică (de specialitate inginer construcții) Direcție administrare bunuri imobile.

Reprezentanții Antreprenorului:

Serghei CIOBANU, directorul SC „Prestigiu-Az” SRL;

Ion STRILETCHI, diriginte de șantier atestat.

3. Constatările comisiei de recepție:

În urma examinării și analizei lucrărilor efectuate au rezultat următoarele:

1) Antreprenorul general SRL „Prestigiu-Az” SRL, a prezentat, în baza contractului EUCOM/#15JPSS20D00000035 din „15” octombrie 2021, pentru recepție lucrările de construcții și reparație la depozitele de muniții din cadrul Brigăzii 3 infanterie motorizată.

2) Constatările comisiei de recepție mai sînt expuse în următoarele anexe la prezentul proces verbal:

-Lista-anexă nr.1: Din documentația scrisă și desenată, care trebuia prezentată, au lipsit sau sînt incomplete;

-Lista-anexă nr. 2: Lucrări neexecutate;

-Lista-anexă nr.3: Lucrările, la executarea cărora nu s-au respectat prevederile proiectului.

3) Obiectele și neconformitățile Beneficiarului, au fost remediate în timpul executării lucrărilor de către Antreprenor.

Totodată, în cazul în care o anumită lucrare neesențială care necesită remedieri sau corectări nu este inclusă în prezentul proces verbal, Antreprenorul nu

va fi scutit de responsabilitatea de executare corespunzătoare a acestora în conformitate cu prevederile contractului nominalizat.

4) În conformitate cu prevederile contractului EUCOM/P010247335 din „15” octombrie 2021, se stabilește termenul de garanție de bună execuție de la recepția la terminarea lucrărilor la obiectivul nominalizat - **1 (unu) ani**.

4. Comisia de recepție, în baza constatărilor făcute, propune următoarele:

- de a recepționa terminarea lucrărilor la obiectivul „Lucrări de construcții și reparație la depozitele de muniții” din cadrul Brigăzii 3 infanterie motorizată, **fără obiecții.**

5. Comisia de recepție motivează propunerea făcută prin constatarea la fața locului a executării lucrărilor de construcție și reparație contractate.

6. Comisia de recepție studiind documentele și constatarea la fața locului, recomandă următoarele:

- de supus recepției la terminarea lucrărilor, cu propunerea acestuia **spre recepție finală**, conform prevederilor legislației în vigoare.

7. Prezentul proces-verbal, conținând **3** (trei) file și **3** (trei) anexe, cu un total de **6** (șase) file, a fost încheiat astăzi, „**02**” „**09**” 2022 în 4 exemplare.

Comisia de recepție:

Președintele comisiei:

locotenent-colonel Anatolie STRATU

Membrii comisiei:

maior Valeri DUȘA

căpitan Ilia GARABAJIU

sergent clasa II Iurie CIOBANU

Au mai participat la recepție:

Reprezentantul J4 Direcție logistică, Marele Stat Major al Armatei Naționale

locotenent-colonel Alexandru ARION

Reprezentantul Agenției Asigurare Resurse și Administrare Patrimoniu a Ministerului Apărării

funcționarul Victor MORGOCI

Reprezentanții Antreprenorului:

Serghei CIOBANU

Ion STRILETCHII

8. Lucrarea „Construcția și reparația la depozitul de muniții” din cadrul Brigăzii 3 infanterie motorizată este:

TRANSMISĂ:
ANTREPRENORUL:

(semnătura)



Documentația scrisă și desenată, care trebuia prezentată, au lipsit sau sînt incomplete

Comisia de recepție la terminarea lucrărilor constată că din documentația scrisă și desenată, care trebuia prezentată, **NU** a lipsit nimic.

Comisia de recepție:

Președintele comisiei:


locotenent-colonel Anatolie STRATU

Membrii comisiei:

maior Valeri DUȘA

căpitan Ilia GARABAJIU

sergent clasa II Iurie CIOBANU

Handwritten signatures of the commission members: Anatolie STRATU, Valeri DUȘA, Ilia GARABAJIU, and Iurie CIOBANU.

Au mai participat la recepție:

Reprezentantul J4 Direcție logistică, Marele Stat Major al Armatei Naționale

locotenent-colonel Alexandru ARION

Handwritten signature of Alexandru ARION.

Reprezentantul Agenției Asigurare Resurse și Administrare Patrimoniu a Ministerului Apărării


funcționarul Victor MORGOCI

Handwritten signature of Victor MORGOCI.

Reprezentanții Antreprenorului:

Serghei CIOBANU

Ion STRILETCHII

Handwritten signatures of the entrepreneurs: Serghei CIOBANU and Ion STRILETCHII.

Lucrări neexecutate

Comisia de recepție la terminarea lucrărilor constată că **NU** sunt lucrări neexecutate.

Comisia de recepție:

Președintele comisiei:

locotenent-colonel Anatolie STRATU

Membrii comisiei:

maior Valeriu DUȘA

căpitan Ilia GARABAJIU

sergent clasa II Iurie CIOBANU

Au mai participat la recepție:

Reprezentantul J4 Direcție logistică, Marele Stat Major al Armatei Naționale

locotenent-colonel Alexandru ARION



Reprezentantul Agenției Asigurare Resurse și Administrare Patrimoniu a Ministerului Apărării

funcționarul Victor MORGOCI

Reprezentanții Antreprenorului:

Serghei CIOBANU

Ion STRILETCHII

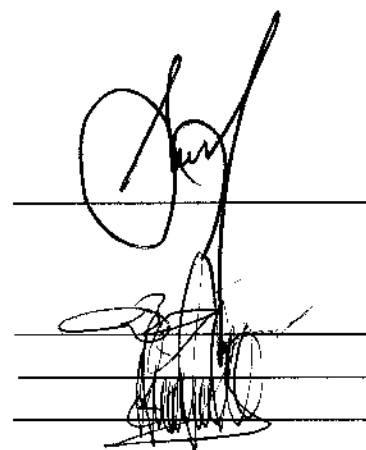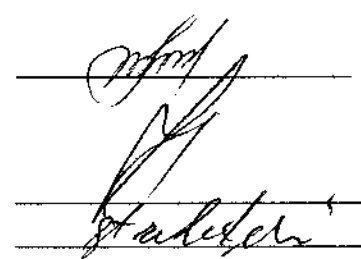Handwritten signatures of the commission members, including the president and members, written over horizontal lines.Handwritten signature of the J4 representative, written over a horizontal line.Handwritten signatures of the contractor representatives, written over horizontal lines.

Lucrări, la care nu s-au respectat prevederile proiectului

Comisia de recepție la terminarea lucrărilor constată că **NU** sunt lucrări la care nu s-au respectat prevederile proiectului.

Comisia de recepție:

Președintele comisiei:


locotenent-colonel Anatolie STRATU

Membrii comisiei:

maior Valeriu DUȘA

căpitan Ilia GARABAJIU

sergent clasa II Iurie CIOBANU









Au mai participat la recepție:

Reprezentantul J4 Direcție logistică, Marele Stat Major al Armatei Naționale

locotenent-colonel Alexandru ARION



Reprezentantul Agenției Asigurare Resurse și Administrare Patrimoniu a Ministerului Apărării

funcționarul Victor MORGOCI




Reprezentanții Antreprenorului:

Serghei CIOBANU

Ion STRILETCHII





Privind lucrarea „**Construcția și reparația la depozitul de muniții**” executată la obiectul Bazei păstrare tehnică, armament și patrimoniu militar în cadrul contractului EUCOM/P010247335 din „/S” 10 202 / încheiat între Golden West Humanitarian Foundation și SRL „Prestigiu-Az”.

1. Comisia de recepție la terminarea lucrărilor și-a desfășurat activitatea pe data de „01” 09 2022, instituită prin ordinul Șefului Bazei păstrare tehnică, armament și patrimoniu militar nr. 82 din 26 august 2022, fiind formată din:

Președintele comisiei:

maior Eduard RÎȘNEAC, șef secție operații logistice-loctiitor șef stat major.

Membrii comisiei:

funcționara Tatiana CIOBANU, specialist (exploatare imobil) serviciu exploatare spațiu locativ;

funcționarul Vladimir DOBROVOLSCHI, contabil-șef.

2. Au mai participat la recepție în calitate de invitați:

Reprezentantul J4 Direcție logistică, Marele Stat Major al Armatei Naționale

locotenent-colonel Alexandru ARION, ofițer principal secție armament și blindate.

Reprezentantul Agenției Asigurare Resurse și Administrare Patrimoniu a Ministerului Apărării

funcționar Victor MORGOCI, inspector superior secție infrastructură și supraveghere tehnică (de specialitate inginer construcții) Direcție administrare bunuri imobile.

Reprezentanții Antreprenorului:

Serghei CIOBANU, directorul SC „Prestigiu-Az” SRL;

Ion STRILETCHI, diriginte de șantier atestat.

3. Constatările comisiei de recepție:

În urma examinării și analizei lucrărilor efectuate au rezultat următoarele:

1) Antreprenorul general SRL „Prestigiu-Az” SRL, a prezentat, în baza contractului EUCOM/P010247335 din „/S” 10 202 / pentru recepție lucrările de construcții și reparație la depozitele de muniții a Bazei păstrare tehnică, armament și patrimoniu militar.

2) Constatările comisiei de recepție mai sînt expuse în următoarele anexe la prezentul proces verbal:

-Lista-anexă nr.1: Din documentația scrisă și desenată, care trebuia prezentată, au lipsit sau sînt incomplete;

-Lista-anexă nr. 2: Lucrări neexecutate;

-Lista-anexă nr.3: Lucrările, la executarea cărora nu s-au respectat prevederile proiectului.

3) Obiecțiile și neconformitățile Beneficiarului, au fost remediate în timpul executării lucrărilor de către Antreprenor.

Totodată, în cazul în care o anumită lucrare neesențială care necesită remedieri sau corectări nu este inclusă în prezentul proces verbal, Antreprenorul nu va fi scutit de responsabilitatea de executare corespunzătoare a acestora în conformitate cu prevederile contractului nominalizat.

Privind lucrarea „**Construcția și reparația la depozitele de muniții**” executată la obiectul Brigăzii 3 infanterie motorizată în cadrul contractului EUCOM/P010247335 din „15” 10 2021 încheiat între Golden West Humanitarian Foundation și SRL „Prestigiu-Az”.

1. Comisia de recepție la terminarea lucrărilor și-a desfășurat activitatea în intervalul „02” 09 2022, instituită prin ordinul Comandantului Brigăzii 3 infanterie motorizată nr. 34 din 03.08. 2022, fiind formată din:

Președintele comisiei:

locotenent-colonel Anatolie STRATU, foștii comandant de brigadă (șef S4 secție logistică) stat major.

Membrii comisiei:

maior Valeri DUȘA, șef serviciu cazare S4 secție logistică stat major;

căpitan Ilia GARABAIU, șef serviciu armament și muniții S4 secție logistică stat major;

sergent clasa II Iurie CIOBANU, șef depozit (muniții) grupă depozite pluton asigurare companie logistică.

2. Au mai participat la recepție în calitate de invitați:

Reprezentantul J4 Direcție logistică, Marele Stat Major al Armatei Naționale

locotenent-colonel Alexandru ARION, ofițer principal secție armament și blindate.

Reprezentantul Agenției Asigurare Resurse și Administrare Patrimoniu a Ministerului Apărării

funcționar Victor MORGOCI, inspector superior secție infrastructură și supraveghere tehnică (de specialitate inginer construcții) Direcție administrare bunuri imobile.

Reprezentanții Antreprenorului:

Sergei CIOBANU, directorul SC „Prestigiu-Az” SRL;

Ion STRILETCHII, diriginte de șantier atestat.

3. Constatările comisiei de recepție:

În urma examinării și analizei lucrărilor efectuate au rezultat următoarele:

1) Antreprenorul general SRL „Prestigiu-Az” SRL, a prezentat, în baza contractului EUCOM/P010247335 din „15” octombrie 2021, pentru recepție lucrările de construcții și reparație la depozitele de muniții din cadrul Brigăzii 3 infanterie motorizată.

2) Constatările comisiei de recepție mai sînt expuse în următoarele anexe la prezentul proces verbal:

-Lista-anexă nr.1: Din documentația scrisă și desenată, care trebuia prezentată, au lipsit sau sînt incomplete;

-Lista-anexă nr. 2: Lucrări neexecutate;

-Lista-anexă nr.3: Lucrările, la executarea cărora nu s-au respectat prevederile proiectului.

3) Obiecțiile și neconformitățile Beneficiarului, au fost remediate în timpul executării lucrărilor de către Antreprenor.

Totodată, în cazul în care o anumită lucrare neesențială care necesită remedieri sau corectări nu este inclusă în prezentul proces verbal, Antreprenorul nu

INVESTITOR

Golden West Humanitarian Foundation

GESTIONAR

Brigada 3 infanterie motorizată

ANTREPRENOR

SRL „Prestigiu-Az”

**PROCES-VERBAL
DE RECEPȚIE FINALĂ**

Nr. 138 / din „02” „09” 2022

**Lucrări de construcție și reparație
la depozitele de muniții
din cadrul Brigăzii 3 infanterie motorizată**

Obiectul „**Lucrări de construcții și reparații la depozitele de muniții**” este executat în cadrul Brigăzii 3 infanterie motorizată conform contractului EUCOM/P010247335 din 15 octombrie 2021 încheiat între Golden West Humanitarian Foundation și SRL „Prestigiu-Az”.

1. Comisia de recepție finală și-a desfășurat activitatea în intervalul 09 2022, instituită prin ordinul Comandantului Brigăzii 3 infanterie motorizată nr. 24 din 03.08. 2022, fiind formată din:

Președintele comisiei:

locotenent-colonel Anatolie STRATU, locțiitor comandant de brigadă (șef S4 secție logistică) stat major.

Membrii comisiei:

maior Valeri DUȘA, șef serviciu cazare S4 secție logistică stat major;
căpitan Ilia GARABAJIU, șef serviciu armament și muniții S4 secție logistică stat major;
sergent clasa II Iurie CIOBANU, șef depozit (muniții) grupă depozite pluton asigurare companie logistică.

2. Au mai participat la recepție în calitate de invitați:

Reprezentantul J4 Direcție logistică, Marele Stat Major al Armatei Naționale

locotenent-colonel Alexandru ARION, ofițer principal secție armament și blindate.

Reprezentantul Agenției Asigurare Resurse și Administrare Patrimoniu a Ministerului Apărării

funcționar Victor MORGOCI, inspector superior secție infrastructură și supraveghere tehnică (de specialitate inginer construcții) Direcție administrare bunuri imobile.

Reprezentanții Antreprenorului:

Serghei CIOBANU, directorul SC „Prestigiu-Az” SRL;
Ion STRILETCHII, diriginte de șantier atestat.

3. Comisia de recepție finală, în urma examinării și analizei lucrărilor efectuate a constatat următoarele:

1) Lucrările pe specialități au fost executate și recepționate conform procesului verbal de recepție la terminarea lucrărilor nr. __ din „02” 09 2022;

2) Conform demersului SC „Prestigiu-Az” SRL nr. 18 din 26.07.2022 lucrările de construcții și reparații au fost terminate la data de „26” 07 2022;

3) Observații a comisiei de recepție finală: **fară obiecții**;

4) În baza datelor prezentate de către Antreprenor, **valoarea totală a obiectului (inclusiv utilajul)**, la data de „02” 09 2022 constituie **469 297,39 USD**, echivalentul **8 536 170,97 lei/MD**, care vor fi repartizate și luate la evidență contabilă, de către reprezentanții secției financiare a Brigăzii 3 infanterie motorizată, după cum urmează:

- **valoarea lucrărilor de construcție**, conform bilanțului de transmitere la data de „02” 09 2022 constituie **7 990 624,21 lei/MD**, care vor fi luate la evidență contabilă, conform anexei nr.1.

- **valoarea utilajului tehnologic și a bunurilor materiale** montate la obiect, conform bilanțului de transmitere la data de „02” 09 2022 constituie **545 546,76 lei/MD**, care vor fi luate la evidență contabilă, conform anexei nr.2.

4. În baza constatărilor făcute, comisia de recepție finală propune:

- **spre recepție finală** a obiectivului „Lucrări de construcții și reparații la depozitele de muniții” din cadrul Brigăzii 3 infanterie motorizată.

5. Comisia de recepție finală motivează propunerea făcută prin constatarea la fața locului **a finalizării lucrărilor de construcții și reparații** la obiectivul nominalizat.

6. Comisia de recepție finală recomandă următoarele:

- **admiterea recepției finale** a obiectivului „Lucrări de construcții și reparații la depozitele de muniții” din cadrul Brigăzii 3 infanterie motorizată.

6'. Descrierea obiectului recomandat spre recepție:

a) Construcții:

- **Valuri de protecție**, cu volum de **60 000,00,0 m³**;

- **Copertină cu cadre din metal** (25,80x16,85m), suprafața la sol **434.73 m²**, nr. etaje -, conform rezultatelor inspectării bunului imobil;

b) Obiective de infrastructură tehnico-edilitară:

- **Sistem de iluminare exterior (perimetral)**, cu lungimea **1500,0 m/l** conform rezultatelor inspectării bunului imobil;

- **Sistem de electricitate exterior subteran** cu lungimea **1500,0 m/l**, conform rezultatelor inspectării bunului imobil.

- **Sistem de supraveghere video**, conform rezultatelor inspectării bunului imobil.

7. Prezentul proces-verbal, conținând **4** (patru) file și **2** (două) anexe, cu un total de **6** (șase) file, a fost încheiat astăzi „02” 09 2022 în 4 exemplare.

Comisia de recepție finală:

Președintele comisiei:

locotenent-colonel Anatolie STRATU

Membrii comisiei:

maior Valeri DUȘA

căpitan Ilia GĂRABAJIU

sergent clasa II Iurie CIOBANU

Au mai participat la recepție:


Reprezentantului J4 Direcție logistică, Marele Stat Major al Armatei Naționale

locotenent-colonel Alexandru ARION

**Reprezentantul Agenției Asigurare Resurse și Administrare Patrimoniu
a Ministerului Apărării**
funcționarul Victor MORGOCI

Reprezentanții Antreprenorului:
Serghei CIOBANU
Ion STRILETCHII






8. Lucrarea „Construcția și reparația la depozitul de muniții”, din cadrul
Brigăzii 3 infanterie motorizată este:

TRANSMISĂ:
ANTREPRENORUL:


(semnătura)



**PROCES-VERBAL
DE RECEPȚIE LA TERMINAREA LUCRĂRILOR**

nr. 1 din "20" decembrie 2022

privind: "Reparația capitală și replanificarea saloanelor etajul II al blocului curativ cu V nivele al IMSP Spitalul raional Ștefan Vodă" conform contractului nr. 3319121C0006 din 17 mai 2021 încheiat între IMSP Spitalul raional Ștefan Vodă și SRL „Prestigiu Az” pentru "Reparația capitală și replanificarea saloanelor etajul II al blocului curativ cu V nivele al IMSP Spitalul raional Ștefan Vodă"

1. Comisia de recepție și-a desfășurat activitatea în intervalul de **o zi**, fiind formată din:

Președintele comisiei:

Anatolie Balanețchi

Director IMSP SR Ștefan -Vodă

Secretar al comisiei :

Svetlana Filimonov

Jurist IMSP SR Ștefan -Vodă

Membrii comisiei:

Anatolie Gurilă

Vicedirector medical IMSP SR Ștefan - Vodă

Vladimir Baligari

Vicepreședintele raionului Ștefan -Voda

Iurie Afanasiev

Șef Direcție construcții,gospodărie și drumuri a
Consiliului raional Ștefan – Vodă

Ecaterina Ciuico

Contabil -șef IMSP SR Ștefan -Vodă

Artimon Zubco

Șef serviciu tehnic și gospodăresc IMSP SR Ștefan- Vodă

Valeriu Beril

Responsabil tehnic

Alexandru Platon

Specialist atestat în construcții

Vasilii Bircă

Specialist atestat în construcții

Mihai Cacean

Șef secție obstetrico- ginecologie

Valentin Gurila

Medic -oncolog

2. Au mai participat la recepție:

Sergiu Ciobanu – Director SC "Prestigiu Az" SRL,

Ion Beșelea – diriginte de șantier.

3. Constatările comisiei de recepție:

1) din documentația scrisă și desenată, care trebuia prezentată, au lipsit sau sunt incomplete piesele cuprinse în lista-anexă nr. 1;

2) lucrările cuprinse în lista-anexă nr. 2 nu au fost executate;

3) în lucrările, cuprinse în lista-anexă nr. 3, nu s-au respectat prevederile proiectului.

4. Comisia de recepție, în urma constatărilor făcute, propune:

Se acceptă recepția la terminarea lucrărilor

5. Comisia de recepție motivează propunerea făcută prin:

Examinarea lucrarilor de către comisie.

7. Comisia de recepție recomandă următoarele:

Se recomandă recepția la terminarea lucrărilor cu înlăturarea neconformităților reflectate în anexele nr. 1, 2, 3 în termen de 30 zile.

7¹. Descrierea obiectului recomandat spre recepție:

"Reparația capitală și replanificarea saloanelor etajul II al blocului curativ cu V nivel al IMSP Spitalul raional Ștefan Vodă"

8. Prezentul proces-verbal, conținând 2 file și 3 anexe numerotate, cu un total de 5 file, a fost încheiat astăzi " " decembrie 2022 în 5 exemplare.

Președintele comisiei:

Anatolie Balanețchi

Secretar al comisiei :

Svetlana Filimonov

Membrii comisiei:

Anatolie Gurilă

Vladimir Baligari

Iurie Afanasiev

Ecaterina Ciunico

Artimon Zubco

Valeriu Beril

Alexandru Platon

Vasilii Bircă

Mihai Cacean

Valentin Gurila

10. Lucrarea " "Reparația capitală și replanificarea saloanelor etajul II al blocului curativ cu V nivel al IMSP Spitalul raional Ștefan Vodă" este recepționată.

TRANSMISĂ:

EXECUTANTUL:

SRL „Prestigiu Az”

Sergiu Ciobanu

"20" decembrie 2022

PRIMITĂ:

BENEFICIAR:

director IMSP SR Ștefan - Vodă

Anatolie Balanețchi

"20" decembrie 2022

L.Ș.

L.Ș.

Anexa nr. 1
la Procesul verbal de recepție la terminarea lucrărilor
nr. din „___” decembrie 2022

LISTA

lista documentației scrise și desenate care lipsește

Ciobanu Sergiu

Director SRL „Prestigiu Az”

Anatolie Balaneţchi

Preşedinte al comisi



La Procesul verbal de receptivitate la terminarea lucrarilor

Nr. _____ din _____ 2022

LISTA

lucrarilor care nu au fost executate

1. De instalat 2 chiuvete in sectia fizioterapie si anume: salon masaj si salon parafina.
2. De instalat priza dubla in salonul parafina.
3. De instalat tampoane (stopuri) la pragurile usilor din PVC in grupurile sanitare si bai.
4. De camuflat si izolat pe faianta la iesiri – intrari tevi canalizare si apa.
5. Instalare in sala de gimnastica a peretelui suiedez si sistem dublu de bara la oglinzi.
6. Instalarea unei masini de uscat rufe in salonul sora gospodina din sectia fizioterapie.
7. Instalare putere de urgenta (UPS- grad medical 5kva, pentru camerele 17,18,19,20,21,22 cu sustinere a sarcinii pentru 12 ore

Ciobanu Sergiu

Anatolie Balanetchi

Director SRL "Prestigiu AZ"

Presedinte al comisiei



LISTA
lista observațiilor comisiei de recepție și a lucrărilor care nu
au respectat prevederile proiectului

Ciobanu Sergiu

Anatolie Balanetchi

Balanetchi

Director SRL „Prestigiu Az”

Președinte al comisiei



SOLICITATION, OFFER, AND AWARD <i>(Construction, Alteration, or Repair)</i>	1. SOLICITATION NO.	2. TYPE OF SOLICITATION	3. DATE ISSUED	PAGE OF PAGES
	N3319121R4008	☐ SEALED BID (IFB) ☒ NEGOTIATED (RFP)	17-May-2021	1 OF 28

IMPORTANT - The "offer" section on the reverse must be fully completed by offeror.

4. CONTRACT NO. N3319121C0006	5. REQUISITION/PURCHASE REQUEST NO. ACQR5794155	6. PROJECT NO.
7. ISSUED BY CODE N33191	8. ADDRESS OFFER TO (If Other Than Item 7) CODE	
TEL:	See Item 7	
FAX: 39 081 568 7750	TEL:	FAX:
9. FOR INFORMATION CALL:	A. NAME	B. TELEPHONE NO. (Include area code) (NO COLLECT CALLS)

SOLICITATION

NOTE: In sealed bid solicitations "offer" and "offeror" mean "bid" and "bidder".

10. THE GOVERNMENT REQUIRES PERFORMANCE OF THE WORK DESCRIBED IN THESE DOCUMENTS (Title, identifying no., date):

N3319121R4008 D-B Renovate Hospital, Stefan Voda, Moldova

Proposals shall be submitted electronically per the instruction in Block 13 and Section 00100.

Please note: The deadline to submit proposals is in Central European Time (CET).

In accordance with FAR 36.204, the magnitude of this project is estimated to be between \$250,000 and \$500,000.

11. The Contractor shall begin performance within <u>10</u> calendar days and complete it within <u>700</u> calendar days after receiving ☒ award, ☐ notice to proceed. This performance period is ☒ mandatory, ☐ negotiable. (See _____.)	
12 A. THE CONTRACTOR MUST FURNISH ANY REQUIRED PERFORMANCE AND PAYMENT BONDS? (If "YES," indicate within how many calendar days after award in Item 12B.) ☐ YES ☒ NO	12B. CALENDAR DAYS

13. ADDITIONAL SOLICITATION REQUIREMENTS:

- A. Sealed offers in original and 1 copies to perform the work required are due at the place specified in Item 8 by 02:00 PM (hour) local time 24 Mar 2021 (date). If this is a sealed bid solicitation, offers must be publicly opened at that time. Sealed envelopes containing offers shall be marked to show the offeror's name and address, the solicitation number, and the date and time offers are due.
- B. An offer guarantee ☐ is, ☒ is not required.
- C. All offers are subject to the (1) work requirements, and (2) other provisions and clauses incorporated in the solicitation in full text or by reference.
- D. Offers providing less than 180 calendar days for Government acceptance after the date offers are due will not be considered and will be rejected.

SOLICITATION, OFFER, AND AWARD (Continued)*(Construction, Alteration, or Repair)***OFFER (Must be fully completed by offeror)**14. NAME AND ADDRESS OF OFFEROR *(Include ZIP Code)*PRESTIGIU-AZ SRL
SERGIU CIOBANU
PADURILOR
CHISINAU MD 209215. TELEPHONE NO. *(Include area code)*

373 022 00 95 00

16. REMITTANCE ADDRESS *(Include only if different than Item 14)*

See Item 14

CODE
STE93

FACILITY CODE

17. The offeror agrees to perform the work required at the prices specified below in strict accordance with the terms of this solicitation, if this offer is accepted by the Government in writing within _____ calendar days after the date offers are due. *(Insert any number equal to or greater than the minimum requirements stated in Item 13D. Failure to insert any number means the offeror accepts the minimum in Item 13D.)*

AMOUNTS

SEE SCHEDULE OF PRICES

18. The offeror agrees to furnish any required performance and payment bonds.

19. ACKNOWLEDGMENT OF AMENDMENTS*(The offeror acknowledges receipt of amendments to the solicitation -- give number and date of each)*

AMENDMENT NO.

DATE

20A. NAME AND TITLE OF PERSON AUTHORIZED TO SIGN
OFFER *(Type or print)*

20B. SIGNATURE

20C. OFFER DATE

AWARD (To be completed by Government)

21. ITEMS ACCEPTED:

SEE SCHEDULE22. AMOUNT
\$201,600.0023. ACCOUNTING AND APPROPRIATION DATA
See Schedule24. SUBMIT INVOICES TO ADDRESS SHOWN IN
(4 copies unless otherwise specified)

ITEM

25. OTHER THAN FULL AND OPEN COMPETITION PURSUANT TO

☐ 10 U.S.C. 2304(c)☐ 41 U.S.C. 253(c)

26. ADMINISTERED BY

CODE

See Item 7

27. PAYMENT WILL BE MADE
BY:

CODE

N61240

CONTRACTING OFFICER WILL COMPLETE ITEM 28 OR 29 AS APPLICABLE

☐ 28. NEGOTIATED AGREEMENT *(Contractor is required to sign this document and return _____ copies to issuing office.)* Contractor agrees to furnish and deliver all items or perform all work, requisitions identified on this form and any continuation sheets for the consideration stated in this contract. The rights and obligations of the parties to this contract shall be governed by (a) this contract award, (b) the solicitation, and (c) the clauses, representations, certifications, and specifications or incorporated by reference in or attached to this contract.

☒ 29. AWARD *(Contractor is not required to sign this document.)*

Your offer on this solicitation, is hereby accepted as to the items listed. This award consummates the contract, which consists of (a) the Government solicitation and your offer, and (b) this contract award. No further contractual document is necessary.

REF: Proposal dated 24 March 2021

30A. NAME AND TITLE OF CONTRACTOR OR PERSON AUTHORIZED
TO SIGN *(Type or print)*31A. NAME OF CONTRACTING OFFICER *(Type or print)*
Sabrina M Wenning / Contract Specialist

30B. SIGNATURE

30C. DATE

TEL: EMAIL

31B. UNITED STATES OF AMERICA

BY Sabrina M. Wenning

31C. AWARD DATE

17-May-2021

INVESTITOR Guvernul SUA, NAVFAC
BENEFICIAR IMSP Spitalul raional Cahul

Anexa nr. 1
la Regulamentul de recepție
a construcțiilor și instalațiilor
afereente

PROCES-VERBAL
DE RECEPȚIE LA TERMINAREA LUCRĂRILOR
Nr. _____ din 28, 09 2023

privind lucrarea de construcție executată la obiectivul: **"Renovarea interioară a etajului doi, blocul perinatal IMSP Spitalul raional Cahul"**.

în baza contractului de antrepriză nr.N3319121C0001 din 04.03.2021

încheiat între :

pe de o parte NAVFAC și Antreprenor SRL "Prestigiu-AZ",

pentru lucrările de construcție , : **"Renovarea interioară a etajului doi, blocul perinatal IMSP Spitalul raional Cahul"**.

1. Autorizație de construcție nr.044/2 eliberată de primăria mun. Cahul din 07.07.2021 cu valabilitate pînă la expirarea termenului legal.

2. Comisia de recepție la terminarea lucrărilor și-a desfășurat activitatea în intervalul **22-28 septembrie 2023**, fiind formată din:

presedintele comisiei

Vasile Rotaru – director IMSP Spitalul raional Cahul
Membrii comisiei

Lilea Postolachi	vicedirector IMSP Spitalul raional Cahul
Denis Saviuc	șef Departament logistic IMSP Spitalul raional Cahul
Ion Ostaș	șef interimar Centru perinatal de nivelul doi a IMSP Spitalul raional Cahul
Alexandru Nebunu	șef Secție gospodărie IMSP Spitalul raional Cahul
Crețu Dumitru	tehnician construtor IMSP Spitalul raional Cahul
Ion Ceban	responsabil tehnic

3. Au mai participat la recepție:

Ciobanu Sergiu -	administrator SRL "Prestigiu-AZ"
(numele, prenumele)	(calitatea)

4. Constatările comisiei de recepție:

- 1) din documentația scrisă și desenată, care trebuia prezentată, au lipsit sau sînt incomplete piesele cuprinse în lista-anexă nr. 1;
 - 2) lucrările cuprinse în lista-anexă nr. 2 nu au fost executate;
 - 3) în lucrările, cuprinse în lista-anexă nr. 3, nu s-au respectat prevederile proiectului.
- 5. Comisia de recepție, în urma constatărilor făcute, propune:**
Recepția la terminarea lucrărilor a obiectului sus nominalizat.
- 6. Comisia de recepție motivează propunerea făcută prin:**
Lucrările de construcție-montaj prevăzute în contract au fost finalizate

7. Comisia de recepție recomandă următoarele:

Se recomandă recepția la terminarea lucrărilor și exploatarea conform destinației.

8. Descrierea obiectului recomandat spre recepție:

Obiectul cu numărul cadastral 1701106070.03, adresa poștală str. Ștefan cel Mare 122 **mun. Cahul**, destinația **obiect social cu destinație servicii medicale** compus din următoarele construcții clădire edificiul _____, numărul de nivele 5, conform certificatului despre rezultatele inspectării bunului imobil _____ eliberat de _____, anexat la prezentul proces-verbal. Din cadrul proiectului:

"Renovarea interioară a etajului doi, blocul perinatal IMSP Spitalul raional Cahul".

9. Prezentul proces-verbal, conținând 2 file și 3 file anexe, cu un total de 5 file, a fost încheiat astăzi 28 septembrie 2023 în 6 exemplare. Anexe:

Proces-verbal de recepție a lucrărilor executate pe septembrie 2023. (total proces-verbal suma = 4 946 154,08 lei)

Comisia de recepție la terminarea lucrărilor :

Președinte: Vasile Rotaru

Membri

Lilea Postolachi

Denis Saviuc

Ion Ostaș

Alexandru Nebunu

Dumitru Crețu

Ion Ceban

(numele, prenumele)

(semnătura)

Concluzia Inspectoratului Național pentru Supraveghere Tehnică

9. Lucrarea : **"Renovarea interioară a etajului doi, blocul perinatal IMSP Spitalul raional Cahul".**
este finalizată și se admite spre recepție.

TRANSMISĂ:

EXECUTANTUL:

SRL "Prestigiu AZ"

"28" septembrie 2023

L.Ș. _____

(semnătura)

PRIMITĂ:

Beneficiar:

IMSP Spitalul raional Cahul

"28" septembrie 2023

L.Ș. _____

(semnătura)

ANEXĂ nr.1
La procesul-verbal de receptivitate la terminarea
Lucrarilor nr. Din 28.09.2023

Lista pieselor din documentația scrisă și desenată a obiectului
care sunt lipsă sau incomplete.

2



Lista lucrărilor cuprinse în Documentația Tehnică ce n-au fost executate.

3



ANEXĂ nr.3
La procesul-verbal de receptivitate la terminarea
Lucrarilor nr. Din 28.09.2023

Lista lucrărilor cuprinse în Documentația Tehnică la care nu s-a respectat prevederile proiectului.

2



SOLICITATION, OFFER, AND AWARD (Construction, Alteration, or Repair)	1. SOLICITATION NO. N3319121R4004	2. TYPE OF SOLICITATION ☐ SEALED BID (IFB) ☒ NEGOTIATED (RFP)	3. DATE ISSUED 04-Mar-2021	PAGE OF PAGES 1 OF 24

IMPORTANT - The "offer" section on the reverse must be fully completed by offeror.

4. CONTRACT NO. N3319121C0001	5. REQUISITION/PURCHASE REQUEST NO.	6. PROJECT NO.
7. ISSUED BY NAVFAC EUROPE AFRICA CENTRAL VIALE PORTO CAPODICHINO NAPOLI 80144	CODE N33191	8. ADDRESS OFFER TO (If Other Than Item 7) CODE See Item 7
TEL: 39 081 568 7750	FAX: 39 081 568 7750	TEL: FAX:
9. FOR INFORMATION CALL	A. NAME TERESA C. SMITH	B. TELEPHONE NO. (Include area code) (NO COLLECT CALLS) 39-081-568-7744.

SOLICITATION

NOTE: In sealed bid solicitations "offer" and "offeror" mean "bid" and "bidder".

10. THE GOVERNMENT REQUIRES PERFORMANCE OF THE WORK DESCRIBED IN THESE DOCUMENTS (Title, identifying no., date):

N3319121R4004 D-B Renovate Cahul Hospital, Cahul, Moldova

Proposals are to be submitted electronically per the instructions in Block 13 and Section 00100.

Please note: the deadline to submit proposals is in Central European Time (CET).

In accordance with FAR 36.204, the magnitude of this project is estimated to be between \$250,000 and \$500,000.

11. The Contractor shall begin performance within 10 calendar days and complete it within 700 calendar days after receiving ☒ award, ☐ notice to proceed. This performance period is ☒ mandatory, ☐ negotiable. (See _____.)

12 A. THE CONTRACTOR MUST FURNISH ANY REQUIRED PERFORMANCE AND PAYMENT BONDS?
(If "YES," indicate within how many calendar days after award in Item 12B.)

☐ YES ☒ NO

12B. CALENDAR DAYS

13. ADDITIONAL SOLICITATION REQUIREMENTS:

- A. Sealed offers in original and 1 copies to perform the work required are due at the place specified in Item 8 by 02:00 PM (hour) local time 16 Feb 2021 (date). If this is a sealed bid solicitation, offers must be publicly opened at that time. Sealed envelopes containing offers shall be marked to show the offeror's name and address, the solicitation number, and the date and time offers are due.
- B. An offer guarantee ☐ is, ☒ is not required.
- C. All offers are subject to the (1) work requirements, and (2) other provisions and clauses incorporated in the solicitation in full text or by reference.
- D. Offers providing less than 120 calendar days for Government acceptance after the date offers are due will not be considered and will be rejected.

SOLICITATION, OFFER, AND AWARD (Continued)

(Construction, Alteration, or Repair)

OFFER (Must be fully completed by offeror)

14. NAME AND ADDRESS OF OFFEROR (Include ZIP Code)

PRESTIGIU-AZ SRL
SERGIU CIOBANU
PADURILOR
CHISINAU MD 2092

15. TELEPHONE NO. (Include area code)

373 022 00 95 00

16. REMITTANCE ADDRESS (Include only if different than Item 14)

See Item 14

CODE
STE93

FACILITY CODE

17. The offeror agrees to perform the work required at the prices specified below in strict accordance with the terms of this solicitation, if this offer is accepted by the Government in writing within _____ calendar days after the date offers are due. (Insert any number equal to or greater than the minimum requirements stated in Item 13D. Failure to insert any number means the offeror accepts the minimum in Item 13D.)

AMOUNTS

SEE SCHEDULE OF PRICES

18. The offeror agrees to furnish any required performance and payment bonds.

19. ACKNOWLEDGMENT OF AMENDMENTS

(The offeror acknowledges receipt of amendments to the solicitation -- give number and date of each)

AMENDMENT NO.

DATE

20A. NAME AND TITLE OF PERSON AUTHORIZED TO SIGN
OFFER (Type or print)

20B. SIGNATURE

20C. OFFER DATE

AWARD (To be completed by Government)

21. ITEMS ACCEPTED

SEE SCHEDULE

22. AMOUNT

\$265,000.00

23. ACCOUNTING AND APPROPRIATION DATA

See Schedule

24. SUBMIT INVOICES TO ADDRESS SHOWN IN

(4 copies unless otherwise specified)

ITEM

25. OTHER THAN FULL AND OPEN COMPETITION PURSUANT TO

☐ 10 U.S.C. 2304(c)☐ 41 U.S.C. 253(c)

26. ADMINISTERED BY

CODE

27. PAYMENT WILL BE MADE BY:

CODE

N61240

CBPO EURAFSWA IRAPT
PSC 817 BOX 58
FPO AE 09622

See Item 7

CONTRACTING OFFICER WILL COMPLETE ITEM 28 OR 29 AS APPLICABLE

☐ 28. NEGOTIATED AGREEMENT

(Contractor is required to sign this

document and return _____ copies to issuing office.) Contractor agrees to furnish and deliver all items or perform all work, requisitions identified on this form and any continuation sheets for the consideration stated in this contract. The rights and obligations of the parties to this contract shall be governed by (a) this contract award, (b) the solicitation, and (c) the clauses, representations, certifications, and specifications or incorporated by reference in or attached to this contract.

☒

29. AWARD (Contractor is not required to sign this document.)

Your offer on this solicitation, is hereby accepted as to the items listed. This award commutes the contract, which consists of (a) the Government solicitation and your offer, and (b) this contract award. No further contractual document is necessary.

REF: Proposal February 16, 2021

30A. NAME AND TITLE OF CONTRACTOR OR PERSON AUTHORIZED TO SIGN (Type or print) Sergiu Ciobanu, Director

31A. NAME OF CONTRACTING OFFICER

(Type or print)

Teresa C. Smith / Contract Specialist

30B. SIGNATURE

30C. DATE

04-Mar-2021

TEL: 39-081-568-7744.

EMAIL: teresa.smith@eu.navy.mil

31B. UNITED STATES OF AMERICA

BY

Teresa C Smith

31C. AWARD DATE

04-Mar-2021

SOLICITATION, OFFER, AND AWARD <i>(Construction, Alteration, or Repair)</i>		1. SOLICITATION NO. N3319120R40220001	2. TYPE OF SOLICITATION ☐ SEALED BID (IFB) ☒ NEGOTIATED (RFP)	3. DATE ISSUED 21-Jul-2020	PAGE OF PAGES 1 OF 24
IMPORTANT - The "offer" section on the reverse must be fully completed by offeror.					
4. CONTRACT NO. N3319120C0006		5. REQUISITION/PURCHASE REQUEST NO. ACQR5780886		6. PROJECT NO.	
7. ISSUED BY NAVFAC EUROPE AFRICA CENTRAL VIALE PORTO CAPODICHINO NAPOLI 80144 TEL: 39 081 568 7750 FAX: 39 081 568 7750		8. ADDRESS OFFER TO <i>(If Other Than Item 7)</i> CODE See Item 7			
9. FOR INFORMATION CALL:	A. NAME SABRINA M WENNING		B. TELEPHONE NO. <i>(Include area code) (NO COLLECT CALLS)</i>		
SOLICITATION					
NOTE: In sealed bid solicitations "offer" and "offeror" mean "bid" and "bidder".					
10. THE GOVERNMENT REQUIRES PERFORMANCE OF THE WORK DESCRIBED IN THESE DOCUMENTS <i>(Title, identifying no., date):</i> N3319120R4022 D-B Renovate Falesti Kindergarten, Falesti, Moldova Proposals are to be submitted electronically per the instructions in Block 13 and Section 00100. Please note: the deadline to submit proposals is in Central European Time (CET). In accordance with FAR 36.204, the magnitude of this project is estimated to be between \$250,000 and \$500,000.					
11. The Contractor shall begin performance within <u>10</u> calendar days and complete it within <u>700</u> calendar days after receiving ☒ award, ☐ notice to proceed. This performance period is ☒ mandatory, ☐ negotiable. <i>(See _____.)</i>					
12 A. THE CONTRACTOR MUST FURNISH ANY REQUIRED PERFORMANCE AND PAYMENT BONDS? <i>(If "YES," indicate within how many calendar days after award in Item 12B.)</i> ☒ YES ☐ NO				12B. CALENDAR DAYS	
13. ADDITIONAL SOLICITATION REQUIREMENTS: A. Sealed offers in original and <u>1</u> copies to perform the work required are due at the place specified in Item 8 by <u>02:00 PM</u> <i>(hour)</i> local time <u>30 Mar 2020</u> <i>(date)</i> . If this is a sealed bid solicitation, offers must be publicly opened at that time. Sealed envelopes containing offers shall be marked to show the offeror's name and address, the solicitation number, and the date and time offers are due. B. An offer guarantee ☐ is, ☒ is not required. C. All offers are subject to the (1) work requirements, and (2) other provisions and clauses incorporated in the solicitation in full text or by reference. D. Offers providing less than <u>120</u> calendar days for Government acceptance after the date offers are due will not be considered and will be rejected.					

(Construction, Alteration, or Repair)

14. NAME AND ADDRESS OF OFFEROR	(Include ZIP Code)
PRESTIGIU-AZ SRL	
SERGIU CIOBANU	
PADURILOR	
CHISINAU MD 2092	

16. REMITTANCE ADDRESS (Include only if different than Item 14)

FACILITY CODE

SEE SCHEDULE OF PRICES

(The offeror acknowledges receipt of amendments to the solicitation -- give number and date of each)

20C. OFFER DATE


STANDARD FORM 1442 BACK (REV. 4-85)

3.3. Pictures to Describe the Exterior Works of Base-Bid

The following pictures do not include or describe all requirements of the contract, but all requirements described in the pictures are part of the contract



In red: north-east block to be demolished. Rest of building to remain.

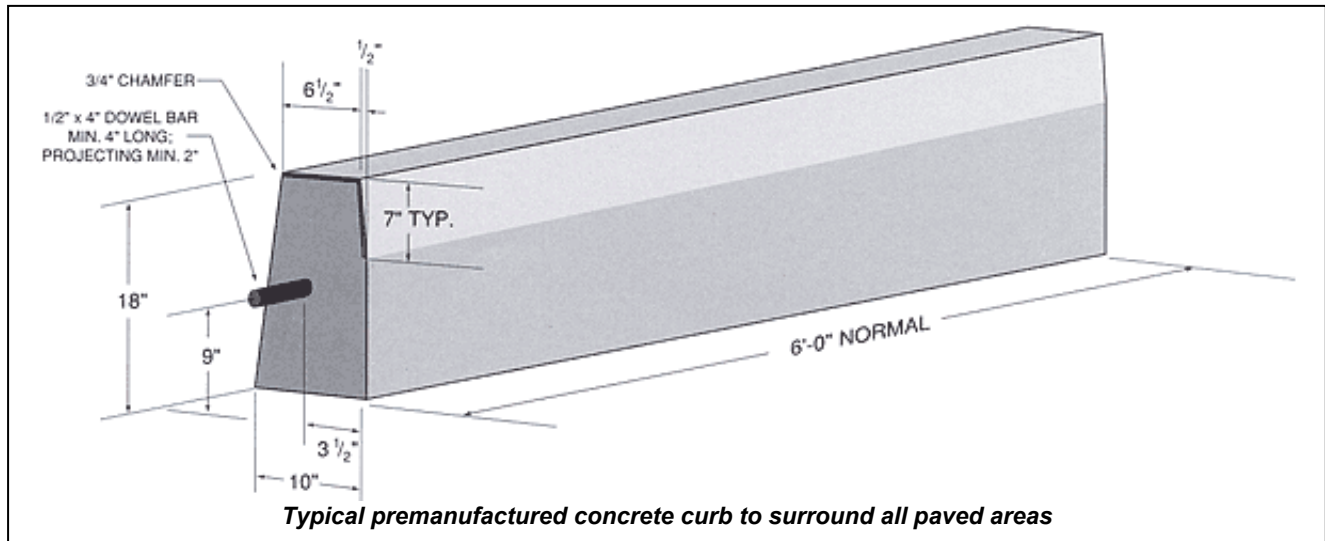

Picture from recently completed kindergarten renovation project in Moldova (Drochia). Typical pavement required around the new building for minimum of 1,000 m² including all CLIN's. Note also acceptable façade finishes and commemorative plaque.

PROCES-VERBAL DE RECEPȚIE LA TERMINAREA LUCRĂRILOR

nr. 01 din "18" ianuarie 2023

privind: "Anexa la blocul central a construcției de cultura și agrement IET nr.10 din or. Fălești" conform contractului nr. N3319120C0006 din 21.07.2020 încheiat între Primăria orașului Fălești și SRL „Prestigiu Az” pentru "Anexa la blocul central a construcției de cultura și agrement IET nr.10 din or. Fălești"

1. Comisia de recepție și-a desfășurat activitatea în intervalul de **o zi**, fiind formată din:

Președintele comisiei:

Alexandru Severin

Primar al orașului Fălești

Membrii comisiei:

Russu Evghenia

Contabil- sef, primăria or. Fălești

Anatolie Antonciuc

Viceprimar al orașului Fălești

Aliona Stavciuc

Director IET nr. 10

Ion Ciobanu

Responsabil tehnic

Vasile Puu

Responsabil tehnic

Ion Leahu

Responsabil tehnic

Ivan Negura

Specialist principal

Boris Dedov

Consilier, consiliul local Fălești

2. Au mai participat la recepție:

Sergiu Ciobanu – Director SC "Prestigiu Az" SRL,
Ion Beșelea – diriginte de șantier,
Ciobanu ION – responsabil tehnic

3. Constatările comisiei de recepție:

1) din documentația scrisă și desenată, care trebuia prezentată, au lipsit sau sunt incomplete piesele cuprinse în lista-anexă nr. 1;

2) lucrările cuprinse în lista-anexă nr. 2 nu au fost executate;

3) în lucrările, cuprinse în lista-anexă nr. 3, nu s-au respectat prevederile proiectului.

4. Comisia de recepție, în urma constatărilor făcute, propune:

Se acceptă recepția la terminarea lucrărilor

5. Comisia de recepție motivează propunerea făcută prin:

Examinarea lucrărilor de către comisie.

7. Comisia de recepție recomandă următoarele:
Se recomandă recepția la terminarea lucrărilor cu înlăturarea neconformităților reflectate în anexele nr. 1, 2, 3 în termen de 30 zile.

7¹. Descrierea obiectului recomandat spre recepție:
"Anexa la blocul central a construcției de cultura și agrement IET nr.10 din or. Fălești"

8. Prezentul proces-verbal, conținând 2 file și 3 anexe numerotate, cu un total de 5 file, a fost încheiat astăzi " " ianuarie 2023 în 5 exemplare.

Președintele comisiei:

Alexandru Severin

Membrii comisiei:

Russu Evghenia

Anatolie Antonciuc

Aliona Stavciuc

Ion Ciobanu

Vasile Puiu

Ion Leahu

Ivan Negura

Boris Dedov

Beșelea Ion

Ciobanu Ion



10. Lucrarea "Anexa la blocul central a construcției de cultura și agrement IET nr.10 din or. Fălești" este recepționată.

TRANSMISĂ:

EXECUTANTUL:

SRL „Prestigiu Az”

Sergiu Ciobanu

" 18 " ianuarie 2023

L.Ș.



PRIMITĂ:

BENEFICIAR:

Primar al orașului Fălești

Alexandru Severin

" 18 " ianuarie 2023

L.Ș.



Anexa nr. 1
la Procesul verbal de recepție la terminarea lucrărilor
nr. din „___” ianuarie 2023

LISTA
lista documentației scrise și desenate care lipsește

Ciobanu Sergiu



Director SRL „Prestigiu Az”

Alexandru Severin



Președinte al comisiei

Anexa nr. 2
la Procesul verbal de recepție la terminarea lucrărilor
nr. din „____” ianuarie 2023

LISTA
lista lucrărilor care nu au fost executate

Ciobanu Sergiu

Director SRL „Prestigiu Az”

Alexandru Severin

Președinte al comisiei



LISTA
lista observațiilor comisiei de recepție și a lucrărilor care nu
au respectat prevederile proiectului

Ciobanu Sergiu

Alexandru Severin



Director SRL „Prestigiu Az”

Președinte al comisiei

SOLICITATION, OFFER, AND AWARD (Construction, Alteration, or Repair)		1. SOLICITATION NO. N3319120R40170001	2. TYPE OF SOLICITATION ☐ SEALED BID (IFB) ☒ NEGOTIATED (RFP)	3. DATE ISSUED 05-Aug-2020	PAGE OF PAGES 1 OF 23
IMPORTANT - The "offer" section on the reverse must be fully completed by offeror.					
4. CONTRACT NO. N3319120C0009		5. REQUISITION/PURCHASE REQUEST NO. ACQR5779430		6. PROJECT NO.	
7. ISSUED BY NAVFAC EUROPE AFRICA CENTRAL VIALE PORTO CAPODICHINO NAPOLI 80144 TEL: 39 081 568 7750 FAX: 39 081 568 7750		CODE N33191	8. ADDRESS OFFER TO (If Other Than Item 7) CODE See Item 7 TEL: FAX:		
9. FOR INFORMATION CALL:	A. NAME SABRINA M WENNING		B. TELEPHONE NO. (Include area code) (NO COLLECT CALLS) 00 39 081 568 6211		
SOLICITATION					
NOTE: In sealed bid solicitations "offer" and "offeror" mean "bid" and "bidder".					
10. THE GOVERNMENT REQUIRES PERFORMANCE OF THE WORK DESCRIBED IN THESE DOCUMENTS (Title, identifying no., date): N3319120R4017 D-B RENOVATE TARACLIA HOSPITAL, TARACLIA, MOLDOVA Please note: the deadline to submit proposals is in Central European Time (CET). In accordance with FAR 36.204, the magnitude of this project is estimated to be between \$250,000 and \$500,000.					
11. The Contractor shall begin performance within <u>10</u> calendar days and complete it within <u>700</u> calendar days after receiving ☒ award, ☐ notice to proceed. This performance period is ☒ mandatory, ☐ negotiable. (See _____.)					
12 A. THE CONTRACTOR MUST FURNISH ANY REQUIRED PERFORMANCE AND PAYMENT BONDS? (If "YES," indicate within how many calendar days after award in Item 12B.) ☐ YES ☒ NO					12B. CALENDAR DAYS
13. ADDITIONAL SOLICITATION REQUIREMENTS: A. Sealed offers in original and <u>1</u> copies to perform the work required are due at the place specified in Item 8 by <u>02:00 PM</u> (hour) local time <u>30 Mar 2020</u> (date). If this is a sealed bid solicitation, offers must be publicly opened at that time. Sealed envelopes containing offers shall be marked to show the offeror's name and address, the solicitation number, and the date and time offers are due. B. An offer guarantee ☐ is, ☒ is not required. C. All offers are subject to the (1) work requirements, and (2) other provisions and clauses incorporated in the solicitation in full text or by reference. D. Offers providing less than <u>120</u> calendar days for Government acceptance after the date offers are due will not be considered and will be rejected.					

SOLICITATION, OFFER, AND AWARD (Continued)

(Construction, Alteration, or Repair)

OFFER (Must be fully completed by offeror)

14. NAME AND ADDRESS OF OFFEROR (Include ZIP Code)

PRESTIGIU-AZ SRL
SERGIU CIOBANU
PADURILOR
CHISINAU MD 2092

15. TELEPHONE NO. (Include area code)

373 022 00 95 00

16. REMITTANCE ADDRESS (Include only if different than Item 14)

See Item 14

CODE
STE93

FACILITY CODE

17. The offeror agrees to perform the work required at the prices specified below in strict accordance with the terms of this solicitation, if this offer is accepted by the Government in writing within _____ calendar days after the date offers are due. (Insert any number equal to or greater than the minimum requirements stated in Item 13D. Failure to insert any number means the offeror accepts the minimum in Item 13D.)

AMOUNTS

SEE SCHEDULE OF PRICES

18. The offeror agrees to furnish any required performance and payment bonds.

19. ACKNOWLEDGMENT OF AMENDMENTS

(The offeror acknowledges receipt of amendments to the solicitation - give number and date of each)

AMENDMENT NO.

DATE

20A. NAME AND TITLE OF PERSON AUTHORIZED TO SIGN
OFFER (Type or print)

20B. SIGNATURE

20C. OFFER DATE

AWARD (To be completed by Government)

21. ITEMS ACCEPTED:

SEE SCHEDULE22. AMOUNT
\$280,000.0023. ACCOUNTING AND APPROPRIATION DATA
See Schedule24. SUBMIT INVOICES TO ADDRESS SHOWN IN
(4 copies unless otherwise specified)

ITEM

25. OTHER THAN FULL AND OPEN COMPETITION PURSUANT TO

☐ 10 U.S.C. 2304(c)☐ 41 U.S.C. 253(c)

26. ADMINISTERED BY

CODE

See Item 7

27. PAYMENT WILL BE MADE BY:
COMMERCIAL BILL PAYING OFFICE - NAPLES
NSA, COMPTROLLER DEPT.
ADMIN III
VIALE FULCO RUFFO DI CALABRIA
NAPOLI 80144

CODE

N62588

CONTRACTING OFFICER WILL COMPLETE ITEM 28 OR 29 AS APPLICABLE

☐ 28. NEGOTIATED AGREEMENT (Contractor is required to sign this document and return _____ copies to issuing office.) Contractor agrees to furnish and deliver all items or perform all work, requisitions identified on this form and any continuation sheets for the consideration stated in this contract. The rights and obligations of the parties to this contract shall be governed by (a) this contract award, (b) the solicitation, and (c) the clauses, representations, certifications, and specifications or incorporated by reference in or attached to this contract.

☒ 29. AWARD (Contractor is not required to sign this document.)

Your offer on this solicitation, is hereby accepted as to the items listed. This award commutes the contract, which consists of (a) the Government solicitation and your offer, and (b) this contract award. No further contractual document is necessary.

REF: Proposal dated May 4, 2020

30A. NAME AND TITLE OF CONTRACTOR OR PERSON AUTHORIZED TO SIGN (Type or print)
Sergiu Ciobanu, Director31A. NAME OF CONTRACTING OFFICER (Type or print)
Cynthia Mafara / Contract Specialist

TEL: 081 568 7745

EMAIL: cynthia.mafara@eu.navy.mil

30B. SIGNATURE

30C. DATE

05-Aug-2020

31B. UNITED STATES OF AMERICA

BY *Cynthia C. Mafara*

31C. AWARD DATE

05-Aug-2020

PROCES – VERBAL № 1
DE RECEPȚIE LA TERMINAREA LUCRĂRILOR
din 28 decembrie 2023 a.

privind lucrarea: „Renovarea interioaraa aripii de sud și de est a etajului III, IMSP Spitalul raional Taraclia” executată la obiectivul din ул. В. Чебанова г. Тараклия în cadrul contractului: nr. 3319120C0009 din 05.08.2023 încheiat între S.C.“Prestigiu-AZ” SRL și NAVFAC EUCOM Humanitarian Assistance Program pentru lucrările de капитальный ремонт 3-го этажа основного корпуса РБ Тараклия

1. Lucrările au fost executate în baza în baza autorizației de construcție nr.01din 22.06.2021
2. Comisia de recepție și-a desfășurat activitatea 28/12/2023 a.

Presedintele comisiei:

Ковач Артур - директор ПМСУ РБ Тараклия, председатель комиссии

Membrii comisiei de recepție:

Дериволкова Валентина - представитель отдела строительства района Тараклия

Пасларь Мария - главный бухгалтер ПМСУ РБ Тараклия

Бешеля Ион - руководитель стройки

Чебан Ион – технадзор объекта

Топал Вячеслав - технадзор

3. Au mai participat

Сергей Чобану - Директор S.C.“Prestigiu-AZ” SRL.

4. Constatările comisiei de recepție:

- 1) din documentația scrisă și destinată, care trebuia prezentată, au lipsit sau sunt incomplete piesele cuprinse în lista anexă nr.1.
- 2) lucrările cuprinse în lista anexată nr.2 nu au fost executate.
- 3) în lucrările, cuprinse în lista – anexă nr.3, nu s-au respectat prevederile proiectului.

5. Comisia de recepție, în urma constatărilor făcute, propune – **Recepția la terminarea lucrărilor.**

6. Comisia de recepție motivează propunerea făcută prin: **Terminarea integrală a volumelor de lucrări prevăzute în documentația de proiect si schimbarile coordonate.**

7.Comisia de recepție recomandă următoarele: **Admiterea recepției la terminarea lucrărilor cu observatii care sunt indicate in anexa nr.3.**

7¹. Descrierea obiectului recomandat spre recepție: Obiectul cu numărul cadastral__ **087012080355.01** __, adresa poștală **RM, r-n Taraclia, or. Taraclia, str. V. Cioban 1** destinația_ **Оказание медицинских услуг** compus din următoarele compartimente:

suprafața la sol 1289 m², numărul de etaje 6, conform certificatului despre rezultatele
inspectării bunului imobil, anexat la prezentul proces-verbal.

8. Prezentul proces-verbal, conținând 2 file și 3 anexe numerotate, cu un total de 5
file, a fost încheiat astăzi 28/12/2023 a. în 5 exemplare.

Presedintele comisiei:

Ковач Артур _____

Membrii comisiei de recepție:

Дериволкова Валентина

Digitally signed by Derivoltova Valentina
Date: 2024.01.24 16:57:36 EET
Reason: MoldSign Signature
Location: Moldova



Пасларь Мария

Digitally signed by Paslari Maria
Date: 2024.01.25 13:05:30 EET
Reason: MoldSign Signature
Location: Moldova



Бешеля Ион

Digitally signed by Beșelea Ion
Date: 2024.01.24 15:45:03 EET
Reason: MoldSign Signature
Location: Moldova



Чебан Ион

Digitally signed by Ceban Ion
Date: 2024.01.24 14:42:34 EET
Reason: MoldSign Signature
Location: Moldova



Топал Вячеслав

Digitally signed by TOPAL VEACESLAV
Date: 2024.01.24 16:47:34 EET
Reason: MoldSign Signature
Location: Moldova



9. Lucrarea : «Renovarea interioara a aripii de sud și de est a etajului III, IMSP Spitalul
raional Taraclia» - este.

TRANSMISĂ:

EXECUTANTUL:

29.12.2023

Digitally signed by Ciobanu Sergiu
Date: 2024.01.24 16:12:18 EET
Reason: MoldSign Signature
Location: Moldova



(semnătura)

PRIMITĂ:

INVESTITORUL:

28.12.2023

Digitally signed by Govaci Artur
Date: 2024.01.25 12:58:54 EET
Reason: MoldSign Signature
Location: Moldova



(semnătura)

În cadrul proiectului: «Renovarea interioaraa aripiei de sud și de est a etajului III, IMSP Spitalul raional Taraclia»

Lucrări la care nu s-au respectat conform prevederilor proiectului

1. Отсутствуют исполнительные схемы установленного оборудования и аварийного освещения;

2. Не установлен пандус в душевой для пациентов с ограниченными возможностями;

3. Не укомплектован тех. паспорт сооружения отд. "В" (отсутствуют сертификаты соответствия на применённые материалы и тех. паспорта установленного оборудования, вкл. гарантийные талоны).

Președintele comisiei _____ Ковач А

Director S.C.“Prestigiu-AZ” SRL _____ Чобану С.

Responsabil tehnic _____ Чебан И.
